

AgriPartners Development Round Funding Package

Authoritative Master Edition — Version v1.0 R1

5 August 2026

Publication Status

Publication Ready — Remediation Verified

Development Budget: USD 40,000 — product development only

Target Outcome: Pilot Operations & Investor Evidence Beta Candidate

Boundary: Non-production; no Corporate Setup, Operational Readiness costs, Pilot Capital, live custody, payout or settlement.

Document Architecture

This Master Document contains Sections 1–21 in the approved order, followed by Appendices A–J. Sections 1, 3, 5 and 13 are newly reissued canonical texts. Sections 2, 4, 6–12 and 14–21 preserve the approved source texts without substantive change.

Table of Contents

- Section 1: Executive Summary
- Section 2: Why This Round Matters
- Section 3: Development Round Definition
- Section 4: Current Product Baseline
- Section 5: Development Objective
- Section 6: Beta Candidate
- Section 7: Development Scope
- Section 8: Development Work Packages
- Section 9: Deliverables
- Section 10: Development Budget
- Section 11: Use of Funds
- Section 12: Excluded Costs
- Section 13: Development Milestones
- Section 14: Verification and Reporting Evidence
- Section 15: Completion and Acceptance Criteria
- Section 16: Expected Outcomes
- Section 17: Dependencies and Assumptions
- Section 18: Risks and Controls
- Section 19: Relationship to Operational Readiness
- Section 20: Post Round Position
- Section 21: Funder Adaptation Framework
- Appendix A: Terminology Register
- Appendix B: Scope Work Package Crosswalk
- Appendix C: Deliverable Milestone Crosswalk
- Appendix D: Budget Control Schedule
- Appendix E: Evidence Register Template
- Appendix F: Risk and Dependency Register Template
- Appendix G: Acceptance Record Template

- Appendix H: Claims and Positioning Matrix
- Appendix I: Funder Adaptation Crosswalk
- Appendix J: Publication and Change Control Checklist

1. Executive Summary

AgriPartners

AgriPartners is an Alpha-stage platform designed to improve transparency, operational accountability, and Investor visibility throughout agricultural investment workflows. It provides structured digital workflows through which Investors can review Project information, operational participants can report progress and supporting evidence, and platform administrators can monitor Project activity, expenses, return records, and lifecycle events.

The current product is a working prototype designed to validate these workflows and demonstrate how Investor visibility and operational accountability can be improved. NEAR Protocol is currently used in a Testnet environment for wallet-linked workflows and technical experimentation. This Alpha implementation does not accept live investments and is not a production custody, payment, settlement, or investment system.

Current Product Baseline

AgriPartners Alpha v1.2 currently includes a public opportunity experience, Investor Portal, Farmer Portal, Admin Portal, Treasury Dashboard, Presentation Mode, wallet authentication, backend API, PostgreSQL database, and NEAR Testnet integration.

The verified technical baseline also includes the completed Stage 2 Financial Workflow Foundation and Stage 2 Project Expense Accounting Foundation.

These foundations provide structured workflow budgets, Project Expense records, immutable Expense lifecycle history, supporting-evidence foundations, and derived budget reservations. They also include concurrency-safe controls intended to prevent inconsistent reservations and overspending.

This baseline demonstrates that AgriPartners is beyond the idea stage and already has a functioning product and technical foundation. However, the Project Expense API and its dedicated authorization layer, complete Operator Expense Workspace, integrated evidence workflow, and Investor-facing Expense transparency required for the next product milestone have not yet been completed.

Development Round

AgriPartners is seeking **USD 40,000** to complete one defined product milestone:

Pilot Operations & Investor Evidence Beta Candidate

This Development Round represents the next measurable value milestone in the AgriPartners product roadmap.

The round exists to convert the current Alpha and its completed accounting foundations into a coherent, end-to-end, externally demonstrable Beta Candidate. Funding is restricted to product development and the associated quality, security, deployment, documentation, and delivery evidence required to complete and verify that milestone.

Corporate Setup, legal and accounting readiness, banking or payment infrastructure, construction, animals, agricultural operating expenses, and capital for physical Pilots are outside the scope of this Development Round.

Expected Result

After completion, AgriPartners will have a demonstrable Beta Candidate through which:

an authorized Operator can manage a controlled Project Expense workflow;

Project budgets, Expenses, lifecycle states, and supporting evidence can be recorded and reviewed;

Investors can access appropriately disclosed information about Project activity and use of funds;

operational history and reporting can be demonstrated through an end-to-end Project scenario;

completion can be supported by repository history, testing, security verification, deployment evidence, documentation, and a structured demonstration package.

The resulting Beta Candidate will provide demonstrable value for grant programmes, accelerator reviewers, Investors, and strategic partners through a consistent, verifiable, and reviewable operational workflow.

It will provide a stronger basis for grant reporting, accelerator review, Investor demonstrations, strategic-partner evaluation, and preparation for a controlled Feedlot Pilot.

Completion of the Development Round will not mean that AgriPartners is production-ready, regulated, audited, deployed on Mainnet, accepting live investments, operating a Feedlot, or generating verified investment returns. It will make the product ready to enter a separate Operational Readiness Review, where product, corporate, legal, financial, Operator, and funding readiness must be assessed before any real Pilot may begin.

Strategic Position

The Development Round is one component of the wider AgriPartners Funding Strategy v1. It finances the defined Beta Candidate product milestone only.

Corporate Setup, including establishment of AgriPartners OÜ and initial corporate readiness, is governed separately. The Feedlot and Hissar Pilots require separately controlled and fully funded Pilot Capital.

This separation ensures that development funding produces a measurable product result without being diluted by Corporate Setup costs or physical Pilot expenditure.

2. Why This Round Matters

The Development Round exists to convert AgriPartners' verified Alpha foundation into a coherent and demonstrable product milestone: the Pilot Operations & Investor Evidence Beta Candidate.

The current Alpha has already established that the core product concept can be implemented. However, the platform does not yet provide the complete operational, evidence, authorization, and investor-transparency experience required for a credible Beta demonstration. The proposed round addresses this specific maturity gap.

The purpose of the round is therefore not to finance exploratory product discovery or an untested concept. It is to complete a defined progression from an existing technical foundation to a measurable, reviewable, and externally demonstrable Beta Candidate whose completion can be assessed against documented evidence and acceptance criteria.

2.1 Why Now

AgriPartners has reached the point at which an additional funded development milestone can build directly on its verified product and engineering foundations.

The current Alpha has established the principal product roles, workflow concepts, reporting capabilities, demonstration environment, and underlying financial and project expense accounting structures. The next logical step is to connect these foundations through a complete user-visible operational experience.

The principal challenge is no longer to determine whether the core workflow can be represented technically. It is to convert the existing components into an integrated experience that can demonstrate how operational activity, project expenses, authorization controls, supporting evidence, and investor visibility function together.

The current Alpha remains insufficient for that purpose because several important product layers are not yet complete. In particular, the existing accounting foundation must be exposed through the planned Project Expense API and Authorization, connected to a functional Operator Workspace, integrated with evidence handling, and presented through clear investor-facing transparency and reporting.

There is no currently identified technical dependency that requires postponing this work. The required foundations are already present, while the remaining gap limits the platform's ability to demonstrate the complete operational workflow as a single reviewable product experience.

The Development Round is therefore timely because AgriPartners has completed enough foundational work to support a bounded Beta milestone but has not yet completed the user-visible and verifiable product layer required to demonstrate that milestone.

2.2 Why This Creates Value

The Development Round creates value by transforming separate technical capabilities into a coherent, end-to-end product experience.

At the Alpha stage, AgriPartners can demonstrate individual roles, workflows, financial-state foundations, reporting concepts, and Testnet capabilities. After the proposed round, the platform is expected to demonstrate how an operator records and manages project expenses, how authorization controls are applied, how supporting evidence is associated with operational activity, and how relevant information becomes visible to an investor.

This progression creates measurable value in five areas.

First, it increases product maturity. The platform advances from a working Alpha with completed foundations to a Beta Candidate with an integrated operational workflow.

Second, it improves demonstrability. Reviewers will be able to follow a consistent end-to-end scenario instead of assessing isolated features or relying primarily on architectural descriptions.

Third, it strengthens operational transparency. Budgets, expenses, lifecycle states, supporting evidence, and reporting will be connected within a controlled workflow that can be examined and verified.

Fourth, it improves investor visibility. The resulting Beta Candidate will show how an investor can review relevant operational and financial evidence without implying that the platform is already processing live investments or production payments.

Fifth, it strengthens evidence generation. Completion can be supported through repository history, tests, acceptance results, demonstration scenarios, system records, and reporting outputs. This gives grant programmes, accelerators, investors, venture studios, and strategic partners a more concrete basis for evaluating delivery.

The resulting value is not based on projected valuation, commercial returns, or an assumed production launch. It is based on an observable improvement in the product: a reviewer should be able to see and verify a substantially more complete operational workflow than is available in the current Alpha.

Completion of the round will also place AgriPartners in a stronger position for an Operational Readiness Review. It will not predetermine the outcome of that review or authorize live pilot operations, but it will provide the product evidence required for a structured readiness assessment.

2.3 Why This Is Fundable

In this context, fundable means that the proposed Development Round is sufficiently defined, measurable, and verifiable for funding consideration. It does not imply approval by any particular grant programme, accelerator, investor, venture studio, or strategic partner.

The proposed Development Round represents an appropriate funding milestone because it is specific, bounded, measurable, and capable of evidence-based verification.

The requested \$40,000 is assigned exclusively to product development. The round is organized around one defined outcome: completion of the Pilot Operations & Investor Evidence Beta Candidate. It does not combine product development with Corporate Setup, agricultural assets, construction, operational Feedlot expenses, banking infrastructure, or Pilot Capital.

This separation makes the funding request easier to assess. Reviewers can evaluate whether the proposed development activities are necessary, whether the resulting deliverables are relevant, and whether completion has been demonstrated.

The round is also suitable for milestone-based funding and reporting because its scope can be divided into identifiable deliverables with explicit dependencies, acceptance criteria, evidence requirements, and exit criteria. Progress does not need to be assessed through general statements about development activity. It can be assessed through completed workflows, functioning product capabilities, test results, demonstration evidence, and documented acceptance.

Technical risk is bounded because the round extends an existing platform and completed accounting foundations. It is not dependent on proving an entirely new product concept or building the complete system from the beginning.

Risk nevertheless remains. The Project Expense API and Authorization, user experience, evidence handling, security, integration, and end-to-end verification still require disciplined implementation and validation. The funding case is credible because these remaining risks can be addressed within a controlled development scope and measured against predefined completion criteria.

The Development Round is therefore suitable for funding consideration as a discrete value milestone: the requested capital is tied to a defined product outcome, and that outcome can be evaluated using verifiable technical and user-visible evidence.

2.4 Why the Current Baseline Reduces Execution Risk

AgriPartners begins this Development Round with a verified Alpha platform rather than a concept, specification, or prototype consisting only of isolated demonstrations.

The existing product baseline includes functioning product portals and workflows, onboarding and reporting capabilities, a Treasury Dashboard, Presentation Mode, wallet-based Alpha authentication, and a NEAR Testnet demonstration environment. These capabilities provide an established product context within which the Beta Candidate can be completed.

Execution risk is further reduced by the completed financial workflow foundation and project expense accounting foundation. The repository already contains core structures for workflow budgets, project expenses, immutable state history, supporting evidence, derived reservations, and concurrency-safe financial controls.

This means the proposed round does not need to recreate the underlying accounting model before producing user-visible results. Development can proceed from established data structures, financial invariants, workflow concepts, and verification coverage.

Repository maturity provides an additional risk reduction. The project maintains an auditable implementation history, structured documentation, testing infrastructure, and a verified engineering baseline. Repository Documentation Ready v1 provides an internally consistent source for current product capabilities, architecture, business rules, financial boundaries, and implementation status.

Existing demonstration capabilities reduce the amount of work required to make future progress externally visible. AgriPartners can already present the Alpha platform and its principal roles. The Development Round extends this capability toward a complete operational demonstration rather than introducing demonstration readiness only at the end of development.

These factors do not eliminate execution risk. The Project Expense API and Authorization, Operator Workspace, evidence workflow, investor transparency experience, reporting integration, quality assurance, security validation, and final end-to-end demonstration must still be completed and verified.

They do, however, reduce uncertainty compared with a concept-stage project. The proposed Beta Candidate is based on existing code, tested foundations, established product workflows, documented architecture, and a defined next milestone. This provides a credible basis for assessing the requested Development Round as a controlled progression from Alpha to a demonstrable Beta Candidate.

3. Development Round Definition

The AgriPartners Development Round is a dedicated, product-only funding phase established to complete the **Pilot Operations & Investor Evidence Beta Candidate**.

In this context, **product-only** means that Development Round funds may be used only for activities directly required to build, integrate, verify, secure, document, and demonstrate the approved Beta Candidate.

It is a separate component of the broader AgriPartners funding architecture. Its scope, Use of Funds, completion logic, and acceptance conditions are governed independently from Corporate Setup, Operational Readiness, and Pilot Capital.

3.1 Purpose of the Round

The primary purpose of the Development Round is to advance AgriPartners from its current verified Alpha baseline to a demonstrable Beta Candidate.

The target outcome is the Pilot Operations & Investor Evidence Beta Candidate: a coherent product milestone that connects controlled operational workflows, Project Expense management, authorization, supporting evidence, Investor transparency, reporting, and demonstration capabilities.

The round is intended to produce measurable product outcomes rather than finance general organizational activity or open-ended development. Completion must be demonstrated through defined Deliverables, Verification Evidence, and Acceptance Criteria.

The Development Round does not by itself establish Production Readiness, Operational Readiness, regulatory readiness, or authorization to begin a real agricultural Pilot.

3.2 Funding Ask

The approved Development Round funding request is:

USD 40,000

The full amount is designated for product-development activities required to complete and verify the Beta Candidate.

The Development Round is intentionally defined as a product-only request. It does not include:

Corporate Setup or establishment of AgriPartners OÜ;

initial corporate, legal, tax, or accounting readiness;

agricultural assets, livestock, construction, or Feedlot infrastructure;

working capital or operational expenses for a real Pilot;

Feedlot Pilot Capital;

Hissar Pilot Capital;

production banking, payment, custody, or settlement infrastructure.

Detailed allocation of the USD 40,000 is defined later in this Funding Package. This section establishes only the approved amount and its product-development boundary.

3.3 Development Period

The Development Round is defined as a milestone-based development phase rather than an unconditional calendar commitment.

Its duration is governed by completion of the approved Scope, Deliverables, verification requirements, and Acceptance Criteria. A target schedule may be established for planning and funding administration, but the passage of time alone does not constitute progress or completion.

The round begins when the required funding and any agreed commencement conditions are satisfied. It concludes when the Beta Candidate has met the approved Completion and Acceptance Criteria.

Any schedule presented to a funder must distinguish between:

estimated delivery dates;

Milestone completion;

verified acceptance of Deliverables.

A planned date, marketing event, external presentation, or target launch date cannot substitute for completion of the required product milestone.

3.4 Funding Model and Milestone Logic

Development Round funding supports completion of defined and reviewable product Milestones.

Progress is determined through:

completion of measurable Deliverables;

satisfaction of Milestone-specific Exit Criteria;

production of required Verification Evidence;

confirmation that applicable Dependencies and Acceptance conditions have been addressed.

The specific forms of Milestone Verification Evidence are defined in the later verification and reporting sections of this Funding Package.

Milestone reporting must be based on demonstrated results rather than expenditure alone. Use of funds may show that development activity occurred, but expenditure by itself does not establish that a Milestone has been completed.

Depending on a specific funder's requirements, the Development Round may be financed through a single tranche, multiple Milestone-based tranches, or another controlled release structure. The funding mechanism may change, but the approved product objective and Completion Criteria must remain consistent.

Milestone completion is independent of promotional schedules, fundraising events, public demonstrations, or planned launch dates. No external deadline may redefine an incomplete product Milestone as complete.

Completion of the Development Round confirms completion of the approved Beta Candidate Scope only. It does not constitute an Operational Readiness decision or authorize the start of a real Feedlot or Hissar Pilot.

3.5 Boundaries of the Round

Activities belong within the Development Round when they are directly necessary to build, integrate, verify, secure, document, deploy for controlled demonstration, or present the approved Beta Candidate.

The Development Round may therefore fund:

product engineering;

backend and frontend development;

database and workflow integration;

quality assurance and testing;

product-level security work;

controlled development or demonstration deployment;

technical and user documentation required for the milestone;

demonstration data, scenarios, and evidence preparation;

completion reporting and Deliverable verification.

All funded activities must have a clear relationship to the approved Beta Candidate outcome.

The Development Round does not finance company formation, general corporate administration, live agricultural operations, physical Pilot infrastructure, livestock acquisition, production financial services, Investor returns, or unrestricted business expenditure.

These boundaries prevent the product milestone from being combined with legally, operationally, and financially distinct activities. The later Use of Funds and Excluded Costs sections provide detailed classification and treatment of individual cost categories.

3.6 Relationship to Corporate Setup and Pilot Funding

Funding Strategy v1 separates the AgriPartners financing architecture into distinct components with different purposes, eligibility rules, risks, and completion conditions.

Corporate Setup covers establishment of AgriPartners OÜ and the initial corporate, legal, accounting, and administrative readiness required to enter into appropriate agreements and receive funding. It is governed separately from the USD 40,000 Development Round.

Where a funder permits a broader readiness commitment, Development and Corporate Setup may be presented within one external funding proposal. However, AgriPartners must continue to account for them as separate internal budget components. Combining them in an external proposal does not change the product-only definition of the Development Round.

Following completion of the Beta Candidate, AgriPartners must conduct an Operational Readiness Review. Product completion is one input to that review, not a substitute for it. The review must also consider applicable corporate, legal, financial, Operator, funding, and operational readiness conditions.

A real Pilot may begin only following an explicit GO decision by the appropriate AgriPartners governance authority or its designated decision-makers. Neither completion of the Development Round nor availability of a planned Pilot date automatically produces that decision.

The Feedlot Pilot Round and Hissar Pilot Round are separate Pilot Capital components. They are intended to finance their respective real-world Pilot requirements and are governed independently from the Development Round and from each other.

Accordingly:

the Development Round finances completion of the Beta Candidate;

Corporate Setup finances establishment and initial readiness of the company;

the Operational Readiness process determines whether a real Pilot may proceed;

the Feedlot Pilot Round finances the approved Feedlot Pilot;

the Hissar Pilot Round finances the approved Hissar Pilot.

This separation preserves financial discipline and funding transparency, maintains clear Use-of-Funds controls, prevents cross-subsidisation between independent funding components, and ensures that completion of one component is not presented as completion of another.

4. Current Product Baseline

This section establishes the verified starting point for the Development Round.

The baseline was reviewed against the current main branch of the public farabek/agripartners repository at commit: 2d46df862f49346e876d9bb16a75d4714c69a9c8

The repository classifies the current product as AgriPartners Alpha v1.2 — working prototype on NEAR Testnet.

AgriPartners is beyond the concept stage: it contains an implemented browser application, backend API, PostgreSQL database model, role-based workflows, NEAR Testnet integration, demonstration capabilities, executable tests, and maintained technical and product documentation.

The current baseline is not a production investment platform. It does not accept live investments and does not provide production custody, banking, payment execution, crypto-to-fiat conversion, KYC/KYB, Mainnet settlement, or live agricultural pilot operations.

4.1 Product Capabilities Public and demonstration experience

The current frontend provides an implemented public-facing product experience, including:

a public landing page; an Alpha opportunity catalog; Project and Deal presentation views; Feedlot and Hissar demonstration profiles; audience-specific Presentation Mode; guided Investor, NEAR ecosystem, accelerator, and enterprise demonstrations.

Presentation Mode can be reviewed without configuring a backend, database, wallet, or Testnet funds. It is a demonstration capability and does not represent a live investment offering.

Feedlot and Hissar profiles use demonstration data derived from the approved Master Investment Models. Their displayed activity, projected economics, recorded returns, and lifecycle states are not evidence of deployed capital, audited performance, or production settlement.

Investor experience

The Investor Portal is implemented and demonstrable for Alpha-stage workflows.

It provides:

opportunity and Project review; investor profile and portfolio views; projected economic information with Alpha-stage status framing; Project progress and reporting visibility; recorded return information; withdrawal-readiness and lifecycle presentation; access to Farmer-submitted reports where supported by the current workflow.

The Investor experience demonstrates how relevant Project information may be organized and disclosed. It does not provide live investor onboarding, KYC/KYB, production capital intake, custody, banking, or production settlement.

Projected, recorded, paid, and reconciled values remain distinct concepts. Alpha return records are demonstration and workflow-validation records rather than audited or production-settled performance.

Farmer experience

The Farmer Portal is implemented and demonstrable as an Alpha product workflow.

It currently supports:

Farmer role and profile records; access to assigned Deals; funding-status visibility; Production Cycle visibility; operational progress reporting; funding confirmation; report submission; access controls based on the current Alpha identity model.

Some current Farmer flows retain wallet-linked, NEAR-funding, withdrawal, and smart-contract behavior from the Legacy Testnet Alpha. These capabilities are historical technical demonstrations and are not the target production financial architecture.

Under the approved target model, the Farmer is a fiat-only, non-crypto product role. The current repository has not yet completed the implementation migration required to remove all Farmer wallet and crypto dependencies.

Administrative experience

The current Alpha includes administrative routes and product controls for managing platform records and selected lifecycle actions.

The administrative experience supports aspects of:

Deal and Project preparation; participant and role coordination; lifecycle monitoring; reporting oversight; return and treasury record visibility; selected administrative actions; Alpha-stage access control.

Current application roles and administrative permissions do not establish legal signing authority, payment authority, corporate mandate, or production-grade segregation of duties.

Reporting and lifecycle visibility

The current platform includes implemented reporting and lifecycle capabilities across Investor, Farmer, and administrative experiences.

These include:

Farmer progress reports; Production Cycle records; Deal and Project lifecycle events; recorded return information; operational status visibility; role-filtered access to relevant information.

The platform can demonstrate how operational activity becomes visible across participant roles. It does not yet provide the complete evidence-linked Project Expense workflow planned for the Beta Candidate.

Treasury visibility

The Treasury Dashboard and Treasury Shadow Accounting capabilities are implemented for Alpha-stage visibility and demonstration.

They show how capital activity, return records, and selected operational events may be organized and presented. Treasury Shadow Accounting is non-authoritative and does not replace bank records, accounting records, contracts, reconciliation evidence, or production treasury controls.

Wallet authentication and NEAR Testnet demonstration

Wallet-signature authentication is implemented and verified within the Alpha environment.

The current platform also demonstrates selected NEAR Testnet capabilities, including:

wallet-linked authentication; smart-contract experimentation; contract status and balance reads; selected lifecycle and transaction actions; recording of Testnet transaction references; presentation of blockchain-supported transparency concepts.

These capabilities are limited to NEAR Testnet. They do not constitute audited smart contracts, Mainnet readiness, production custody, production payments, or authoritative evidence that a fiat transaction occurred.

4.2 Technical Baseline Application architecture

The current application uses a hybrid browser, API, database, and Testnet architecture:

Browser application | v Node.js / Express REST API | v PostgreSQL database

Wallet-signed messages and selected Legacy Alpha actions | v NEAR Testnet

The frontend is a Vite-built single-page application using JavaScript, HTML, and CSS. It uses hash-based routing and provides public, Investor, Farmer, administrative, Treasury, and Presentation Mode experiences.

The backend is a Node.js and Express REST API. Its current responsibilities include:

authentication; role-scoped access; profiles; Deals and Projects; Farmer cycles and reports; investor views; administrative actions; return records; treasury visibility; database access and migrations; selected NEAR Testnet interactions.

PostgreSQL is the operational application data store. Ordered SQL migrations are the schema authority.

Authentication baseline

The Alpha contains two implemented authentication paths:

legacy username-and-password authentication using role-bearing JWTs; wallet-signature authentication using wallet-linked JWTs.

The wallet flow uses a backend-issued challenge, a signed NEAR message, access-key verification, and a time-limited JWT.

This is an Alpha authentication baseline. It is not a completed production identity, KYC/KYB, legal-authority, or corporate-mandate system. Existing limitations include Testnet-specific configuration, process-local authentication elements, browser-accessible token storage, and continued wallet dependency in Legacy Farmer flows.

NEAR technical baseline

The repository contains NEAR Testnet integration using near-api-js and Rust smart-contract code using near-sdk.

The current integration supports Testnet experimentation with wallet authentication, contract deployment and initialization, selected state reads, lifecycle actions, funding or withdrawal demonstrations, and transaction references.

Farmer withdrawal, Farmer NEAR balances, smart-contract payouts, and related signer behavior remain Legacy Testnet Alpha functionality. They must not be presented as the approved production financial model.

Under the approved architecture, any future NEAR audit and automation infrastructure must remain on the External Investor and AgriPartners OÜ Estonia side. Uzbekistan-facing Operator and Farmer workflows must remain fiat-only.

Financial Workflow Foundation

Stage 2 Slice 1 — Financial Workflow Foundation is completed and merged.

Migration 016 establishes a database foundation for:

Uzbekistan Operator representation; Operator, Farmer, and Deal assignment; one financial workflow per Deal; Estonia-layer crypto-conversion records; fiat-only Operator transfer records; financial evidence references; immutable financial state events; controlled financial-state transitions; idempotency protections; separation between instruction and authorization; event-backed state projections.

The modeled workflow distinguishes Investor funding, crypto conversion where applicable, fiat clearing, Operator disbursement, Operator confirmation, Project expense recording, returned proceeds, reconciliation, and Investor settlement.

These are implemented database structures and constraints. They do not execute production conversion, banking, payments, custody, or settlement.

Project Expense Accounting Foundation

Stage 2 Slice 2 — Project Expense Accounting Foundation is completed and merged.

Migration 017 establishes database support for:

approved expense categories; financial workflow budgets; Project Expenses; immutable Project Expense lifecycle events; Project Expense evidence references; expense states including REQUESTED, APPROVED, REJECTED, CANCELLED, and PAID; requester, approver, and payer separation; authoritative fiat-payment evidence requirements; derived budget reservations; budget capacity controls; overspending protection; concurrency-safe approval behavior; linkage between paid Project Expenses and financial workflow events; preservation of historical workflow records.

Project Expense reservations are derived rather than independently editable. Budget reductions cannot reduce available capacity below existing reservations. A paid Project Expense requires the relevant approved state and authoritative fiat-payment evidence reference.

This foundation is implemented and verified at the PostgreSQL layer. It is not yet exposed as a complete user-facing product workflow.

Testing and verification baseline

The repository contains executable backend tests using Jest and Supertest, together with migration-specific and PostgreSQL runtime verification.

Repository evidence includes tests for:

authentication; wallet authentication; Investor routes; Farmer routes and reporting; profiles and onboarding; NEAR services; financial workflow migration behavior; Project Expense accounting migration behavior; Project Expense runtime behavior; concurrency and competing transitions; budget reductions and overspending controls; migration repeat-run behavior; rollback and immutable history.

The Project Expense runtime tests use a disposable PostgreSQL verification harness with safeguards intended to prevent execution against production, staging, shared, or otherwise important databases.

The repository also contains a GitHub Actions workflow configured to run backend tests and build the frontend for pushes and pull requests targeting main.

This baseline review confirms the presence of the tests, verification harness, and CI configuration in the repository. It does not claim that the complete test suite was independently rerun as part of preparing this Funding Package section.

Repository and documentation baseline

The repository has reached Repository Documentation Ready v1.

The maintained documentation baseline includes:

a canonical Platform Model; accepted high-level Architecture; Product Book and documentation navigation; approved operating and financial models; documented Estonia-to-Uzbekistan fiat boundary; software delivery roadmap; release documentation; pilot planning and readiness materials; legal and contractual planning documents; documentation authority and governance rules.

Current code, migrations, configuration, and executable tests remain authoritative for implemented behavior. Documentation defines approved architecture and operating boundaries but does not convert planned capabilities into implemented functionality.

The latest reviewed main commit contains the Repository Documentation Ready v1 merge. The canonical Platform Model retains the earlier Stage 2 implementation checkpoint as its technical evidence reference.

Planned but unimplemented capabilities

The following capabilities are not part of the current verified baseline:

Project Expense API; application-level Project Expense authorization service; Operator expense interface or dashboard; complete evidence submission and review workflow; complete Investor Project Expense transparency experience; integrated expense reporting and export layer; completed fiat-only Farmer and Operator product migration; non-wallet production authentication for Uzbekistan-facing roles; production-grade identity and authority controls; dedicated contract registry; dedicated verified legal-entity registry; production KYC/KYB; electronic-signature infrastructure; bank or payment-provider integration; live crypto-to-fiat conversion; production fiat disbursement or repayment execution; production reconciliation; production investor settlement; production custody; stablecoin accounting; audited Mainnet smart contracts; Mainnet deployment; production operational readiness; live Feedlot or Hissar pilot operations.

These items must not be described as completed product capabilities.

The current product should therefore be represented as an implemented and demonstrable Alpha platform with verified financial and Project Expense database foundations. It should not be represented as a completed Beta, production platform, regulated investment platform, live payment system, or operational agricultural pilot.

5. Development Objective

The single development objective of the Development Round is:

To transform the current verified AgriPartners Alpha platform into the Pilot Operations & Investor Evidence Beta Candidate by completing an integrated, controlled, evidence-linked, and Investor-visible operational workflow.

This is the single governing product objective of the Development Round.

This objective defines the target product state for the Development Round. All subsequent Scope, Work Packages, Deliverables, Milestones, budget allocations, Verification Evidence, and Completion Criteria must be traceable to it.

5.1 Problem Addressed by the Development Round

The current AgriPartners platform contains implemented participant experiences, operational reporting capabilities, financial workflow foundations, and a verified Project Expense accounting foundation. However, these capabilities do not yet form a complete, integrated product workflow suitable for a Beta-level operational demonstration.

The principal product gap is the absence of a coherent connection between:

controlled Project Expense management;

application-level authorization;

Operator-facing operational activity;

supporting evidence;

Investor-facing transparency;

reporting and lifecycle visibility.

The current database foundations can represent financial workflows, budgets, Project Expenses, lifecycle events, evidence references, reservations, and financial controls. The current platform can also demonstrate Investor, Farmer, administrative, reporting, Treasury, and Presentation Mode experiences.

However, a reviewer cannot yet use the product to follow one complete and controlled Project Expense workflow from operational initiation through authorization, evidence, lifecycle history, and appropriate Investor visibility.

As a result, the current implementation demonstrates important components but does not yet demonstrate the complete product proposition represented by the Beta Candidate.

The Development Round is specifically designed to address this gap by completing the product layer that connects the verified foundations into one consistent and reviewable experience.

5.2 Transition from Alpha to Demonstrable Beta

The current Alpha demonstrates that AgriPartners' principal product roles, workflow concepts, database foundations, reporting capabilities, and Testnet-supported transparency concepts can be implemented.

The Beta Candidate must demonstrate that these elements function together as a coherent product experience.

The intended transformation is:

Verified Alpha foundations

|

v

Integrated operational workflow

|

v

Controlled Project Expense management

|

v

Evidence-linked lifecycle visibility

|

v

Appropriate Investor transparency

|

v

Demonstrable Beta Candidate

Each stage of this transformation builds upon capabilities and technical foundations already present in the verified current baseline.

At the current Alpha stage, AgriPartners provides individual product experiences and verified technical foundations. At the Beta Candidate stage, the platform must connect those elements so that:

an authorized operational user can manage a Project Expense through the supported lifecycle;

relevant controls and role boundaries are consistently applied;

supporting evidence is associated with appropriate operational and financial records;

lifecycle history remains reviewable;

relevant Project Expense information is presented appropriately to an Investor;

the complete workflow can be demonstrated and verified end to end.

This transition is a product-completeness milestone. It is not a transition to production operations.

The Beta Candidate will remain distinct from:

a production investment platform;

a regulated financial service;

a live custody or payment system;

a production banking or settlement integration;

a Mainnet deployment;

an operational Feedlot or Hissar Pilot;

an approved Operational Readiness state.

The term **Beta Candidate** therefore describes a complete and reviewable candidate product milestone. It does not imply that production, regulatory, corporate, security, or operational approval has been granted.

5.3 Target Value Milestone

The formal target value milestone of the Development Round is:

Pilot Operations & Investor Evidence Beta Candidate

This milestone represents the point at which AgriPartners can demonstrate how controlled agricultural Project activity is recorded, authorized, supported by evidence, and disclosed appropriately to an Investor within one integrated product workflow.

It is a value milestone because it produces a measurable change in the product.

Before completion, the principal components exist at different levels of maturity, but the complete operational and Investor evidence workflow is not available.

After completion, the resulting Beta Candidate must provide a consistent connection between:

Project context;

operational roles;

controlled Expense activity;

authorization;

budgets and financial controls;

supporting evidence;

immutable or reviewable lifecycle history;

reporting;

Investor-facing transparency;

demonstration evidence.

The milestone is not achieved by changing the product label from Alpha to Beta. It is achieved only when the required product capabilities are integrated, demonstrable, verified, and accepted against the approved criteria.

The value created by this milestone must therefore be measurable through completed capabilities, reviewable against documented evidence, and demonstrable through the integrated product workflow rather than remaining theoretical.

The milestone has been selected because it builds directly on the verified current baseline while addressing the most important product-completeness gap. It creates a reviewable result that can be evaluated by grant programmes, accelerators, Investors, venture studios, and strategic partners without requiring the platform to claim Production Readiness or live Pilot execution.

5.4 Development Round Success Definition

The Development Round is successful when the Pilot Operations & Investor Evidence Beta Candidate has been completed and accepted as a measurable product outcome.

Success requires that:

the approved Beta Candidate capabilities are complete;

the relevant operational, evidence, reporting, and Investor-transparency experiences function as one integrated workflow;

applicable roles and product-level authorization controls operate consistently;

Project Expense activity is connected to relevant budgets, lifecycle states, and supporting evidence;

the complete intended scenario can be demonstrated end to end;

required quality, security, and documentation conditions are satisfied;

completion is supported by required technical, product, testing, and demonstration evidence;

approved Acceptance and Completion Criteria are met;

no critical unresolved defect prevents the intended Beta Candidate workflow from being demonstrated.

Development activity, expenditure, elapsed time, or completion of isolated components does not by itself constitute success.

Success must be established through demonstrable functionality and documented Verification Evidence. Detailed evidence requirements and Acceptance Criteria are defined in the corresponding later sections of this Funding Package.

Completion of the Development Round confirms that the approved product transformation has been achieved. It does not confirm Corporate Setup, Production Readiness, Operational Readiness, regulatory approval, live funding capability, or authorization to begin a real Pilot.

This Development Objective is the controlling product reference for the remainder of the Funding Package. Every subsequent section must demonstrate how its proposed Scope, Deliverables, Work Packages, Milestones, budget allocations, evidence, and Acceptance Criteria contribute directly to achieving this objective. Any activity that does not contribute directly to the objective must be excluded from the Development Round or separately justified under the approved funding architecture.

6. Pilot Operations & Investor Evidence Beta Candidate

The **Pilot Operations & Investor Evidence Beta Candidate** is the completed demonstrable product state produced by the Development Round.

It connects operational activity, controlled Project Expense management, supporting evidence, reporting, lifecycle history, and appropriate Investor transparency within one coherent product experience.

This section defines what the completed Beta Candidate will be. It does not represent the current Alpha baseline or describe the development process required to reach the target state.

6.1 Beta Candidate Definition

The Pilot Operations & Investor Evidence Beta Candidate is an integrated version of AgriPartners that demonstrates how authorized participants can manage and review the operational and financial evidence associated with an agricultural Project.

The completed Beta Candidate will provide:

- a coherent Project-based operational context;
- a controlled Project Expense workflow;
- role-appropriate authorization and actions;
- workflow budget visibility and control;
- supporting-evidence association;
- reviewable expense and operational lifecycle history;
- structured reporting;
- appropriate Investor-facing transparency;
- a complete end-to-end demonstration experience.

The Beta Candidate will connect these capabilities as one product state. It will not consist only of isolated screens, database structures, technical demonstrations, or separately functioning features.

Its operational workflow must be demonstrable from the initiation of an authorized Project Expense through the applicable review, authorization, evidence, status, reporting, and disclosure stages supported by the product.

Its evidence workflow must allow relevant operational and financial records to be associated with supporting evidence and reviewed according to the applicable product role and disclosure boundary.

The Beta Candidate is considered a completed product milestone only when this integrated experience can be demonstrated and reviewed against documented evidence and acceptance criteria.

6.2 Operator-visible Outcome

Within the completed Beta Candidate, an authorized Operator will have a coherent product workspace for managing the supported Project Expense and evidence workflow.

Subject to the Operator's assigned product role and authority, the completed experience will allow the Operator to:

- access the relevant Project context;

- review the Project's financial workflow and applicable budgets;

- initiate or record a Project Expense within an approved category;

- provide the required expense information;

- associate supporting evidence with the relevant Expense;

- review the current Expense status;

- perform permitted review, authorization, rejection, cancellation, or payment-recording actions;

- follow the operational and Expense lifecycle history;

- review available and reserved budget information;

- identify actions that cannot proceed because of applicable controls;

- prepare or review operational reports;

- monitor the information made available for Investor review;

- follow one complete supported workflow from initiation to its accepted end state.

The product will distinguish between operational participation, expense initiation, authorization, payment recording, and disclosure. An authenticated product role alone will not be presented as proof of legal authority, corporate mandate, contractual authority, or external payment authority.

The Operator-visible experience will present budget and Expense information in a form that supports controlled operational decision-making. It will show relevant states, amounts, categories, evidence references, and lifecycle history without treating the interface as a bank, accounting system, or payment-execution service.

Where an action is not permitted by the applicable product controls, the completed experience will prevent or clearly reject that action rather than relying solely on procedural guidance.

The resulting Operator experience will therefore demonstrate controlled operational accountability: Project Expenses are not presented as informal entries but as role-aware records connected to budgets, evidence, state history, and appropriate review.

6.3 Investor-visible Outcome

Within the completed Beta Candidate, an Investor will be able to review an appropriate and understandable view of Project operations and approved Project Expense information.

Subject to the applicable Project relationship, role, status, and disclosure policy, the Investor experience will provide visibility into:

Project identity and context;

operational progress;

relevant reporting periods or Production Cycles;

approved Project budgets or budget summaries where disclosure is permitted;

disclosed Project Expense categories and amounts;

Expense lifecycle status;

supporting-evidence availability or approved evidence references;

relevant operational reports;

reviewable lifecycle history;

distinctions between projected, recorded, approved, paid, reconciled, and completed information.

Investor visibility will be controlled rather than unrestricted. The Beta Candidate will not automatically disclose every internal record, personal document, commercial detail, administrative action, or evidence item.

Investor-facing information must remain subject to:

the Investor's relationship to the Project;

role-based access;

Project status;

approval and disclosure controls;

privacy requirements;

legal and operational information boundaries.

The Investor experience will demonstrate how AgriPartners can provide structured transparency without implying that an on-screen record independently proves a bank payment, legal agreement, audited expense, or production settlement.

Where supporting evidence is available, the product will present its status and relationship to the relevant operational record clearly. Evidence references, uploaded materials, blockchain references, and internal records must not be represented as having greater authority than they possess.

The completed Investor experience will therefore provide a reviewable connection between Project activity, Project Expenses, supporting evidence, reporting, and lifecycle progress while preserving appropriate disclosure boundaries.

6.4 Demonstration Value

The Beta Candidate will be suitable for external demonstration because it will present one coherent and reviewable product workflow rather than a collection of disconnected technical foundations.

A reviewer will be able to observe:

how a Project is represented;

how an authorized operational user interacts with the Project;

how a Project Expense enters and progresses through the supported lifecycle;

how budget controls affect permitted actions;

how authorization boundaries are applied;

how supporting evidence is associated with the Expense;

how operational history remains reviewable;

how appropriate information becomes visible to an Investor;

how the product distinguishes workflow records from external legal, banking, and accounting authority.

For grant programmes, the Beta Candidate will provide evidence that funded development produced a defined and demonstrable product outcome.

For accelerators, it will provide a reviewable representation of the product's principal operational and transparency proposition.

For investors and venture studios, it will show how the platform can connect agricultural operations, controlled expense records, evidence, and Investor visibility without claiming that production financial infrastructure already exists.

For strategic partners, it will provide a concrete basis for evaluating potential operational, technology, compliance, or ecosystem collaboration.

The demonstration value will come from observable functionality and supporting verification evidence. It will not depend solely on presentation materials, architectural descriptions, projected business results, or long-term product claims.

The Beta Candidate should allow a reviewer to understand what the platform does, follow the supported workflow, inspect the resulting records, and distinguish completed functionality from remaining production requirements.

6.5 Remaining Non-Production Boundaries

Completion of the Beta Candidate will not mean that AgriPartners is production-ready or authorized to conduct live investment or agricultural pilot activity.

The Beta Candidate will not represent:

a production investment platform;

a regulated financial service;

an authorized securities, crowdfunding, custody, exchange, or payment service;

live Investor onboarding or KYC/KYB;

acceptance of live Investor capital;

production banking or payment integration;

live crypto-to-fiat conversion;

production custody of fiat or cryptoassets;
production fiat disbursement, repayment, or settlement;
audited accounting or bank reconciliation;
audited Mainnet smart contracts;
NEAR Mainnet deployment;
a production treasury system;
completed Corporate Setup;
completed legal or regulatory readiness;
an Operational Readiness approval;
an operational Feedlot pilot;
an operational Hissar pilot;
purchased livestock, constructed facilities, or funded agricultural operations;
verified, audited, or guaranteed investment returns.

Demonstration records, Project profiles, Project Expenses, evidence, reports, lifecycle states, and return information within the Beta Candidate will remain controlled product and demonstration records unless separately supported by authoritative external evidence.

An on-chain reference will not establish that fiat cleared, an external payment occurred, a legal agreement was executed, an expense was audited, or a production settlement was completed.

Completion of the Beta Candidate will make the product eligible to proceed to a separate Operational Readiness Review. It will not predetermine the result of that review. Corporate, legal, financial, security, Operator, funding, and operational readiness must remain independently assessed under the approved governance process.

The Development Round will therefore produce a completed and demonstrable Beta Candidate—not a live financial or agricultural operation.

This definition is the product-state reference for the remaining sections of the Funding Package. All subsequent scope, work packages, deliverables, budget allocations, milestones, verification evidence, completion criteria, and expected outcomes must contribute directly to producing the Beta Candidate defined in this section.

7. Development Scope

The Development Scope defines the work that must be completed to transform the verified current baseline into the **Pilot Operations & Investor Evidence Beta Candidate**.

It establishes three priority levels:

Minimum Viable Development Scope — mandatory for successful completion;

Recommended Development Scope — materially strengthens the Beta Candidate;

Optional Scope — may be activated only when it does not place mandatory completion at risk.

This classification governs all subsequent Work Packages, Deliverables, Budget Allocation, Milestones, Verification, and Completion Criteria.

7.1 Minimum Viable Development Scope

The Minimum Viable Development Scope is the non-negotiable scope required to produce the approved Beta Candidate.

The Development Round cannot be considered successfully completed unless every mandatory capability has been delivered, integrated, demonstrated, and accepted.

Project Expense product capability

The Beta Candidate must provide a complete user-visible Project Expense capability built upon the existing verified accounting foundation.

The completed product must support the applicable Expense lifecycle, including:

creation or initiation of a Project Expense;

association with the correct Project, financial workflow, budget, category, currency, and Operator context;

review of the current Expense state;

permitted authorization decisions;

rejection or cancellation where applicable;

recording of the supported payment state;

preservation and presentation of the relevant lifecycle history.

The product experience must remain consistent with the approved fiat-only Operator boundary and must not require Uzbekistan-facing cryptocurrency, wallets, tokens, smart contracts, or on-chain transactions.

Product-level authorization and operational controls

The Beta Candidate must apply role-appropriate authorization to Project Expense actions.

The mandatory scope must ensure that:

only an authenticated and permitted product user can perform a supported action;

prohibited actions are rejected consistently;

requester, approver, and payer responsibilities remain appropriately separated;

Project, workflow, Operator, budget, category, and currency boundaries are preserved;

Expense transitions follow the permitted lifecycle;

applicable budget-capacity and overspending controls remain effective;

actions produce reviewable records.

Product authorization demonstrates controlled application behaviour. It does not establish legal signing authority, corporate mandate, bank authority, or regulatory approval.

Operator Workspace

The Beta Candidate must provide an integrated Operator-facing experience for the supported operational workflow.

An authorized Operator must be able to:

- access the relevant Project context;
- review applicable workflow and budget information;
- initiate and follow Project Expenses;
- provide required operational information;
- associate supporting evidence;
- perform permitted review or authorization actions;
- identify blocked or rejected actions;
- review relevant lifecycle and reporting information;
- complete the supported end-to-end operational scenario.

The Operator experience must present a coherent workflow rather than a collection of disconnected administrative screens.

Evidence management

The Beta Candidate must provide a complete evidence workflow for the supported Project Expense scenario.

The mandatory scope must allow relevant evidence to be:

- associated with the correct Project Expense;
- classified according to its supported purpose;
- linked to the relevant lifecycle state or action;
- reviewed by an appropriately authorized user;
- retained as part of the reviewable product record;
- presented to an Investor only where disclosure is permitted.

The product must preserve the distinction between evidence references, uploaded or recorded materials, bank or payment records, accounting records, contractual documents, and supplementary blockchain references.

No internal record or on-chain reference may be presented as independent proof of a fiat payment, executed agreement, audited expense, or production settlement.

Investor transparency

The Beta Candidate must provide an appropriate Investor-facing view of the supported operational and Project Expense workflow.

Subject to Project relationship, role, state, approval, and disclosure controls, the Investor must be able to review:
relevant Project context;

operational progress;

disclosed budget or budget-summary information;

disclosed Project Expense information;

Expense status and relevant lifecycle history;

supporting-evidence availability or permitted evidence references;

applicable operational reports;

clear distinctions between projected, recorded, approved, paid, reconciled, and completed information.

Investor transparency must remain controlled. The mandatory scope does not include unrestricted access to internal, personal, commercially sensitive, or legally restricted information.

Reporting

The Beta Candidate must connect operational activity, Project Expenses, evidence, and Investor transparency through understandable reporting.

Mandatory reporting must be sufficient for:

Operator review of the supported workflow;

Investor review of permitted Project information;

verification of the end-to-end demonstration;

assessment of Development Round completion.

Reports must preserve the status and authority of the underlying records and must not imply audited or production-settled results.

End-to-end demonstration capability

The Beta Candidate must support a complete, repeatable, and reviewable demonstration of the approved product scenario.

The demonstration must show:

the relevant Project context;

authorized Operator participation;

controlled Project Expense progression;

budget and lifecycle controls;

supporting evidence;

operational reporting;

appropriate Investor visibility;

reviewable resulting records.

The demonstration must rely on observable product behaviour and system records rather than presentation materials alone.

Demonstration data must be clearly identified and must not be presented as live Investor funding, real pilot expenditure, audited performance, or verified investment returns.

Quality, security, documentation, and controlled deployment

The minimum scope must include the quality and supporting conditions required for the Beta Candidate to be credible and reviewable.

This includes:

- verification of the principal user journeys;
- regression protection for relevant existing capabilities;
- validation of authorization and prohibited-action behaviour;
- validation of Project Expense, evidence, and budget controls;
- resolution of critical defects affecting the approved workflow;
- product-level security review appropriate to the Beta Candidate;
- controlled demonstration deployment or equivalent review environment;
- technical and user documentation necessary to operate and assess the Beta Candidate;
- completion evidence suitable for review against the approved acceptance criteria.

These requirements support a demonstrable Beta Candidate. They do not constitute a production security audit, regulatory approval, Mainnet readiness, or production deployment certification.

7.2 Recommended Development Scope

The Recommended Development Scope consists of improvements that materially strengthen usability, presentation quality, reporting clarity, and external review value but are not individually required for minimum completion.

Recommended improvements may include:

- improved Operator Workspace navigation and information hierarchy;
- clearer status, validation, and prohibited-action feedback;
- improved Investor dashboard presentation;
- enhanced charts and visual summaries;
- more usable Expense, budget, evidence, and lifecycle views;
- reporting and data export capabilities;
- higher-quality demonstration datasets;
- dedicated presentation views for external reviewers;
- improved demonstration reset and repeatability;

stronger accessibility and responsive usability;

enhanced controlled deployment and environment reliability;

expanded user guidance and demonstration documentation;

clearer presentation of Alpha, Beta Candidate, and non-production boundaries.

These improvements increase the value of the Beta Candidate by making its completed capabilities easier to understand, operate, demonstrate, and evaluate.

Recommended work must remain directly connected to the Development Objective. It must not introduce live financial activity, production operations, Corporate Setup, or Pilot Capital into the Development Round.

If available resources are insufficient to complete both Minimum and Recommended Scope, completion and verification of the Minimum Viable Development Scope take priority.

7.3 Optional Scope

Optional Scope consists of additional capabilities that may extend the usefulness or demonstration range of the Beta Candidate but are not required for Development Round success.

Optional capabilities may include:

advanced operational or Investor analytics;

AI-assisted analysis or summarization of reports;

AI-assisted identification of missing or inconsistent evidence;

expanded reporting and export formats;

enhanced mobile optimization;

additional audience-specific demonstration views;

additional demonstration scenarios based on approved Investment Models;

optional non-financial external integrations;

extended trend, comparison, or exception analysis;

additional language or localization support.

Any AI-assisted capability must remain advisory. It must not make financial approvals, replace authorized human decisions, establish the authority of evidence, or present generated conclusions as audited facts.

Optional integrations must not expand the Development Round into production banking, custody, payment execution, crypto-to-fiat conversion, KYC/KYB, Mainnet settlement, or live pilot operations.

Optional Scope Activation Rules

Optional work may be activated only when all of the following conditions are satisfied:

the Minimum Viable Development Scope remains fully funded and deliverable;

optional work will not delay mandatory completion;

optional work will not reduce the quality, security, verification, or documentation of mandatory capabilities;

the required resources and delivery capacity are available;

the optional capability contributes directly to the approved Development Objective;

applicable dependencies and risks are understood;

activation is explicitly approved through the applicable Development Round governance process;

the optional capability can be completed without changing the non-production boundaries of the Beta Candidate.

Optional work must be suspended or removed if it begins to threaten mandatory scope, acceptance criteria, funding discipline, or completion of the Beta Candidate.

Recommended and Optional Scope cannot compensate for an incomplete mandatory capability. A Beta Candidate with additional analytics, presentation features, integrations, or demonstration scenarios cannot be considered complete if the Minimum Viable Development Scope has not been achieved.

This Development Scope is the governing scope reference for the remainder of the Funding Package. Every subsequent Work Package, Deliverable, budget item, Milestone, verification requirement, and Completion Criterion must identify whether it supports Minimum, Recommended, or Optional Scope and must remain traceable to the Development Objective and target Beta Candidate.

8. Development Work Packages

Development Work Packages divide the approved Development Scope into controlled, independently manageable implementation units.

Each Work Package has a defined purpose, output, completion basis, dependency position, budget reference, and relationship to the approved Development Milestones.

Independent management does not mean that every Work Package can produce a complete Beta Candidate by itself. Work Packages may depend on one another and must operate collectively to achieve the Development Objective.

8.1 Work Package Governance

Work Package identification

Every Work Package must have:

a unique identifier;

a unique title;

a defined scope classification: Core, Recommended, or Optional;

a clearly stated purpose;

one accountable ownership assignment under the approved delivery governance;

a current status;

a reference to the relevant Development Scope.

Identifiers defined in this section must remain stable throughout planning, delivery, reporting, verification, and acceptance.

Sequencing rules

Work Packages may depend on capabilities, decisions, or outputs produced by other Work Packages.

Sequencing must:

- respect material dependencies;
- reduce integration and delivery risk;
- preserve the approved Development Objective;
- protect completion of Core Work Packages;
- allow verification evidence to be produced at the appropriate stage;
- avoid treating unfinished dependencies as completed inputs.

Sequencing may be adjusted when necessary, but it must not redefine the Beta Candidate, expand the Development Scope, or weaken applicable Acceptance Criteria.

Parallel execution is permitted where dependencies, resources, controls, and verification responsibilities remain clear.

Scope change rules

A Work Package must remain within the Development Scope approved in Section 7.

A proposed change must identify:

- the reason for the change;
- the affected scope classification;
- the impact on Deliverables;
- the impact on dependencies;
- the impact on Acceptance Criteria and Verification Evidence;
- the impact on related Milestones;
- the applicable budget effect;
- any effect on Beta Candidate completion.

No Work Package may be expanded through informal implementation decisions.

Material scope changes require formal approval through the applicable Development Round governance process. Approved changes must preserve complete traceability and, where necessary, trigger a formal revision of this Funding Package.

Work Package completion rules

A Work Package is complete only when:

- all approved Deliverables are complete;
- all Acceptance Criteria are satisfied;

the required Verification Evidence exists and is reviewable;

applicable dependencies and blocking conditions are resolved;

unresolved defects do not invalidate the intended outcome;

the result remains within the approved product and non-production boundaries;

completion has been formally recorded through the applicable review process.

Budget expenditure, engineering activity, elapsed time, code submission, or a demonstration alone does not establish completion.

A Work Package may be marked conditionally complete only where the remaining condition is explicitly documented, does not invalidate the completed output, and is accepted by the applicable governance authority. Conditional completion cannot be used to declare a related Milestone or the Beta Candidate complete when mandatory criteria remain unsatisfied.

Scope priority

Core Work Packages take priority over Recommended and Optional Work Packages.

Recommended work may proceed only while successful delivery of all Core Work Packages remains achievable.

Optional work may proceed only under the activation rules established in Section 7.3.

Recommended or Optional outputs cannot compensate for an incomplete Core Work Package.

8.2 Mandatory Work Package Template

Every Development Work Package must use the following template.

Objective

Explains why the Work Package exists and how it contributes to the Development Objective and Beta Candidate.

Scope

Defines the body of work included within the Work Package and identifies the applicable Minimum, Recommended, or Optional Development Scope.

The Scope must also make important exclusions visible where confusion with another Work Package or a non-production capability is reasonably possible.

Deliverables

Identifies the tangible, reviewable outputs produced by the Work Package.

Deliverables must be capable of being verified and linked to the related Milestone.

Dependencies

Identifies earlier Work Packages, product foundations, external conditions, approvals, or inputs required for successful completion.

A dependency must not be treated as resolved without appropriate evidence.

Acceptance Criteria

Defines the conditions that must be satisfied before the Work Package can be considered complete.

Acceptance Criteria must describe outcomes rather than activity alone.

Verification Evidence

Identifies the evidence required to demonstrate that the Deliverables exist and the Acceptance Criteria have been satisfied.

Evidence may include product behaviour, system records, tests, review records, controlled demonstrations, documentation, deployment evidence, or other approved artifacts.

Budget

References the corresponding Development Budget allocation defined in Section 10.

A Work Package budget field must identify the applicable allocation but must not independently redefine the Development Budget or duplicate detailed financial calculations.

Related Milestone

Identifies the Development Milestone primarily supported by the Work Package.

A Work Package may contribute to more than one Milestone, but one primary relationship must remain identifiable.

8.3 Work Package Portfolio

The Development Round portfolio consists of Core, Recommended, and Optional Work Packages.

Core Work Packages

Core Work Packages are mandatory for completion of the Minimum Viable Development Scope.

WP-C01 — Project Expense Platform

Objective: Establish the complete user-visible Project Expense capability required by the Beta Candidate.

Scope: Project Expense initiation, context, supported lifecycle, status visibility, and connection to the existing financial workflow and accounting foundation.

Deliverables: A complete and reviewable Project Expense product capability operating within the approved Project, workflow, budget, category, currency, and Operator boundaries.

Dependencies: Verified Stage 2 financial workflow and Project Expense accounting foundations.

Acceptance Criteria: The supported Expense lifecycle functions coherently, preserves applicable financial controls, and can be followed through the product.

Verification Evidence: Product demonstration, lifecycle records, relevant tests, and acceptance review records.

Budget: Section 10 — Project Expense Platform allocation.

Related Milestone: Milestone 1 — Expense Platform Complete.

WP-C02 — Project Expense Authorization and Operational Controls

Objective: Ensure that Project Expense actions are available only to permitted product roles and remain subject to the approved operational controls.

Scope: Authentication context, role-appropriate actions, prohibited-action handling, responsibility separation, and enforcement of relevant Project Expense boundaries.

Deliverables: A reviewable authorization and control capability covering the supported Expense workflow.

Dependencies: WP-C01 and the existing authentication and role baseline.

Acceptance Criteria: Permitted actions succeed for the appropriate role, prohibited actions are consistently rejected, and required responsibility separation remains effective.

Verification Evidence: Authorization tests, prohibited-action evidence, role-based demonstrations, and review records.

Budget: Section 10 — Authorization and Operational Controls allocation.

Related Milestone: Milestone 1 — Expense Platform Complete.

WP-C03 — Operator Workspace

Objective: Provide an authorized Operator with one coherent product experience for managing the supported operational and Project Expense workflow.

Scope: Operator access to Project context, budgets, Expenses, permitted actions, evidence, lifecycle information, and operational reporting.

Deliverables: A functional Operator Workspace supporting the approved end-to-end operational scenario.

Dependencies: WP-C01 and WP-C02.

Acceptance Criteria: An authorized Operator can complete the supported workflow without relying on disconnected administrative tools or direct database intervention.

Verification Evidence: Operator journey demonstration, product records, role validation, and acceptance review.

Budget: Section 10 — Operator Workspace allocation.

Related Milestone: Milestone 2 — Operator Workspace Complete.

WP-C04 — Evidence Management

Objective: Connect Project Expenses and operational activity to supporting evidence within a controlled and reviewable product workflow.

Scope: Evidence association, classification, status, role-appropriate review, retention, and permitted disclosure.

Deliverables: An integrated evidence workflow supporting the approved Project Expense scenario.

Dependencies: WP-C01, WP-C02, and relevant Operator Workspace capabilities.

Acceptance Criteria: Required evidence can be associated with the correct record, reviewed according to product authority, and distinguished from external legal, banking, accounting, or blockchain authority.

Verification Evidence: Evidence records, product demonstrations, validation tests, disclosure checks, and acceptance records.

Budget: Section 10 — Evidence Management allocation.

Related Milestone: Milestone 3 — Evidence Layer Complete.

WP-C05 — Investor Transparency

Objective: Provide Investors with appropriate visibility into disclosed Project operations, Expenses, evidence, reporting, and lifecycle history.

Scope: Investor-facing Project Expense information, operational progress, status semantics, evidence availability, and disclosure controls.

Deliverables: A controlled Investor transparency experience connected to the supported operational workflow.

Dependencies: WP-C01, WP-C04, and applicable disclosure rules.

Acceptance Criteria: An authorized Investor can review the permitted information while restricted, internal, or unsupported information remains protected and accurately labelled.

Verification Evidence: Investor journey demonstration, disclosure tests, role-access evidence, and acceptance review.

Budget: Section 10 — Investor Transparency allocation.

Related Milestone: Milestone 4 — Investor Transparency Complete.

WP-C06 — Operational and Investor Reporting

Objective: Present operational activity, Project Expenses, evidence status, and lifecycle information in reviewable reports.

Scope: Minimum reporting required for Operator use, Investor review, demonstration, and Development Round verification.

Deliverables: Integrated reports supporting the approved Beta Candidate workflow.

Dependencies: WP-C01, WP-C03, WP-C04, and WP-C05.

Acceptance Criteria: Reports accurately represent the supported records, preserve applicable status distinctions, and do not imply audited or production-settled results.

Verification Evidence: Report outputs, source-record comparison, role-based review, and acceptance records.

Budget: Section 10 — Reporting allocation.

Related Milestone: Milestone 4 — Investor Transparency Complete.

WP-C07 — Demonstration Environment and Scenario

Objective: Provide a controlled, repeatable environment in which the complete Beta Candidate can be demonstrated and reviewed.

Scope: Demonstration environment, approved scenario, clearly labelled demonstration data, repeatable product journey, and resulting system records.

Deliverables: A reviewable end-to-end demonstration of the Beta Candidate.

Dependencies: WP-C01 through WP-C06.

Acceptance Criteria: A reviewer can follow the approved scenario through observable product behaviour without interpreting demonstration data as live investment or pilot activity.

Verification Evidence: Deployed or controlled review environment, demonstration record, scenario evidence, and reviewer checklist.

Budget: Section 10 — Demonstration Environment allocation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

WP-C08 — Quality Assurance and Product Security

Objective: Establish that the Beta Candidate functions reliably within its approved scope and that relevant product controls have been evaluated.

Scope: Principal user journeys, regression protection, authorization behaviour, financial and evidence controls, critical-defect resolution, and Beta-appropriate product security review.

Deliverables: Verified quality and security evidence supporting Beta Candidate acceptance.

Dependencies: All product-facing Core Work Packages.

Acceptance Criteria: Required journeys and controls pass the approved verification process, and no unresolved critical defect prevents demonstration or invalidates the target workflow.

Verification Evidence: Test results, defect records, security review evidence, regression evidence, and closure review.

Budget: Section 10 — Quality Assurance and Product Security allocation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

WP-C09 — Documentation, Delivery Evidence, and Acceptance Support

Objective: Ensure that the completed Beta Candidate can be operated, reviewed, reported, and assessed against the Funding Package.

Scope: Required technical and user documentation, demonstration guidance, delivery evidence, completion records, and acceptance support.

Deliverables: A complete review package connecting delivered capabilities to Deliverables, Milestones, Verification Evidence, and Acceptance Criteria.

Dependencies: All Core Work Packages.

Acceptance Criteria: Documentation reflects the delivered product accurately, evidence is traceable, non-production boundaries remain explicit, and the completion review can be conducted without unsupported claims.

Verification Evidence: Approved documentation, traceability records, delivery report, acceptance checklist, and review decision.

Budget: Section 10 — Documentation and Delivery allocation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Recommended Work Packages

Recommended Work Packages materially improve the value of the Beta Candidate but are subordinate to Core completion.

WP-R01 — Product Experience and Accessibility Enhancements

Objective: Improve the usability, clarity, responsiveness, and accessibility of the Operator and Investor experiences.

Scope: Navigation, information hierarchy, status communication, validation feedback, responsive behaviour, and accessibility improvements beyond minimum completion.

Deliverables: Improved user-visible product experience across the supported Beta Candidate workflow.

Dependencies: Relevant Core user-facing Work Packages.

Acceptance Criteria: Approved usability improvements function consistently without changing mandatory workflow or authorization boundaries.

Verification Evidence: Usability review, responsive checks, accessibility evidence, and updated demonstrations.

Budget: Section 10 — Product Experience Enhancement allocation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

WP-R02 — Enhanced Reporting, Export, and Presentation

Objective: Improve the clarity and external review value of reporting and presentation capabilities.

Scope: Enhanced visual summaries, charts, exports, demonstration datasets, and audience-appropriate presentation views.

Deliverables: Improved reporting and presentation outputs built upon verified Core records.

Dependencies: WP-C05 and WP-C06.

Acceptance Criteria: Enhanced outputs remain consistent with source records, disclosure controls, and non-production positioning.

Verification Evidence: Report comparisons, export validation, presentation review, and acceptance records.

Budget: Section 10 — Enhanced Reporting and Presentation allocation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

WP-R03 — Demonstration Reliability and Environment Enhancements

Objective: Improve the repeatability, stability, and reviewer accessibility of the demonstration environment.

Scope: Environment reliability, demonstration reset capability, review access, operational guidance, and supporting observability.

Deliverables: A more reliable and repeatable external review environment.

Dependencies: WP-C07 and WP-C08.

Acceptance Criteria: The demonstration can be repeated consistently without weakening security, data labelling, or product boundaries.

Verification Evidence: Repeat-run demonstrations, environment checks, operational records, and reviewer validation.

Budget: Section 10 — Demonstration Reliability allocation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Optional Work Packages

Optional Work Packages are not required for Development Round completion and may be activated only under the Optional Scope Activation Rules.

WP-O01 — Advanced Analytics and AI Assistance

Objective: Explore advisory capabilities that improve interpretation of operational reports, Expenses, or evidence.

Scope: Advanced analytics, trend or exception views, and optional AI-assisted summarization or consistency checks.

Deliverables: Clearly labelled advisory outputs that do not replace authorized decisions or establish evidence authority.

Dependencies: Completed and verified Core data, evidence, reporting, and authorization capabilities.

Acceptance Criteria: Outputs are accurate within the approved use case, remain advisory, disclose applicable limitations, and do not perform financial approval or autonomous decision-making.

Verification Evidence: Evaluation results, sample outputs, limitation review, and acceptance record.

Budget: Section 10 — Optional Analytics and AI allocation, if activated.

Related Milestone: Optional extension following Milestone 5.

WP-O02 — Extended Demonstration Coverage

Objective: Extend the review value of the Beta Candidate through additional approved scenarios or audience support.

Scope: Additional demonstration scenarios, localization, extended reporting formats, or non-financial integrations consistent with the approved boundaries.

Deliverables: One or more approved extensions to the Core demonstration experience.

Dependencies: Completed Core demonstration capability and formal Optional Scope activation.

Acceptance Criteria: The extension does not alter the Development Objective, delay Core completion, introduce live financial activity, or create unsupported product claims.

Verification Evidence: Extended scenario demonstration, boundary review, and acceptance record.

Budget: Section 10 — Optional Demonstration Extension allocation, if activated.

Related Milestone: Optional extension following Milestone 5.

Cross-Work-Package Dependencies

Dependencies must be managed according to the following principles:

the Project Expense Platform and Authorization capabilities establish the controlled workflow foundation;

the Operator Workspace depends on that controlled workflow;

Evidence Management depends on the relevant Expense, authorization, and Operator context;

Investor Transparency depends on approved operational records, evidence status, and disclosure controls;

Reporting depends on verified source records and role-appropriate visibility;

the complete demonstration depends on the integrated Core product experience;

Quality Assurance and Product Security apply across all Core Work Packages;

Documentation and acceptance evidence must reflect the delivered product rather than anticipated functionality;

Recommended and Optional Work Packages remain subordinate to Core completion.

A dependency relationship does not transfer completion status. Every Work Package must satisfy its own Deliverables, Acceptance Criteria, and Verification Evidence requirements.

Traceability requirements

Every Work Package must remain traceable through the complete governance chain:

Development Objective



Beta Candidate



Development Scope



Work Package



Deliverables



Milestone



Verification Evidence



Acceptance Criteria

No Work Package may exist outside this chain.

If a proposed Work Package cannot demonstrate a direct contribution to the Development Objective and Beta Candidate, it must be excluded or processed through formal scope revision.

Budget discipline

Each Work Package must reference the corresponding allocation in Section 10 — Development Budget.

Work Package budget references must not:

- create an additional funding request;

- alter the approved Development Round amount;

- transfer resources across independent funding components;

- include Corporate Setup or Pilot Capital;

- treat expenditure as evidence of completion;

- duplicate or supersede the detailed Development Budget.

Any material budget reallocation must follow the applicable funding and scope-change governance while preserving successful completion of all Core Work Packages.

This Work Package portfolio is the governing implementation structure for the Development Round. Implementation activity must be assigned to an approved Work Package, remain within its scope, produce its Deliverables, satisfy its Acceptance Criteria, and generate the required Verification Evidence.

9. Deliverables

This section defines the official catalogue of tangible outputs to be produced by the Development Round.

A Deliverable is a completed result, not an implementation activity. It must be capable of being reviewed, demonstrated, verified, and formally accepted.

Deliverable Governance

Every Deliverable must:

- have a unique and stable identifier;

- represent a completed output;

- identify its related Work Package or Work Packages;

- identify its Development Scope classification;

- identify its primary related Milestone;

- have defined Verification Evidence;

- have defined Acceptance Criteria;

remain traceable to the Development Objective and Beta Candidate;

remain within the approved non-production boundaries.

Deliverables classified as **Minimum** are mandatory for successful completion of the Development Round.

Deliverables classified as **Recommended** or **Optional** become required only if their corresponding Work Packages are formally activated. Their absence does not prevent minimum completion unless they have been incorporated into the formally approved delivery commitment.

Completion of an activity, expenditure of allocated funds, submission of code, or passage of time does not establish Deliverable completion.

9.1 Product Deliverables

D-P01 — Completed Project Expense Workflow

Description: A complete user-visible Project Expense capability supporting the approved lifecycle within the correct Project, financial workflow, Operator, budget, category, currency, and evidence context.

Related Work Packages: WP-C01 and WP-C02.

Development Scope: Minimum.

Related Milestone: Milestone 1 — Expense Platform Complete.

Verification Evidence: End-to-end product demonstration, lifecycle records, authorization results, relevant test evidence, and completion review.

Acceptance Criteria: An authorized user can complete the supported Project Expense lifecycle; prohibited actions are rejected; applicable budget, lifecycle, and responsibility-separation controls remain effective.

D-P02 — Completed Operator Workspace

Description: A coherent Operator-facing product experience for managing the supported Project Expense, evidence, reporting, and operational workflow.

Related Work Packages: WP-C03, supported by WP-C01, WP-C02, and WP-C04.

Development Scope: Minimum.

Related Milestone: Milestone 2 — Operator Workspace Complete.

Verification Evidence: Operator journey demonstration, role-access evidence, resulting product records, and completion review.

Acceptance Criteria: An authorized Operator can follow the approved operational scenario without direct database intervention or reliance on disconnected administrative tools.

D-P03 — Completed Evidence Workflow

Description: A controlled product capability for associating, classifying, reviewing, retaining, and disclosing supporting evidence related to the approved Project Expense workflow.

Related Work Packages: WP-C04.

Development Scope: Minimum.

Related Milestone: Milestone 3 — Evidence Layer Complete.

Verification Evidence: Evidence records, association and disclosure demonstrations, validation results, and completion review.

Acceptance Criteria: Evidence is connected to the correct Expense and lifecycle context, remains accessible only to permitted roles, and is presented according to its actual authority and status.

D-P04 — Completed Investor Transparency Experience

Description: A controlled Investor-facing experience presenting permitted Project activity, Project Expense information, evidence availability, reporting, and lifecycle history.

Related Work Packages: WP-C05.

Development Scope: Minimum.

Related Milestone: Milestone 4 — Investor Transparency Complete.

Verification Evidence: Investor journey demonstration, disclosure-control results, role-access evidence, and acceptance review.

Acceptance Criteria: An authorized Investor can review the approved information while restricted or unsupported information remains protected and accurately labelled.

D-P05 — Completed Operational and Investor Reporting

Description: Reviewable reporting that connects operational activity, Project Expenses, evidence status, lifecycle information, and permitted Investor visibility.

Related Work Packages: WP-C06.

Development Scope: Minimum.

Related Milestone: Milestone 4 — Investor Transparency Complete.

Verification Evidence: Completed reports, source-record comparison, role-based review, and acceptance evidence.

Acceptance Criteria: Reports accurately reflect approved source records, preserve applicable status distinctions, and do not imply audited performance or production settlement.

D-P06 — Product Experience Enhancements

Description: Approved improvements to navigation, information hierarchy, responsive behaviour, accessibility, validation feedback, and user-visible clarity.

Related Work Packages: WP-R01.

Development Scope: Recommended; conditional upon activation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Usability review, responsive and accessibility checks, and updated product demonstration.

Acceptance Criteria: Activated enhancements function consistently and do not change mandatory workflow, authorization, or non-production boundaries.

D-P07 — Enhanced Reporting and Presentation Outputs

Description: Approved visual summaries, charts, exports, demonstration datasets, and external-review presentation capabilities beyond minimum reporting.

Related Work Packages: WP-R02.

Development Scope: Recommended; conditional upon activation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Export validation, report comparison, presentation review, and acceptance evidence.

Acceptance Criteria: Enhanced outputs remain consistent with authoritative product records, disclosure controls, and non-production positioning.

D-P08 — Advisory Analytics or AI Capability

Description: An optional advisory capability for analysis, summarization, consistency checking, or exception identification within approved operational records.

Related Work Packages: WP-O01.

Development Scope: Optional; conditional upon formal activation.

Related Milestone: Optional extension following Milestone 5.

Verification Evidence: Evaluation results, controlled sample outputs, limitation disclosures, and acceptance review.

Acceptance Criteria: The capability remains advisory, does not authorize financial actions, does not replace human judgment, and does not present generated conclusions as audited facts.

9.2 Technical Deliverables

D-T01 — Project Expense API and Authorization Capability

Description: A complete application capability through which permitted product users and interfaces can access and perform the supported Project Expense actions.

Related Work Packages: WP-C01 and WP-C02.

Development Scope: Minimum.

Related Milestone: Milestone 1 — Expense Platform Complete.

Verification Evidence: API behaviour evidence, authorization results, prohibited-action results, integration evidence, and relevant tests.

Acceptance Criteria: Supported actions are available to permitted users, prohibited actions are rejected consistently, and the capability preserves applicable database and workflow controls.

D-T02 — Integrated Project Expense and Evidence Data Flow

Description: A completed connection between Project Expense records, financial workflows, budgets, lifecycle events, evidence, reporting, and role-appropriate product views.

Related Work Packages: WP-C01, WP-C02, WP-C04, WP-C05, and WP-C06.

Development Scope: Minimum.

Related Milestone: Milestone 3 — Evidence Layer Complete.

Verification Evidence: End-to-end data-flow records, state comparison, integration tests, and review evidence.

Acceptance Criteria: Information remains connected to the correct Project and workflow context and is represented consistently across the supported Operator, evidence, reporting, and Investor experiences.

D-T03 — Role-aware Frontend Integration

Description: Completed frontend integration for the supported Operator and Investor journeys, including permitted actions, status presentation, evidence visibility, and prohibited-action feedback.

Related Work Packages: WP-C03 and WP-C05.

Development Scope: Minimum.

Related Milestone: Milestone 4 — Investor Transparency Complete.

Verification Evidence: Role-based user journeys, frontend behaviour evidence, access checks, and acceptance review.

Acceptance Criteria: Each supported role can access the appropriate experience, while unavailable or restricted functionality remains inaccessible or clearly rejected.

D-T04 — Controlled Beta Demonstration Deployment

Description: A controlled environment or equivalent review deployment containing the completed Beta Candidate and approved demonstration scenario.

Related Work Packages: WP-C07 and WP-C08.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Deployment record, environment verification, accessibility check, version reference, and end-to-end demonstration.

Acceptance Criteria: The approved Beta Candidate can be reviewed reliably in a controlled environment with clearly identified demonstration data and non-production boundaries.

9.3 Demonstration Deliverables

D-D01 — Approved Demonstration Scenario and Data

Description: A repeatable demonstration scenario and controlled dataset covering the complete approved Operator-to-Investor workflow.

Related Work Packages: WP-C07.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Scenario specification, dataset record, reset or preparation instructions, and completed scenario review.

Acceptance Criteria: The scenario covers the required workflow, produces reviewable system records, and clearly distinguishes demonstration data from live investment or pilot activity.

D-D02 — End-to-End Beta Candidate Demonstration

Description: A complete observable demonstration of the Project context, Operator workflow, Project Expense lifecycle, authorization controls, evidence, reporting, and Investor transparency.

Related Work Packages: WP-C01 through WP-C07.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Live or recorded demonstration evidence, reviewer checklist, resulting system records, and acceptance review.

Acceptance Criteria: A reviewer can follow the complete approved scenario through observable product behaviour without relying on presentation claims alone.

D-D03 — Demonstration Review Package

Description: A reviewer-oriented package containing access guidance, scenario instructions, product boundaries, expected outcomes, and references to supporting evidence.

Related Work Packages: WP-C07 and WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Completed package, link and access validation, reviewer walkthrough, and approval record.

Acceptance Criteria: An external reviewer can understand how to access, operate, and evaluate the demonstration without interpreting it as a production or live-investment environment.

D-D04 — Enhanced Demonstration Reliability

Description: Additional reliability, reset, reviewer-access, observability, or repeatability capabilities beyond the minimum demonstration requirement.

Related Work Packages: WP-R03.

Development Scope: Recommended; conditional upon activation.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Repeat-run results, environment checks, review-access validation, and acceptance record.

Acceptance Criteria: The enhanced environment supports repeatable external review without weakening security, data labelling, or product boundaries.

D-D05 — Extended Demonstration Coverage

Description: One or more approved additional scenarios, localizations, reporting formats, or non-financial demonstration integrations.

Related Work Packages: WP-O02.

Development Scope: Optional; conditional upon formal activation.

Related Milestone: Optional extension following Milestone 5.

Verification Evidence: Extended demonstration, boundary review, scenario records, and acceptance evidence.

Acceptance Criteria: The extension remains within the approved product boundaries and does not delay or redefine Core completion.

9.4 Security and QA Deliverables

D-Q01 — Functional and Regression Verification Results

Description: Completed verification results covering principal user journeys, Project Expense behaviour, evidence handling, reporting, role access, and relevant existing functionality.

Related Work Packages: WP-C08.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Test results, regression results, test-environment information, defect records, and closure status.

Acceptance Criteria: Required verification passes, relevant regression protection is demonstrated, and no unresolved critical defect prevents the intended Beta Candidate workflow.

D-Q02 — Authorization and Financial-Control Verification

Description: Completed verification of prohibited actions, responsibility separation, lifecycle controls, Project and workflow boundaries, budget capacity, reservations, and overspending protection.

Related Work Packages: WP-C02 and WP-C08.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Authorization test results, negative-path results, financial-control tests, and review records.

Acceptance Criteria: Applicable controls operate consistently across the supported workflow and known exceptions are documented and accepted.

D-Q03 — Product Security Validation Record

Description: A completed Beta-appropriate review of relevant authentication, authorization, data exposure, evidence access, configuration, and demonstration-environment security conditions.

Related Work Packages: WP-C08.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Security review record, identified findings, remediation status, accepted limitations, and closure decision.

Acceptance Criteria: No unresolved critical security finding invalidates the Beta Candidate demonstration or approved product boundaries.

This Deliverable does not constitute an external security audit, regulatory certification, or production-readiness approval.

D-Q04 — Deployment Verification Record

Description: Completed evidence that the controlled review environment contains the intended Beta Candidate version and supports the approved demonstration.

Related Work Packages: WP-C07 and WP-C08.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Version reference, deployment checks, environment status, access verification, and demonstration result.

Acceptance Criteria: The reviewed environment is identifiable, accessible as intended, and consistent with the version submitted for acceptance.

9.5 Documentation Deliverables

D-DO01 — Updated Product and Technical Documentation

Description: Documentation accurately describing the completed Beta Candidate, its capabilities, architecture, technical boundaries, verification approach, and known limitations.

Related Work Packages: WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Documentation review, repository references, consistency review, and approval record.

Acceptance Criteria: Documentation matches delivered behaviour, distinguishes implemented and planned capabilities, and preserves all non-production boundaries.

D-DO02 — Operator and Reviewer Guidance

Description: Practical guidance for operating and reviewing the supported Operator, evidence, reporting, Investor, and demonstration workflows.

Related Work Packages: WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Completed guidance, walkthrough results, and reviewer feedback.

Acceptance Criteria: An intended user or reviewer can follow the documented workflow without relying on undocumented implementation knowledge.

D-DO03 — Release and Known-Limitations Record

Description: A controlled record identifying the delivered version, included capabilities, excluded capabilities, accepted limitations, and non-production status.

Related Work Packages: WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Version record, scope comparison, limitation review, and approval.

Acceptance Criteria: The record accurately represents the accepted Beta Candidate and does not overstate production, regulatory, Mainnet, Corporate Setup, or pilot readiness.

D-DO04 — Deliverable Traceability Record

Description: A complete mapping between the Development Objective, Beta Candidate, Development Scope, Work Packages, Deliverables, Milestones, Verification Evidence, and Acceptance Criteria.

Related Work Packages: WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Completed traceability matrix, consistency check, exception record, and approval.

Acceptance Criteria: Every mandatory Deliverable has an unbroken traceability chain and no accepted implementation output exists outside the approved governance structure.

9.6 Grant Reporting Deliverables

D-G01 — Development Milestone Reports

Description: Reviewable reports documenting the status, completed Deliverables, Verification Evidence, exceptions, and acceptance position for each funded Development Milestone.

Related Work Packages: WP-C09 and the Work Packages supporting each Milestone.

Development Scope: Minimum.

Related Milestone: Applicable to Milestones 1–5.

Verification Evidence: Submitted reports, referenced Deliverables, evidence links, and review decisions.

Acceptance Criteria: Each report accurately represents achieved results, distinguishes incomplete work, and remains traceable to the approved Funding Package.

D-G02 — Verification Evidence Package

Description: An organized package containing the approved evidence required to verify completed Deliverables and Milestones.

Related Work Packages: WP-C08 and WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Evidence index, test and review records, demonstration evidence, deployment references, documentation references, and integrity review.

Acceptance Criteria: Evidence is complete, accessible to the intended reviewer, correctly attributed, and sufficient to evaluate the applicable Acceptance Criteria.

D-G03 — Development Round Completion Report

Description: A final report explaining what was delivered, what was verified, what remains excluded, how funds were used at the approved reporting level, and whether the Development Objective was achieved.

Related Work Packages: WP-C09, supported by all Core Work Packages.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Final report, Deliverable status register, evidence references, acceptance decisions, and approved exceptions.

Acceptance Criteria: The report provides a factual and traceable account of Development Round completion without presenting planned, Recommended, Optional, or production capabilities as completed.

D-G04 — External Review and Demonstration Package

Description: A funder-adaptable package containing the Beta Candidate overview, demonstration access, reviewer guidance, selected evidence, milestone status, and non-production boundaries.

Related Work Packages: WP-C07 and WP-C09.

Development Scope: Minimum.

Related Milestone: Milestone 5 — Beta Candidate Complete.

Verification Evidence: Completed package, access validation, content review, and funder-adaptation checklist.

Acceptance Criteria: The package allows a grant programme, accelerator, investor, venture studio, or strategic partner to review the funded outcome without requiring unsupported claims or unrestricted repository access.

Deliverable Traceability Rule

Every Deliverable must remain within the following traceability chain:

Development Objective

↓

Beta Candidate

↓

Development Scope

↓

Work Package

↓

Deliverable

↓

Milestone

↓

Verification Evidence

↓

Acceptance Criteria

No Deliverable may exist outside this chain.

Any proposed output that cannot be traced to an approved Work Package and Development Scope classification must be excluded or processed through formal scope revision.

This Deliverable catalogue is the governing output register for the Development Round. Successful completion requires all Minimum Deliverables to be complete, verified, accepted, and accurately reported. Recommended and Optional Deliverables are governed by their activation status and cannot substitute for an incomplete Minimum Deliverable.

10. Development Budget

The Development Budget is the official financial governance model for completing the **Pilot Operations & Investor Evidence Beta Candidate**.

It allocates the approved funding request across the Development Work Package portfolio, protects the Minimum Viable Development Scope, and establishes the controls required for traceable expenditure, milestone reporting, and external review.

10.1 Total Development Budget

The approved Development Round budget is:

USD 40,000

The full amount is designated exclusively for the approved Development Round and its product-development objective.

The Development Budget does not finance:

Corporate Setup;

establishment of AgriPartners OÜ;

legal, tax, accounting, or regulatory readiness;

Operational Readiness activities outside product completion;

Feedlot Pilot Capital;

Hissar Pilot Capital;

livestock acquisition;

construction or physical infrastructure;

agricultural working capital;

production banking or payment infrastructure;

production custody or settlement;

NEAR Mainnet deployment;

production operations.

These components remain separately governed under Funding Strategy v1.

The USD 40,000 Development Budget must not be interpreted as the complete capital requirement for Corporate Setup, Operational Readiness, or either agricultural Pilot Round.

10.2 Budget Allocation by Work Package

The Development Budget gives first priority to the Core Work Packages required to complete the Minimum Viable Development Scope.

Allocation ID	Work Package	Scope	Related Deliverables	Related Milestone	Allocation
BA-01	WP-C01 — Project Expense Platform	Minimum	D-P01, D-T01, D-T02	Milestone 1	\$6,500
BA-02	WP-C02 — Project Expense Authorization and Operational Controls	Minimum	D-P01, D-T01, D-Q02	Milestone 1	\$4,500
BA-03	WP-C03 — Operator Workspace	Minimum	D-P02, D-T03	Milestone 2	\$6,500
BA-04	WP-C04 — Evidence Management	Minimum	D-P03, D-T02	Milestone 3	\$4,000
BA-05	WP-C05 — Investor Transparency	Minimum	D-P04, D-T03	Milestone 4	\$4,000
BA-06	WP-C06 — Operational and Investor Reporting	Minimum	D-P05	Milestone 4	\$2,500

Allocation ID	Work Package	Scope	Related Deliverables	Related Milestone	Allocation
BA-07	WP-C07 — Demonstration Environment and Scenario	Minimum	D-T04, D-D01, D-D02, D-D03	Milestone 5	\$2,500
BA-08	WP-C08 — Quality Assurance and Product Security	Minimum	D-Q01, D-Q02, D-Q03, D-Q04	Milestone 5	\$4,500
BA-09	WP-C09 — Documentation, Delivery Evidence, and Acceptance Support	Minimum	D-DO01–D-DO04, D-G01–D-G04	Milestone 5	\$2,000
BA-10	Controlled Contingency	Minimum-scope protection	Activated only against approved Core requirements	Applicable Core Milestone	\$3,000
	Total Development Budget				\$40,000

The baseline Development Budget assigns no guaranteed funding to Recommended or Optional Work Packages.

Work Package group	Baseline allocation	Activation basis
WP-R01–WP-R03 — Recommended Work Packages	\$0	Verified savings, approved contingency release, or additional eligible funding after Core completion remains protected
WP-O01–WP-O02 — Optional Work Packages	\$0	Additional funding or formally approved surplus after all Core obligations remain fully funded

A zero baseline allocation does not remove a Recommended or Optional Work Package from the approved portfolio. It means that its activation is conditional and cannot displace mandatory delivery.

10.3 Internal Cost Categories

Internal cost categories provide a second financial view of the same USD 40,000 budget. They support accounting, procurement, grant reporting, and management control.

They do not create additional funding and do not redefine the Work Package portfolio.

Cost Category	Planning Purpose	Allocation
Backend and API Engineering	Product Expense capability, authorization, services, and supported backend integration	\$9,000
Frontend and Product Experience	Operator Workspace, Investor Transparency, role-aware interfaces, and minimum usability	\$8,000
Workflow and Data Integration	Connection of Expenses, budgets, lifecycle events, evidence, reporting, and product views	\$5,000
Quality Assurance and Regression Verification	Functional, integration, regression, negative-path, and controlled workflow verification	\$5,000
Product Security Validation	Authentication, authorization, data exposure, evidence access, and Beta-level security review	\$2,500
Documentation and Grant Reporting	Product documentation, user guidance, traceability, milestone reporting, and completion reporting	\$2,000
Demonstration Environment and Data	Controlled environment, demonstration scenario, review data, and demonstration evidence	\$2,500
External Product Specialists	Approved specialist support for product, security, QA, accessibility, or demonstration needs	\$2,000
Development Infrastructure	Eligible hosting, testing, tooling, and controlled review-environment costs	\$1,000
Controlled Contingency	Protection of mandatory Development Scope against approved uncertainty	\$3,000

Cost Category	Planning Purpose	Allocation
Total		\$40,000

Cost categories and Work Package allocations are two views of the same Development Budget. Expenditure must be recorded against both:

one approved Work Package allocation;

one approved internal cost category.

External Product Specialists do not include Corporate Setup, general legal services, company accounting, banking setup, pilot consultants, livestock specialists, construction services, or agricultural operations.

10.4 Contingency Allocation

The approved Development Budget includes a controlled contingency of:

USD 3,000 — 7.5% of the total Development Budget

Contingency exists to protect completion of the Minimum Viable Development Scope against reasonable development uncertainty.

Permitted contingency uses may include:

an underestimated Core Work Package requirement;

resolution of an unexpected integration issue;

additional mandatory QA or security work;

an essential demonstration-environment requirement;

an external specialist required to complete or verify mandatory scope;

an approved cost increase affecting a Core Deliverable.

Contingency is not unrestricted spending.

It must not be used for:

unapproved scope expansion;

Recommended or Optional work while Core completion remains uncertain;

Corporate Setup;

legal or accounting readiness;

Pilot Capital;

physical assets or agricultural operations;

unrelated business expenses;

undocumented cost overruns.

Every contingency release requires:

a documented reason;

identification of the affected Work Package;

identification of the protected Deliverable or Milestone;

confirmation that the expenditure remains within approved Development Scope;

formal approval by the applicable Development Round governance authority;

inclusion in the next financial and milestone report.

Unused contingency remains unspent, is returned, retained subject to the funding agreement, or reallocated only through an approved decision consistent with the funder's rules.

10.5 Funding Assumptions

The Development Round may be adapted to different funding mechanisms without changing its Development Objective, Development Scope, or Beta Candidate.

Single-Tranche Funding

Under a single-tranche model, the approved USD 40,000 is made available at or before commencement.

This model provides the clearest protection against incomplete funding and allows the complete Core portfolio to be managed as one funded commitment.

Receipt of the full tranche does not remove Work Package controls, reporting duties, contingency restrictions, or Deliverable-based completion requirements.

Multi-Tranche Funding

Under a multi-tranche model, funding is released against agreed Milestones or other approved conditions.

A multi-tranche structure is acceptable only when:

the full Development Round is legally or contractually committed;

tranche conditions are clear and objectively reviewable;

the release structure supports the dependency sequence;

early tranches are sufficient for the activities they authorize;

later funding is not dependent on unrelated discretionary events;

no completed tranche creates an unfunded obligation to finish the Beta Candidate.

Milestone acceptance and tranche release remain separate decisions unless the funding agreement explicitly combines them.

Delayed Funding

If committed funding is delayed, AgriPartners is not required to begin or continue unfunded work.

The delivery plan, commencement conditions, and reporting schedule may be adjusted to reflect the delay. A funding delay does not reduce the approved Scope or redefine an incomplete Deliverable as complete.

Controlled Budget Release

A funder or approved governance authority may release budget by Work Package, Milestone, cost category, or controlled spending period.

Controlled release must preserve:

complete funding of mandatory scope;

Work Package dependencies;

traceability;

adequate contingency protection;

the ability to complete the Beta Candidate.

Partial-Funding Restrictions

AgriPartners must not commence the full Development Round on the assumption that an uncommitted funding gap will later be filled.

Funding below USD 40,000 may be accepted only if one of the following applies:

the remaining amount is legally or contractually committed;

a revised, independently complete funding phase is formally approved;

no expenditure begins until the complete financing plan is secured.

Partial funding must not produce a situation in which earlier funds are consumed but the Beta Candidate cannot be completed because the remaining capital was never secured.

A smaller grant may support a separately approved and independently valuable preliminary component only if:

its outcome is useful even without immediate follow-on funding;

it does not create an obligation to deliver the complete Beta Candidate;

its scope and claims are clearly separated from the USD 40,000 Development Round;

the approved Funding Package is formally adapted for that funder.

10.6 Budget Control Principles

The following financial governance principles are mandatory.

Approved-scope expenditure only

Every expenditure must support an approved Work Package and Deliverable within the Development Scope.

Dual classification

Every expenditure must be classified against:

a Work Package allocation;

an internal cost category.

Deliverable linkage

Spending must remain linked to a tangible Deliverable. General activity without a Deliverable relationship is not an approved use of funds.

Minimum Scope protection

Core Work Packages and Minimum Deliverables have financial priority. Recommended or Optional work cannot reduce the resources required for mandatory completion.

Segregation of funding components

Development funds must remain separate from Corporate Setup, Operational Readiness, Feedlot Pilot Capital, Hissar Pilot Capital, and production operations.

Evidence and recordkeeping

Expenditure must be supported by appropriate financial records required by the funding agreement and internal governance. On-chain records alone do not establish an authoritative expense or fiat payment.

No expenditure-based completion

Spending the allocated amount does not prove that a Work Package, Deliverable, Milestone, or Development Round has been completed.

Funder eligibility

If a funder's eligibility rules prohibit a planned cost, that cost must be removed, replaced with an eligible cost, or financed separately. It must not be misclassified.

Financial transparency

Approved allocations, actual expenditure, commitments, variances, contingency use, and reallocations must remain reviewable at the reporting level required by the funder and Development Round governance.

No cross-subsidisation

No Development Budget allocation may subsidise Corporate Setup, either Pilot Round, production operations, or another independent funding component.

10.7 Budget Reallocation Rules

Budget reallocation is permitted only when it supports completion of the approved Beta Candidate and preserves the Minimum Viable Development Scope.

A proposed reallocation must identify:

the source allocation;

the destination allocation;

the amount;

the reason;

the affected Work Packages;

the affected Deliverables and Milestones;

the effect on dependencies;

the effect on remaining contingency;

confirmation of funder eligibility.

Reallocation requires formal approval when it:

moves funding between Work Packages;

uses contingency;

activates Recommended or Optional work;

changes an externally approved budget category;

exceeds a variance threshold established by the funding agreement;

could affect a mandatory Deliverable or Milestone.

Reallocation must not:

reduce a Core Work Package below the amount reasonably required for completion;

conceal an overrun;

finance activity outside the Development Scope;

transfer funds to Corporate Setup or Pilot Capital;

weaken QA, security, documentation, or verification requirements;

redefine an incomplete Deliverable as complete;

increase the total Development Budget without separate funding approval.

Verified savings may be reallocated in the following priority order:

completion risks within the originating Core Work Package;

other mandatory Core Work Packages;

restoration or strengthening of contingency;

formally activated Recommended Work Packages;

formally activated Optional Work Packages.

Any approved reallocation must be recorded in the budget register and reflected in subsequent financial and milestone reporting.

Financial Traceability Rule

Every Development Budget allocation must remain within the following traceability chain:


Development Objective

↓

Beta Candidate

↓

Development Scope

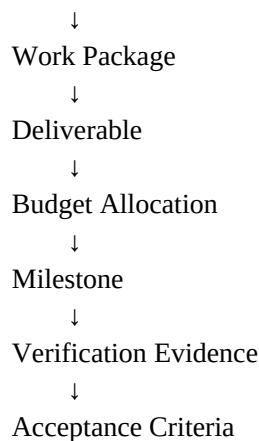

No allocation, commitment, expenditure, contingency release, or reallocation may exist outside this chain.

This Development Budget is the governing financial framework for the Development Round. It ensures that every dollar of the approved USD 40,000 remains directed toward completion of the Beta Candidate, protected from unrelated use, traceable to a tangible output, and reviewable by the applicable funder and governance authority.

11. Use of Funds

This section defines the expenditure that may be financed from the approved **USD 40,000 Development Budget**.

Use of Funds establishes cost eligibility. It does not establish implementation priority, guarantee reimbursement, authorize expenditure automatically, or replace the allocation and approval controls established in Section 10.

An expenditure is eligible only when it contributes directly to the Development Objective and the Pilot Operations & Investor Evidence Beta Candidate.

11.1 Eligible Product Development Costs

Development Round funds may finance reasonable and necessary product-development costs that:

contribute directly to the approved Development Objective;

support completion of the Beta Candidate;

remain within the approved Development Scope;

belong to an approved Work Package;

support one or more approved Deliverables;

correspond to an approved internal cost category;

occur within the eligible funding period;

comply with applicable funder rules;

are supported by appropriate financial and delivery records.

Eligibility does not imply automatic approval.

A cost may be generally eligible but still require:

Work Package owner approval;

procurement approval;

contingency approval;

budget-reallocation approval;

funder pre-approval;

confirmation of cost reasonableness;

confirmation that the relevant Deliverable remains necessary and achievable.

An expenditure is not eligible solely because it is useful, technically interesting, or beneficial to AgriPartners generally. Its relationship to the Development Round must be direct, documented, and reviewable.

Where a funder applies stricter eligibility rules than this Funding Package, the funder's rules control the corresponding funding agreement. A cost permitted by a funder is not automatically eligible internally if it falls outside the Development Objective, Development Scope, or approved Work Package portfolio.

11.2 Engineering and Product Costs

Eligible engineering and product expenditure may include the personnel, contractor, specialist, software, and directly related service costs required to produce the approved product Deliverables.

Eligible categories may include:

backend engineering;

frontend engineering;

Project Expense product capability;

Project Expense API and Authorization;

workflow and product integration;

database integration;

budget, lifecycle, and evidence integration;

role-aware Operator functionality;

role-aware Investor functionality;

reporting functionality;

user-interface and product-experience work;

product accessibility improvements where approved;

technical integration required for the controlled demonstration;

correction of defects that prevent completion or acceptance;

approved code review and integration support.

Engineering expenditure must remain connected to an approved Work Package and Deliverable.

Compensation may be eligible where:

- the person or provider performs approved Development Round work;
- the rate and engagement terms are reasonable and documented;
- the funded effort is attributable to the relevant Work Package;
- time, output, invoice, contract, or equivalent evidence is maintained as required;
- no duplicate funding or charging occurs.

Engineering and product expenditure does not become eligible merely because it affects the repository. Maintenance, experimentation, refactoring, or platform changes must have a documented contribution to an approved Deliverable.

11.3 Infrastructure and Deployment Costs

Eligible infrastructure and deployment expenditure may include services required to build, test, verify, host, and demonstrate the Beta Candidate in a controlled environment.

Eligible categories may include:

- development hosting;
- controlled review or demonstration hosting;
- test databases;
- disposable verification environments;
- development and testing services;
- deployment environments;
- domain, certificate, or access services required for the approved demonstration;
- development tooling;
- repository and delivery tooling where separately chargeable;
- approved observability, logging, or monitoring supporting Beta Candidate verification;
- backup or storage required for Development Round evidence;
- approved third-party services required by a Core Deliverable.

Infrastructure must be:

- proportionate to the Beta Candidate;
- attributable to the eligible Development Round period;
- connected to an approved Work Package;
- documented through provider records or equivalent evidence;
- limited to the capacity reasonably required for development, verification, and controlled demonstration.

Where a subscription or service extends beyond the eligible funding period, only the eligible and properly attributable portion may be charged unless the applicable funder explicitly permits another treatment.

Infrastructure financed by the Development Budget supports development and demonstration. It does not establish production infrastructure, production certification, or Operational Readiness.

11.4 QA and Security Costs

Eligible QA and security expenditure may include costs required to verify that the Beta Candidate operates consistently within its approved scope and boundaries.

Eligible categories may include:

functional testing;

integration testing;

regression verification;

negative-path and prohibited-action testing;

role and authorization verification;

Project Expense lifecycle verification;

budget and overspending-control verification;

evidence-access and disclosure verification;

controlled database and migration verification;

demonstration-environment verification;

deployment verification;

defect assessment and closure validation;

product-level security review;

authentication and authorization review;

data-exposure review;

dependency or configuration review where relevant;

specialist QA or security support;

approved testing tools and services.

QA and security costs are eligible when they support a defined Deliverable, Verification Evidence requirement, or Acceptance Criterion.

Completed testing activity does not by itself establish acceptance. The resulting verification records, findings, remediation status, and applicable limitations must remain reviewable.

These costs support Beta Candidate quality and product-level security validation. They do not imply an external security audit, regulatory certification, Mainnet certification, or production-readiness approval.

11.5 Documentation and Delivery Costs

Eligible documentation and delivery expenditure may include work required to operate, understand, demonstrate, verify, report, and accept the completed Beta Candidate.

Eligible categories may include:

technical documentation;

product documentation;

architecture updates required by delivered behaviour;

API or integration documentation;

Operator guidance;

Investor or reviewer guidance;

demonstration instructions;

controlled environment guidance;

release and known-limitations documentation;

Deliverable records;

traceability documentation;

milestone reports;

verification evidence indexing;

completion reporting;

grant-reporting materials;

external review package preparation;

approved diagrams, screenshots, or demonstration-support materials;

documentation review and consistency validation.

Documentation expenditure must describe or support delivered Development Round outcomes. It must not present planned, Recommended, Optional, production, Corporate Setup, or pilot capabilities as completed unless those capabilities have been separately approved and verified.

Grant adaptation work may be eligible where it is directly required to report or demonstrate the funded Development Round. General fundraising, unrelated marketing, and broader corporate communications are governed separately and do not become eligible merely because a funder may review them.

11.6 External Specialist Costs

External specialists may be funded where their work is directly required to complete, verify, improve, or accept an approved Development Round Deliverable.

Eligible specialist support may include:

product review;

backend or frontend specialist support;

database or workflow review;

QA review;

product-level security review;

authorization review;

accessibility review;

UX and usability review;

reporting review;

controlled deployment review;

demonstration review;

documentation and technical-writing support;

grant-delivery or evidence-reporting support directly related to the funded outcome.

External specialist expenditure must:

belong to an approved Work Package;

support one or more identified Deliverables;

have a documented scope of services;

use reasonable and reviewable commercial terms;

comply with applicable procurement and conflict-of-interest requirements;

produce an identifiable output or review record;

remain within the approved Development Scope;

comply with the funder's eligibility requirements.

Engaging an external specialist does not transfer Work Package accountability or acceptance authority. AgriPartners remains responsible for confirming that the specialist's output satisfies the applicable Deliverable and governance requirements.

A specialist cost that primarily supports another funding component must be assigned to that component rather than charged to the Development Budget.

Eligibility Principles

An expenditure is eligible under the Development Round only if all of the following conditions are satisfied:

It supports the Development Objective.

It contributes directly to the Beta Candidate.

It remains within the approved Development Scope.

It belongs to an approved Work Package.

It supports one or more approved Deliverables.

It corresponds to an approved Development Budget category.

It is reasonable, necessary, and properly attributable.

It is supported by appropriate financial and delivery evidence.

It complies with the applicable funding agreement and funder rules.

It preserves the Development Round's product-only and non-production boundaries.

Failure to satisfy any one of these conditions makes the expenditure ineligible under the Development Round unless a formal Funding Package revision and any required funder approval are completed before the expenditure is committed.

Uncertainty must be resolved before commitment. A cost must not be charged first and justified retrospectively where prior eligibility or approval was required.

Relationship to Section 12

This section defines eligible Development Round expenditure only.

The authoritative negative boundary is defined separately in:

Section 12 — Excluded Costs

An expenditure must satisfy Section 11 and must not fall within any exclusion established by Section 12.

The distinction is absolute:

Section 11 establishes what may qualify for Development Round funding;

Section 12 establishes what must not be financed by the Development Budget.

A cost cannot become eligible through relabelling, allocation transfer, contingency use, or Work Package reassignment if its underlying purpose falls outside the Development Round.

Use-of-Funds Traceability Rule

Every eligible expenditure must remain within the following traceability chain:

Development Objective

↓

Beta Candidate

↓


Development Scope

↓

Work Package

↓

Deliverable



No eligible expenditure may exist outside this chain.

For financial reporting, each expenditure must also remain traceable to:

the applicable Work Package allocation;

the applicable internal cost category;

the supporting financial record;

the relevant approval;

any applicable contingency or reallocation decision.

This Use of Funds section is the authoritative definition of eligible Development Round expenditure. It ensures that approved funds are used only for costs that contribute directly to producing, verifying, documenting, demonstrating, and accepting the Pilot Operations & Investor Evidence Beta Candidate.

12. Excluded Costs

This section defines the authoritative negative financial boundary of the **USD 40,000 Development Budget**.

An Excluded Cost must never be financed from the Development Budget because its principal purpose belongs to another funding component, governance process, or project phase.

Exclusion is determined by the underlying purpose of the expenditure, not by its description, supplier, invoice wording, accounting category, or internal label.

12.1 Corporate Setup Costs

All costs associated with establishing, maintaining, or administering AgriPartners as a legal entity are excluded from the Development Budget.

Excluded Corporate Setup costs include:

e-Residency applications;

AgriPartners OÜ incorporation;

Estonian company registration;

legal address services;

contact-person services;

registration fees;

certified corporate documents;

notarisation, apostille, translation, or administrative formalities;

company secretarial services;
corporate administration;
shareholder or founder documentation;
corporate bank-account preparation;
incorporation-related travel or representation;
initial corporate subscriptions or statutory fees.

These costs belong exclusively to the separate **Corporate Setup funding component**.

Corporate Setup may be included within a broader external Readiness funding request where permitted by the funder. It must nevertheless remain separately identified and accounted for internally and must not be charged to the USD 40,000 Development Budget.

12.2 Legal and Accounting Readiness

Legal, tax, accounting, and compliance-readiness costs are excluded from the Development Budget when their principal purpose is to establish or prepare the company, investment structure, contractual model, or live operations.

Excluded costs include:

corporate legal structuring;
investment or securities legal advice;
jurisdictional legal opinions;
regulatory classification;
tax structuring and tax advice;
accounting-system establishment;
bookkeeping setup;
statutory accounting;
audit preparation;
corporate compliance preparation;
investment documentation;
subscription or participation agreements;
Operator or Farmer contracts;
supplier or service-provider contracts;
data-protection legal advice;
terms of service or privacy-policy legal drafting;

contractual negotiation;

legal due diligence;

corporate governance documentation;

Operational Readiness legal review.

These costs belong to **Corporate Setup**, **Operational Readiness**, or another separately approved legal and compliance budget.

Product and technical documentation eligible under Section 11 must not be used as a substitute for legally reviewed corporate, investment, or operational documentation.

12.3 Banking, Payment and Compliance Infrastructure

Costs required to establish or operate production financial infrastructure are excluded from the Development Budget.

Excluded costs include:

bank-account onboarding;

payment-institution onboarding;

merchant or payment-processing setup;

cryptoasset service-provider onboarding;

crypto-to-fiat provider integration for live operations;

production payment rails;

production treasury infrastructure;

custody arrangements;

settlement-provider services;

production reconciliation services;

AML provider onboarding;

KYC or KYB services;

sanctions-screening services;

transaction-monitoring services;

source-of-funds or source-of-wealth verification;

production compliance systems;

payment reserves, deposits, or minimum balances;

financial-provider legal or compliance fees.

These costs belong to Corporate Setup, Operational Readiness, production financial infrastructure, or another separately approved funding component.

The Development Round finances the Beta Candidate product. It does not finance the operational financial infrastructure required to receive, convert, hold, transfer, reconcile, or settle live funds.

12.4 Feedlot Pilot Capital

All capital required to establish, finance, operate, or complete the real Feedlot pilot is excluded from the Development Budget.

Excluded Feedlot costs include:

livestock acquisition;

feed and nutritional inputs;

veterinary services and medicines;

agricultural labour;

transport and logistics;

farm equipment;

machinery;

livestock facilities;

construction or renovation;

utilities;

insurance;

maintenance;

Operator expenses;

supplier payments;

permits and operational approvals;

working capital;

contingency for agricultural operations;

sale, repayment, reconciliation, or settlement expenses.

These costs belong exclusively to the separately governed **Feedlot Pilot Round**.

Demonstration data or product workflows based on the Feedlot model do not make real Feedlot expenses eligible under the Development Budget.

12.5 Hissar Pilot Capital

All capital required to establish, finance, operate, or complete the real Hissar pilot is excluded from the Development Budget.

Excluded Hissar costs include:

breeding-stock acquisition;

sheep acquisition;

feed and nutritional inputs;

breeding and husbandry costs;

veterinary services and medicines;

agricultural labour;

transport;

facilities;

equipment;

utilities;

insurance;

maintenance;

Operator expenses;

supplier payments;

working capital;

offspring-management costs;

sale, repayment, reconciliation, or settlement expenses.

These costs belong exclusively to the separately governed **Hissar Pilot Round**.

The Hissar Pilot has its own capital requirement, approval conditions, operational risks, reporting duties, and governance. It cannot be financed through the Development Budget or through funds allocated to the Feedlot Pilot.

12.6 Construction and Physical Assets

The Development Budget must not finance the acquisition, construction, improvement, or ownership of physical agricultural or corporate assets.

Excluded physical costs include:

buildings;

livestock shelters;

barns;

Feedlot facilities;

offices;

land purchase or lease deposits;

land development;

fencing;

roads or access improvements;

water systems;

power systems;

storage facilities;

machinery;

agricultural equipment;

vehicles;

trailers;

physical security systems;

permanent infrastructure improvements;

construction materials;

construction labour;

facility renovation or maintenance.

This exclusion applies regardless of whether the asset would support the Feedlot Pilot, Hissar Pilot, company operations, or a later commercial phase.

Physical assets must be financed through the applicable Pilot Capital, asset-financing arrangement, strategic partnership, equipment programme, or other separately approved funding component.

12.7 Animals and Agricultural Operations

Every cost whose principal purpose is to conduct real agricultural production is excluded from the Development Budget.

Excluded operational costs include:

animals;

livestock;

breeding stock;

feed;

supplements;

veterinary care;

medicines and vaccines;
agricultural labour;
farm management;
utilities;
water;
electricity;
fuel;
insurance;
transport;
maintenance;
cleaning;
waste management;
animal identification;
agricultural monitoring equipment;
production supplies;
farm rent;
Operator working capital;
mortality losses;
emergency animal care;
real-pilot contingency;
sale and distribution activity.

These costs belong to the relevant Feedlot, Hissar, or future Pilot funding component.

A cost remains operational even if the platform records, reports, or displays it. Product visibility does not change the funding responsibility for the underlying real-world expense.

12.8 Production Financial Operations

The Development Budget must not finance live financial activity or obligations arising from real investment or commercial operations.

Excluded costs include:

live Investor capital;
Investor deposits;

Investor refunds;
Investor payouts;
profit distributions;
guaranteed returns;
repayment obligations;
production treasury balances;
liquidity reserves;
payment execution;
operational settlement;
live reconciliation;
foreign-exchange transactions;
cryptoasset purchases or conversions;
payment-provider balances;
bank transfer fees for live operations;
financial guarantees;
collateral;
debt service;
commercial transaction losses;
coverage of pilot operating deficits.

The Development Round may demonstrate how such activities could be represented within controlled product records. It must not finance or execute the underlying live financial activity.

No demonstration record, Testnet transaction, accounting projection, or product status creates an obligation to make a real payment from the Development Budget.

12.9 Mainnet, Custody and Settlement

The Development Budget must remain within controlled, non-production product boundaries.

Excluded costs include:

NEAR Mainnet deployment;
production smart-contract deployment;
production smart-contract operation;
Mainnet transaction reserves;

production wallets;

production signing infrastructure;

production private-key management;

production custody;

regulated cryptoasset services;

production stablecoin settlement;

production fiat settlement;

production payout automation;

audited custody infrastructure;

live blockchain-based investment activity;

smart-contract security certification intended for production activation;

regulated financial operations.

Controlled Testnet or development-environment activity may qualify only where it satisfies Section 11 and supports an approved Beta Candidate Deliverable. It must not be presented as Mainnet, custody, production settlement, or regulatory readiness.

Mainnet, custody, and production settlement require separate technical, security, legal, financial, compliance, and governance approval.

Exclusion Principles

A cost is excluded whenever its principal purpose belongs to:

Corporate Setup;

legal or accounting readiness;

Operational Readiness;

Feedlot Pilot Capital;

Hissar Pilot Capital;

physical asset acquisition;

agricultural operations;

production financial infrastructure;

production financial operations;

Mainnet, custody, or settlement;

another independent funding component or later project phase.

The following general costs are also excluded where they do not directly satisfy Section 11:

general corporate overhead;
unrelated salaries or contractor work;
fundraising commissions;
investor-introduction fees;
unrelated marketing or public relations;
founder or shareholder distributions;
repayment of existing debt;
fines, penalties, or late-payment charges;
recoverable taxes where prohibited by the applicable funder;
costs incurred outside the eligible funding period;
duplicated costs financed by another source;
undocumented or unsupported expenditure;
personal expenditure;
unrelated travel, hospitality, or representation.

Changing the name, invoice description, cost category, supplier, Work Package, Deliverable, or Milestone does not change the principal purpose of an expenditure.

Relationship to Section 11

Section 11 and Section 12 must always be interpreted together.

Section 11 — Use of Funds defines expenditure that may qualify.

Section 12 — Excluded Costs defines expenditure that must not be financed.

A cost is fundable only when:

it satisfies every applicable eligibility condition in Section 11; and

it is not excluded by Section 12; and

it complies with the applicable funder's rules and approval requirements.

Funder permission alone does not make a cost eligible under the Development Round if its purpose belongs to another AgriPartners funding component.

Financial Integrity Rule

No Excluded Cost may be financed through:

contingency;

Work Package reassignment;
Deliverable reassignment;
Milestone movement;
internal accounting transfer;
cost-category reclassification;
budget reallocation;
supplier invoice restructuring;
splitting one excluded cost across eligible categories;
retrospective justification.

If an Excluded Cost is necessary for AgriPartners, it must be assigned to its correct funding component and financed separately.

Any suspected misclassification must be resolved before funds are committed or spent.

Funding Component Traceability

Every expenditure must be assigned according to its actual purpose:

Corporate Setup



Corporate Setup Budget

Product Development



USD 40,000 Development Budget

Operational Readiness



Operational Readiness Budget or approved Readiness component

Feedlot Pilot



Feedlot Pilot Capital

Hissar Pilot



Hissar Pilot Capital

Production Financial Operations



Separately approved production funding and governance

An expenditure cannot move between these components merely because funding is available in one component but unavailable in another.

This separation preserves:

financial discipline;

funding transparency;

use-of-funds integrity;

accurate grant reporting;

independent accountability;

protection against cross-subsidisation;

protection of the Beta Candidate budget;

protection of both Pilot Rounds from unrelated expenditure.

This Section is the authoritative negative financial boundary of the Development Round. No excluded expenditure may be charged, allocated, reimbursed, or otherwise financed from the approved USD 40,000 Development Budget.

13. Development Milestones

Development Milestones define the official sequence of verified product states through which the Development Round progresses toward completion of the **Pilot Operations & Investor Evidence Beta Candidate**.

Collectively, the approved Development Milestones define the complete progress-governance framework for the Development Round.

A Milestone represents completed and reviewable value. It is not a measure of elapsed time, expenditure, engineering activity, or percentage complete.

All five mandatory Milestones must be completed before the Development Round can proceed to final acceptance.

13.1 Milestone Structure

Every Development Milestone must contain the following elements.

Objective

Defines the completed project state that the Milestone is intended to establish.

Included Work Packages

Identifies the Work Packages whose completed outputs are required for the Milestone.

Supporting Work Packages may contribute evidence or controls without transferring their own completion status.

Deliverables

Identifies the completed outputs required for Milestone review.

A Deliverable cannot support Milestone completion while remaining incomplete or conditionally represented as finished.

Dependencies

Identifies earlier Milestones, Work Packages, approved decisions, product foundations, or other conditions that must be satisfied.

Verification Evidence

Identifies the evidence required to demonstrate that the Milestone state exists.

Detailed verification methods and reporting requirements are governed by the later Verification and Reporting Evidence section.

Exit Criteria

Defines the conditions that must be satisfied before the Milestone may be formally marked complete.

Exit Criteria measure completed outcomes rather than activity.

Budget Release Relationship

Identifies the Development Budget allocations associated with the Milestone and explains how Milestone completion may relate to controlled funding release.

A Budget Release Relationship does not mean that:

expenditure proves completion;

Milestone completion automatically authorizes payment;

a funder must use a particular tranche structure;

unspent funds must be released without satisfying the funding agreement.

The applicable funding agreement governs actual payment and release mechanics.

Milestone Completion Rule

A Development Milestone is complete only when:

all included Work Packages required for the Milestone have satisfied their Acceptance Criteria;

all required Deliverables are complete;

all required Verification Evidence exists and is reviewable;

applicable Dependencies are satisfied;

Exit Criteria are met;

unresolved defects, risks, or exceptions do not invalidate the completed state;

completion is formally recorded through the applicable governance process.

Implementation activity, code submission, expenditure, elapsed time, demonstration preparation, or a planned completion date does not independently establish Milestone completion.

Milestone completion is determined through the combined satisfaction of all governing requirements rather than any individual criterion in isolation.

13.2 Milestone 1 — Expense Platform Complete

Objective

Establish a complete and controlled Project Expense product capability that can support the remaining Beta Candidate workflow.

The completed state must connect the existing Project Expense accounting foundation to a user-visible lifecycle governed by product-level authorization and operational controls.

Included Work Packages

WP-C01 — Project Expense Platform;

WP-C02 — Project Expense Authorization and Operational Controls;

applicable verification support from WP-C08.

Deliverables

D-P01 — Completed Project Expense Workflow;

D-T01 — Project Expense API and Authorization Capability;

applicable Milestone 1 elements of D-Q02 — Authorization and Financial-Control Verification.

Dependencies

verified current product baseline;

completed Stage 2 Financial Workflow Foundation;

completed Stage 2 Project Expense Accounting Foundation;

existing authentication and role baseline;

approved Development Scope and Work Package governance.

Verification Evidence

end-to-end Project Expense lifecycle evidence;

permitted-action and prohibited-action results;

role and authorization evidence;

relevant financial-control results;

resulting lifecycle and product records;

Work Package completion records.

Exit Criteria

Milestone 1 is complete when:

the supported Project Expense lifecycle is available through the product;

supported Expense actions operate within the correct Project, workflow, Operator, budget, category, and currency context;

permitted roles can perform approved actions;

prohibited actions are consistently rejected;

requester, approver, and payer separation remains effective where applicable;

relevant budget, lifecycle, reservation, and overspending controls remain effective;

required Deliverables and Verification Evidence are complete;

no unresolved critical issue invalidates the Project Expense capability.

Budget Release Relationship

Milestone 1 is primarily associated with:

BA-01 — Project Expense Platform;

BA-02 — Project Expense Authorization and Operational Controls;

applicable verification portion of BA-08;

approved contingency only where necessary to protect mandatory completion.

Where Milestone-based funding is used, Milestone 1 may support release of the next approved tranche after verification and formal recognition.

13.3 Milestone 2 — Operator Workspace Complete

Objective

Establish a coherent Operator-facing experience for managing the supported Project Expense and operational workflow.

The completed state must allow an authorized Operator to use the controlled product capability established by Milestone 1 through one integrated workspace.

Included Work Packages

WP-C03 — Operator Workspace;

completed outputs from WP-C01 and WP-C02;

applicable verification support from WP-C08.

Deliverables

D-P02 — Completed Operator Workspace;

Operator-facing elements of D-T03 — Role-aware Frontend Integration;

applicable Verification Evidence supporting the Operator journey.

Dependencies

Milestone 1 — Expense Platform Complete;

applicable Project, workflow, budget, and Operator context;

completed authorization capability;
approved Operator role boundaries.

Verification Evidence

complete Operator journey;
role-access evidence;
permitted-action and prohibited-action results;
resulting Expense and lifecycle records;
Operator Workspace review record;
applicable quality evidence.

Exit Criteria

Milestone 2 is complete when:

an authorized Operator can access the relevant Project context;
applicable workflow, budget, and Expense information is available;
the Operator can initiate and follow the supported Expense workflow;
permitted operational actions can be completed through the product;
blocked or prohibited actions are clearly rejected;
lifecycle status is visible and understandable;
the supported Operator scenario does not require direct database intervention or disconnected administrative tools;
required Deliverables and Verification Evidence are complete;
no unresolved critical issue prevents completion of the Operator journey.

Budget Release Relationship

Milestone 2 is primarily associated with:

BA-03 — Operator Workspace;
applicable verification portion of BA-08;
approved contingency only where necessary to protect mandatory completion.

Where Milestone-based funding is used, verified completion may support the next controlled release under the applicable funding agreement.

13.4 Milestone 3 — Evidence Layer Complete

Objective

Establish a complete and reviewable evidence capability connected to Project Expenses, lifecycle states, and the wider operational data flow.

The completed state must make supporting evidence part of the controlled product workflow rather than a disconnected reference.

Included Work Packages

WP-C04 — Evidence Management;

supporting outputs from WP-C01, WP-C02, and WP-C03;

applicable integration and verification support from WP-C06 and WP-C08.

Deliverables

D-P03 — Completed Evidence Workflow;

D-T02 — Integrated Project Expense and Evidence Data Flow;

applicable evidence and lifecycle elements required for later reporting.

Dependencies

Milestone 1 — Expense Platform Complete;

Milestone 2 — Operator Workspace Complete;

applicable Expense, lifecycle, role, and disclosure context;

approved evidence classifications and authority boundaries.

Verification Evidence

evidence-association records;

evidence classification and status evidence;

role-appropriate evidence access results;

evidence disclosure and restriction results;

lifecycle linkage evidence;

integrated data-flow evidence;

Work Package completion records.

Exit Criteria

Milestone 3 is complete when:

evidence can be associated with the correct Project Expense;

evidence remains connected to relevant Project, workflow, and lifecycle context;

authorized users can perform supported evidence actions;

restricted evidence remains protected;

evidence status and authority are presented accurately;

evidence references are not represented as independent proof beyond their actual authority;

the evidence workflow supports the reporting and Investor Transparency capabilities required by later Milestones;
required Deliverables and Verification Evidence are complete;
no unresolved critical issue invalidates the evidence workflow.

Budget Release Relationship

Milestone 3 is primarily associated with:

BA-04 — Evidence Management;

applicable integration portions of related Core allocations;

applicable verification portion of BA-08;

approved contingency only where necessary to protect mandatory completion.

Verified completion may support the next controlled funding release where the funding agreement uses Milestone-based tranches.

13.5 Milestone 4 — Investor Transparency Complete

Objective

Establish a controlled Investor-facing experience through which permitted Project operations, Project Expense information, evidence availability, reporting, and lifecycle history can be reviewed.

The completed state must provide meaningful transparency without creating unrestricted disclosure or implying live investment activity.

Included Work Packages

WP-C05 — Investor Transparency;

WP-C06 — Operational and Investor Reporting;

supporting outputs from WP-C01 through WP-C04;

applicable verification support from WP-C08.

Deliverables

D-P04 — Completed Investor Transparency Experience;

D-P05 — Completed Operational and Investor Reporting;

D-T03 — Role-aware Frontend Integration;

applicable disclosure and reporting Verification Evidence.

Dependencies

Milestone 1 — Expense Platform Complete;

Milestone 2 — Operator Workspace Complete;

Milestone 3 — Evidence Layer Complete;

approved role, Project relationship, status, and disclosure boundaries;
verified operational and evidence records.

Verification Evidence

complete Investor review journey;

Investor role-access evidence;

disclosure and restriction results;

reporting outputs;

source-record comparison;

status and authority labelling review;

Work Package completion records.

Exit Criteria

Milestone 4 is complete when:

an authorized Investor can access the approved Project context;

permitted operational and Project Expense information is reviewable;

evidence availability or approved references are presented appropriately;

reporting accurately reflects relevant source records;

projected, recorded, approved, paid, reconciled, and completed states remain distinguishable;

restricted, internal, personal, or unsupported information remains protected;

the experience does not imply live investment, audited performance, or production settlement;

required Deliverables and Verification Evidence are complete;

no unresolved critical issue invalidates Investor review or disclosure control.

Budget Release Relationship

Milestone 4 is primarily associated with:

BA-05 — Investor Transparency;

BA-06 — Operational and Investor Reporting;

applicable verification portion of BA-08;

approved contingency only where necessary to protect mandatory completion.

Verified completion may support the final implementation or completion tranche where permitted by the applicable funding agreement.

13.6 Milestone 5 — Beta Candidate Complete

Objective

Confirm that the Development Objective has been achieved and that the complete **Pilot Operations & Investor Evidence Beta Candidate** exists as an integrated, demonstrable, reviewable, and verifiable product state.

Included Work Packages

WP-C07 — Demonstration Environment and Scenario;

WP-C08 — Quality Assurance and Product Security;

WP-C09 — Documentation, Delivery Evidence, and Acceptance Support;

completed and integrated outputs from WP-C01 through WP-C06.

All Core Work Packages must be complete for Milestone 5.

Recommended or Optional Work Packages are included only when formally activated and incorporated into the approved delivery commitment.

Deliverables

Milestone 5 requires:

all Minimum Product Deliverables;

all Minimum Technical Deliverables;

all Minimum Demonstration Deliverables;

all Minimum Security and QA Deliverables;

all Minimum Documentation Deliverables;

all Minimum Grant Reporting Deliverables.

This includes, in particular:

D-T04 — Controlled Beta Demonstration Deployment;

D-D01 — Approved Demonstration Scenario and Data;

D-D02 — End-to-End Beta Candidate Demonstration;

D-D03 — Demonstration Review Package;

D-Q01–D-Q04;

D-DO01–D-DO04;

D-G01–D-G04.

Dependencies

Milestones 1–4 formally completed;

all Core Work Packages complete;

all Minimum Deliverables complete;
controlled demonstration environment available;
Verification Evidence organized and reviewable;
documentation aligned with delivered product behaviour;
accepted non-production boundaries preserved.

Verification Evidence

complete end-to-end Beta Candidate demonstration;
integrated Operator and Investor journeys;
resulting product and system records;
functional and regression verification results;
authorization and financial-control results;
product security validation record;
deployment verification record;
documentation review;
Deliverable traceability record;
Milestone reports;
Verification Evidence Package;
Development Round Completion Report.

Exit Criteria

Milestone 5 is complete when:
the Development Objective established in Section 5 has been achieved;
the Beta Candidate defined in Section 6 exists as an integrated product state;
all Core Work Packages satisfy their Acceptance Criteria;
all Minimum Deliverables are complete;
all mandatory Verification Evidence exists and is reviewable;
the end-to-end scenario can be demonstrated through observable product behaviour;
no unresolved critical defect prevents the approved workflow;
required documentation accurately represents delivered capabilities and limitations;
complete traceability exists from the Development Objective through Acceptance Criteria;

the Development Round is ready for formal completion and acceptance evaluation.

Milestone 5 does not constitute:

Corporate Setup completion;

Operational Readiness;

Production Readiness;

Mainnet Readiness;

regulatory approval;

live investment authorization;

Feedlot Pilot approval;

Hissar Pilot approval;

a Pilot GO decision.

Successful completion of Milestone 5 establishes completion of the Development Round product objective only.

Budget Release Relationship

Milestone 5 is primarily associated with:

BA-07 — Demonstration Environment and Scenario;

BA-08 — Quality Assurance and Product Security;

BA-09 — Documentation, Delivery Evidence, and Acceptance Support;

any properly approved contingency used to protect Core completion.

Where funding is Milestone-based, verified completion may support final tranche release, retention release, or final grant acceptance subject to the applicable funding agreement.

Milestone completion does not independently establish payment entitlement where additional contractual or financial reporting conditions apply.

13.7 Milestone Dependencies and Sequence

The official Milestone sequence is:

Milestone 1

Expense Platform Complete

↓

Milestone 2

Operator Workspace Complete

↓

Milestone 3

Evidence Layer Complete

↓

Milestone 4

Investor Transparency Complete



Milestone 5

Beta Candidate Complete

Each Milestone builds upon verified outputs produced by earlier Milestones.

Work may proceed in parallel where technically and operationally appropriate, but formal Milestone recognition must preserve the approved dependency sequence.

A later Milestone must not be marked complete when a required earlier Milestone remains incomplete, conditionally represented without approval, or unsupported by the required Verification Evidence.

Completion of one Milestone never implies completion of a later Milestone.

In particular:

an Expense platform does not establish a completed Operator Workspace;

an Operator Workspace does not establish a completed Evidence Layer;

an Evidence Layer does not establish completed Investor Transparency;

Investor Transparency does not establish a completed Beta Candidate;

a completed Beta Candidate does not establish Operational Readiness or Pilot approval.

A Milestone sequence may not be bypassed through:

budget expenditure;

Work Package relabelling;

Deliverable reassignment;

demonstration scheduling;

grant-reporting deadlines;

external presentation dates;

partial implementation;

informal acceptance.

Approved dependency sequencing preserves product integrity and prevents incomplete functionality from being represented as completed value.

Milestone Traceability

Every Milestone must remain within the following traceability chain:


Development Objective



Beta Candidate



Development Scope

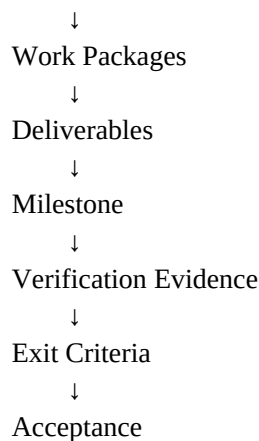

These traceability principles apply uniformly to every mandatory Development Milestone.

Milestones define measurable progress. Verification establishes whether the required evidence supports completion. Acceptance determines whether the verified Milestone is formally approved.

Accordingly, the approved Milestone framework is the governing progress model for execution, reporting, verification, and formal recognition of the Development Round. Successful completion requires every mandatory Milestone to be verified, to satisfy its Exit Criteria, and to receive the required formal recognition. No Milestone may be declared complete solely because time has passed, funds have been spent, or development activity has occurred.

14. Verification and Reporting Evidence

This section defines the official evidence framework used to verify Work Packages, Deliverables, Milestones, and final Development Round completion.

A completion claim is valid only when relevant, attributable, accessible, and reviewable evidence demonstrates that the applicable result exists and can be evaluated against its approved requirements.

The evidence framework distinguishes between:

implementation activity;

evidence that implementation activity occurred;

verification of the completed result;

formal reporting of that result;

acceptance of the result.

These stages are related but are not interchangeable.

Money spent, time elapsed, code written, a commit created, a Pull Request merged, a demonstration prepared, a report submitted, or a task marked complete does not independently prove that a Deliverable or Milestone has been achieved.

Evidence Register

Verification Evidence must be recorded in a controlled Evidence Register.

Each evidence entry should identify:

a unique evidence identifier;

evidence title and type;
related Work Package;
related Deliverable;
related Milestone;
requirement or criterion supported;
source or owner;
creation or execution date;
relevant product version;
relevant environment where applicable;
storage location or review link;
access classification;
review status;
known limitations;
integrity information where appropriate.

Evidence must be accessible to the authorized reviewer. Accessibility does not require all evidence to be made public.

Security-sensitive information, personal data, credentials, private keys, environment secrets, confidential commercial information, and unresolved vulnerability details must not be published in the public repository or unrestricted evidence packages.

14.1 Repository and Pull Request Evidence

Repository evidence establishes what changed within the product source and documentation baseline, why it changed, how it was reviewed, and whether it entered the accepted implementation baseline.

Repository evidence may include:

commit identifiers;
commit messages;
branch references;
Pull Request references;
changed-file records;
code or documentation review records;
review comments and resolution records;
merge records;

accepted baseline commit identifiers;

release tags;

repository status records;

implementation traceability references;

relevant CI or workflow-run records.

Repository evidence supporting a completion claim should identify:

the Work Package and Deliverable supported;

the purpose of the change;

the relevant files or components;

the review performed;

the resulting decision;

whether the change was merged;

the exact accepted baseline containing the change.

Unmerged branches, draft Pull Requests, abandoned commits, or local changes may demonstrate activity but do not establish inclusion in the accepted baseline.

A commit, Pull Request, review, merge, or release tag is supporting evidence only. It does not independently prove:

correct product behaviour;

satisfaction of Acceptance Criteria;

successful deployment;

completed integration;

absence of defects;

Milestone completion;

formal acceptance.

Repository evidence must be evaluated together with the applicable test, product, demonstration, documentation, and review evidence.

14.2 Test and QA Evidence

Test and QA evidence demonstrates whether the applicable product capability behaves as required within the tested scope.

Acceptable evidence may include:

automated test results;

unit-test results;

integration-test results;
database and migration verification;
regression-test results;
negative-path tests;
authentication and authorization tests;
responsibility-separation tests;
Project Expense lifecycle tests;
budget and overspending-control tests;
concurrency tests;
evidence-access and disclosure tests;
API behaviour tests;
frontend user-journey verification;
deployment checks;
defect records;
remediation and closure records;
manual review checklists where automation is not appropriate.

Every test record used as Verification Evidence should identify:

the tested product version or commit;
the applicable environment;
the execution date;
the tested Work Package or Deliverable;
the relevant requirement;
the test result;
failures, warnings, skips, or exclusions;
the responsible reviewer or execution source;
any limitation affecting interpretation.

A passing test suite proves only the behaviour covered by its tested scope. It does not prove requirements that were omitted, disabled, skipped, excluded, or evaluated in a materially different environment.

Skipped and excluded tests must remain visible where they affect a completion claim. A test report must not be represented as fully passing if relevant failures or exclusions have been removed from the reported result without explanation.

Manual QA evidence must identify the scenario, expected result, observed result, tested version, environment, reviewer, and outcome.

Defect records must distinguish among:

open;

under investigation;

resolved;

verified closed;

accepted limitation;

deferred outside the approved scope.

Resolution without verification does not establish defect closure.

14.3 Security Evidence

Security evidence supports Beta-level product security validation within the approved Development Scope.

It may include:

authentication review;

authorization review;

role-boundary review;

prohibited-action testing;

data-exposure review;

evidence-access review;

configuration review;

dependency review;

secret-handling review;

demonstration-environment review;

security findings register;

remediation records;

retest results;

accepted limitations;

closure decision.

Each material security finding should identify:

the affected capability;

severity or risk classification;

evidence supporting the finding;

potential impact;

remediation or control;

retest result where applicable;

residual risk;

disposition;

approving authority for any accepted limitation.

Security evidence must be handled according to its sensitivity. Evidence made available to a funder or reviewer may use controlled summaries where unrestricted disclosure would create security risk.

No secret, token, private key, seed phrase, unrestricted credential, or sensitive production-style configuration may be included in the public repository or public evidence package.

Security Evidence produced under the Development Round is:

Beta-level product security evidence;

limited to the reviewed scope and version;

subject to documented limitations.

It must not be described as:

an independent external security audit unless one was actually commissioned and completed;

production certification;

regulatory approval;

Mainnet smart-contract audit;

custody approval;

banking-security approval;

Operational Readiness approval.

14.4 Deployment Evidence

Deployment Evidence demonstrates that the controlled review or demonstration environment corresponds to the product version submitted for verification.

It may include:

deployed version or commit reference;

environment identifier;
deployment record;
build result;
configuration summary;
migration status;
database status appropriate to the demonstration;
access verification;
health or availability check;
dependency status;
demonstration result;
deployment limitation record.

Deployment Evidence should establish:

what version was deployed;
where it was deployed;
when deployment occurred;
which configuration class was used;
whether required components were available;
whether the approved demonstration could be completed;
whether the environment differed materially from the verified test environment.

Sensitive configuration values must not be exposed. Evidence should confirm the presence and correct treatment of required configuration without publishing secrets.

Deployment Evidence confirms only the controlled Beta Candidate review environment. It does not independently establish:

production readiness;
production scalability;
production monitoring;
disaster recovery;
regulatory compliance;
live financial capability;
Mainnet readiness;

Operational Readiness.

14.5 Demonstration Evidence

Demonstration Evidence shows that the completed Beta Candidate can be observed and reviewed as an integrated product state.

The required evidence may include:

approved demonstration scenario;

clearly labelled demonstration dataset;

demonstration version reference;

environment and access instructions;

live walkthrough;

recorded walkthrough where appropriate;

resulting product records;

resulting lifecycle and evidence records;

Operator journey evidence;

Investor journey evidence;

reviewer checklist;

repeat-run evidence where required;

known-limitations statement;

demonstration outcome record.

The demonstration must show observable product behaviour. Presentation slides, scripts, screenshots, diagrams, or verbal explanations may support the demonstration but cannot replace functioning product behaviour and resulting reviewable records.

Demonstration Evidence must distinguish clearly between:

demonstration data;

internal product records;

Testnet records;

external authoritative records;

real operational or financial evidence.

Demonstration records must not be presented as:

live Investor funding;

real pilot expenditure;

audited accounting;

bank-confirmed payment;

production settlement;

verified or guaranteed investment returns.

A recorded walkthrough must identify the demonstrated version and environment. Where the recording is edited, the edit must not conceal failed steps, missing functionality, or material limitations.

14.6 Documentation Evidence

Documentation Evidence demonstrates that the delivered product can be understood, reviewed, operated within its approved scope, and compared with its governing requirements.

It may include:

product documentation;

technical documentation;

API documentation;

architecture documentation;

Operator guidance;

Investor or reviewer guidance;

demonstration instructions;

release record;

known-limitations record;

Deliverable register;

traceability matrix;

documentation review record;

approval record.

Documentation used as Verification Evidence must:

describe the delivered product accurately;

identify the applicable version or baseline;

distinguish current capabilities from planned capabilities;

distinguish demonstration behaviour from production architecture;

preserve the approved financial and non-production boundaries;

remain consistent with product behaviour and repository evidence;

identify material limitations.

Documentation does not prove implementation merely because it describes a capability. An implementation claim must remain supported by product, repository, test, deployment, or demonstration evidence as applicable.

Planned functionality must not be presented as implemented. Historical Legacy Testnet Alpha behaviour must not be presented as the target production financial architecture.

14.7 Work Package Evidence

Every Work Package must have an independently reviewable Work Package Evidence Record.

The record must include:

Work Package identifier and title;

Development Scope classification;

Work Package objective;

delivered outputs;

related Deliverables;

Acceptance Criteria assessment;

Verification Evidence index;

dependency status;

applicable test or review results;

defects and findings;

unresolved issues;

accepted exceptions or limitations;

relevant budget status at the approved reporting level;

related Milestone;

completion recommendation;

formal completion or non-completion decision.

The record must distinguish between:

activity performed;

output produced;

output verified;

output accepted.

A Work Package must not be reported as complete when:

a mandatory Deliverable is incomplete;
required Verification Evidence is missing;
a dependency remains unresolved;
an unresolved issue invalidates the intended result;
applicable Acceptance Criteria have not been assessed.

Work Package evidence remains independently reviewable even when several Work Packages contribute to the same Deliverable or Milestone.

Completion of one Work Package does not establish completion of another.

14.8 Milestone Reporting Package

Each Development Milestone requires a formal Milestone Reporting Package.

The package must include:

Milestone identifier and title;

Milestone objective;

included Work Packages;

Work Package completion status;

required Deliverables;

Deliverable completion status;

Verification Evidence index;

Exit Criteria assessment;

dependency status;

defects and security findings;

risks and exceptions;

accepted limitations;

budget and variance summary at the approved reporting level;

contingency or reallocation information relevant to the Milestone;

formal completion recommendation;

formal decision and decision authority.

Each Work Package and Deliverable must use one of the approved reporting statuses:

Not Started — no approved delivery activity or output exists;

In Progress — approved work has begun, but completion requirements are not satisfied;

Blocked — progress or verification cannot continue because of an unresolved dependency or condition;

Incomplete — work or review occurred, but one or more completion requirements remain unsatisfied;

Conditionally Complete — outputs are substantially complete, but a specifically documented and approved condition remains;

Complete — all applicable completion requirements have been satisfied and formally recognised.

Conditionally Complete is not equivalent to Complete. A mandatory condition must be resolved before it can support final Beta Candidate acceptance unless the later acceptance governance explicitly permits and documents the remaining condition.

A Milestone report must not conceal:

failed checks;

skipped verification;

incomplete Deliverables;

blocked dependencies;

unresolved defects;

budget variance;

accepted exceptions;

scope changes.

The formal Milestone decision must be one of:

Complete;

Not Complete;

Conditionally Complete where permitted;

Blocked.

Submission of the Milestone Reporting Package does not itself establish Milestone completion.

14.9 Final Delivery Report

The Development Round requires a Final Delivery Report after the Milestone evidence packages have been assembled.

The report must include:

Development Round identification;

reviewed product version and baseline;

Development Objective assessment;

Beta Candidate status;

Development Scope status;

Core Work Package status;

Recommended and Optional Work Package activation and status;

Minimum Deliverable status;

Milestone completion status;

Verification Evidence index;

Acceptance Criteria assessment reference;

total budget summary;

Work Package and cost-category expenditure summary;

material variance summary;

contingency-use summary;

budget-reallocation summary;

funding and payment status where relevant;

defects, risks, and exceptions;

accepted limitations;

unresolved issues;

excluded-cost compliance statement;

non-production boundary statement;

formal acceptance position;

readiness to proceed to a separate Operational Readiness Review.

The Final Delivery Report must distinguish clearly between:

completed;

verified;

accepted;

conditionally accepted;

incomplete;

planned;

excluded.

It must not declare or imply:

production readiness;
Operational Readiness;
Mainnet readiness;
regulatory approval;
live investment capability;
production custody or settlement;
Feedlot Pilot approval;
Hissar Pilot approval;
a Pilot GO decision;
verified or guaranteed investment returns.

The Final Delivery Report may conclude that the Beta Candidate is ready to enter an Operational Readiness Review. It must not predetermine the result of that review.

Evidence Quality Principles

Acceptable Verification Evidence must be:

Relevant — directly connected to the requirement being assessed;

Attributable — linked to an identifiable source, version, owner, or execution record;

Accessible — available to the authorized reviewer in a usable form;

Reviewable — sufficiently clear to support an independent evaluation of the claim;

Version-specific — linked to the product version or baseline being assessed;

Environment-specific — linked to the relevant environment where environment affects interpretation;

Complete enough — sufficient to determine whether the applicable requirement is satisfied;

Consistent — aligned with related repository, product, test, deployment, demonstration, and documentation records;

Integrity-protected — protected against unsupported alteration through appropriate repository history, access control, hashes, immutable storage, signed records, or equivalent controls where proportionate;

Status-aware — clear about whether the evidence is draft, current, superseded, historical, or accepted.

Evidence must also be classified according to its authority.

Primary evidence

Directly demonstrates the claimed product state or result, such as observable product behaviour, test results, system records, or an accepted deployed version.

Supporting evidence

Provides context or corroboration, such as commits, Pull Requests, screenshots, diagrams, explanations, or review notes.

External authoritative evidence

Originates from an appropriate external authority, such as a bank, payment provider, auditor, regulator, legal adviser, or signed contractual source.

Internal product records

Records created by AgriPartners systems. They may demonstrate internal workflow state but do not automatically prove an external legal, banking, accounting, or operational event.

Demonstration records

Records produced using controlled demonstration data. They demonstrate product behaviour but not live investment or agricultural activity.

An evidence item must not be represented as possessing greater authority than its source provides.

Evidence Sufficiency Rule

Evidence is sufficient only when it enables the reviewer to determine whether the applicable requirement has been satisfied.

Evidence volume does not establish evidence quality. Large quantities of irrelevant, duplicated, outdated, or untraceable material do not compensate for missing primary evidence.

One artifact may support multiple requirements, but:

every requirement must be explicitly mapped to the artifact;

the supported relationship must be understandable;

limitations of the artifact must remain visible;

the artifact must remain applicable to the reviewed version and environment.

Where evidence conflicts, the conflict must be investigated and documented. The most favourable evidence must not be selected while contradictory material is omitted.

Absence of a recorded problem is not evidence that the requirement was satisfied.

Exception and Limitation Reporting

All material exceptions, failed checks, unresolved defects, blocked dependencies, scope deviations, and accepted limitations must be documented.

Each exception or limitation record should identify:

a unique identifier;

affected Work Package, Deliverable, Milestone, or requirement;

description;

cause;

impact;

risk;

current status;

proposed resolution or compensating control;

responsible owner;

target resolution condition where applicable;

whether verification may continue;

whether acceptance remains possible;

approving authority for any accepted limitation.

An exception must not be closed merely because it has been documented.

Accepted limitations must remain visible in:

the relevant Work Package Evidence Record;

the relevant Milestone Reporting Package;

the Final Delivery Report;

the release and known-limitations documentation where applicable.

Silence, omission, missing evidence, or lack of a recorded defect must not be treated as evidence that no issue exists.

Verification Traceability

Every Verification Evidence item must remain within the following traceability chain:

Development Objective



Beta Candidate



Development Scope



Work Package



Deliverable



Milestone



Verification Evidence



Acceptance Criteria



Acceptance Decision

No evidence item may be accepted without a clearly identified relationship to the requirement it supports.

The Traceability Matrix must allow an authorized reviewer to move in both directions:

from a requirement to its supporting evidence;

from an evidence item to the requirement and decision it supports.

Relationship to Section 15

Section 14 defines the evidence used to verify Development Round results.

Section 15 defines the Completion and Acceptance Criteria against which that evidence is evaluated.

Evidence does not automatically produce acceptance.

Acceptance requires a documented decision based on:

the applicable criteria;

sufficient Verification Evidence;

disclosed exceptions and limitations;

satisfied governance requirements;

the authorized acceptance process.

This Verification and Reporting Evidence framework is the official evidence standard for the Development Round. It ensures that completion claims are based on demonstrated and reviewable outcomes rather than activity, expenditure, unsupported statements, or presentation materials alone.

15. Completion and Acceptance Criteria

This section establishes the official completion and acceptance framework for the Development Round.

It defines the conditions that must be satisfied before a Work Package, Deliverable, Milestone, or the completed **Pilot Operations & Investor Evidence Beta Candidate** may receive formal acceptance.

The governance sequence is:

Implementation

↓

Verification

↓

Completion Assessment

↓

Acceptance Decision

↓

Formal Recognition

These stages are related but not interchangeable.

Implementation produces the intended output.

Verification produces evidence about that output.

Completion Assessment evaluates the output and evidence against the applicable criteria.

Acceptance is the documented governance decision.

Formal Recognition records the accepted status for reporting and future reliance.

Completion is not acceptance. Verification is not acceptance. Evidence is not acceptance.

15.1 Product Completion Criteria

The product may be assessed as complete only when the delivered product demonstrates that the Development Objective has been achieved.

Product completion requires confirmation that:

the Pilot Operations & Investor Evidence Beta Candidate defined in Section 6 exists;

the Minimum Viable Development Scope has been delivered;

all Core Work Packages are complete;

all Minimum Deliverables are complete;

all mandatory Milestones have satisfied their Exit Criteria;

the required product capabilities operate as an integrated product state;

mandatory role and authorization boundaries are preserved;

Project Expense, evidence, reporting, and Investor Transparency capabilities are connected;

required Verification Evidence exists;

delivered behaviour corresponds to the accepted product version;

no unresolved issue invalidates the Development Objective or Beta Candidate;

non-production boundaries remain accurate and visible.

Completion must be assessed against delivered and observable product behaviour.

Planned, partially implemented, Recommended, Optional, or documented-only functionality must not be counted as completed Minimum Scope.

Recommended or Optional capabilities affect completion only when formally activated and incorporated into the approved delivery commitment.

15.2 End-to-End Workflow Criteria

The complete operational workflow must be observable, repeatable, and reviewable within the controlled Beta Candidate environment.

The end-to-end workflow must demonstrate:

access to the relevant Project context;

an authorized Operator interaction;

initiation or recording of a supported Project Expense;

association with the correct workflow, budget, category, currency, and Operator context;

application of role and authorization controls;

enforcement of the supported Expense lifecycle;
association and review of supporting evidence;
preservation of lifecycle history;
generation or presentation of applicable reporting;
controlled disclosure of relevant information to an Investor;
resulting product and system records.

The workflow satisfies the completion criteria only when:

the approved scenario can be completed through the product;
required steps do not depend on direct database intervention;
prohibited actions are rejected consistently;
required controls remain effective;
resulting records correspond to the performed actions;
the workflow can be reviewed against documented evidence;
demonstration data is clearly identified;
known limitations remain visible;
no critical defect prevents the intended scenario.

A walkthrough, presentation, video, or script cannot independently satisfy these criteria without corresponding observable product behaviour and reviewable records.

15.3 Operator Acceptance Criteria

The Operator-facing product experience may be accepted when an authorized Operator can complete the supported operational scenario within the approved product boundaries.

Operator acceptance requires confirmation that:

the relevant Project context is accessible;
applicable workflow, budget, Expense, evidence, and reporting information is understandable;
the Operator can perform each permitted action required by the supported scenario;
prohibited or unavailable actions are clearly rejected;
role boundaries are applied consistently;
authorization status is visible where necessary;
Project Expense lifecycle state is reviewable;
applicable budget and control information is available;

supporting evidence can be associated and reviewed appropriately;

errors and validation results provide sufficient user feedback;

the workflow does not require an Uzbekistan-facing crypto wallet or on-chain financial action;

the Operator journey can be completed without undocumented technical intervention.

Operator acceptance is product-level acceptance. It does not establish legal identity, corporate mandate, contract authority, banking authority, payment authority, or Operational Readiness.

15.4 Investor Demonstration Criteria

The Investor-facing experience may be accepted when an authorized Investor can review the permitted Project information through a coherent and controlled product experience.

Investor demonstration acceptance requires confirmation that:

relevant Project context is available;

operational progress is understandable;

permitted Project Expense information is reviewable;

applicable budget or budget-summary information is presented appropriately;

evidence availability or permitted evidence references are visible;

relevant reports are accessible;

lifecycle history is reviewable;

projected, recorded, approved, paid, reconciled, and completed states remain distinguishable;

disclosure controls protect restricted information;

internal records are not presented as possessing unsupported external authority;

demonstration records are not presented as live investment activity;

displayed returns are not presented as audited, verified, guaranteed, or production-settled results;

the Investor journey can be demonstrated and reviewed against the applicable evidence.

The accepted Investor experience demonstrates controlled transparency. It does not demonstrate live Investor onboarding, live capital intake, custody, payouts, production settlement, or a regulated investment service.

15.5 QA and Security Criteria

Beta Candidate acceptance requires sufficient QA and product-level security evidence for the approved scope and version.

QA completion requires confirmation that:

mandatory functional tests have been completed;

relevant integration tests have been completed;

relevant regression tests have been completed;
negative-path and prohibited-action behaviour has been evaluated;
authorization boundaries have been evaluated;
Project Expense lifecycle controls have been evaluated;
budget, reservation, and overspending controls have been evaluated;
evidence-access and disclosure controls have been evaluated;
the principal Operator and Investor journeys have been verified;
failed, skipped, or excluded checks affecting acceptance are disclosed;
material defects have documented status;
resolved defects have been appropriately reverified.

Security completion requires confirmation that:

authentication and authorization have received Beta-level review;
relevant data-exposure risks have been reviewed;
evidence-access boundaries have been reviewed;
configuration and secret-handling conditions have been reviewed;
relevant dependency risks have been reviewed where applicable;
security findings have been recorded;
required remediation has been verified;
accepted security limitations are documented;
no unresolved critical security issue invalidates the Beta Candidate or controlled demonstration environment.

These criteria establish Beta-level product quality and security acceptance only.

They do not constitute:

production certification;
an independent external security audit unless separately commissioned;
regulatory approval;
Mainnet approval;
custody approval;
banking approval;

Operational Readiness.

15.6 Deployment Criteria

The controlled Beta Candidate deployment may be accepted when the reviewed environment corresponds to the version submitted for acceptance and supports the approved demonstration.

Deployment acceptance requires confirmation that:

the deployed version or commit is identifiable;

the environment is identified;

the relevant build completed successfully;

required configuration is present without exposing secrets;

applicable database migrations and required data state are established;

the environment is accessible to the intended reviewer;

the approved demonstration scenario can be completed;

the resulting records are reviewable;

material differences between tested and deployed environments are documented;

deployment limitations are disclosed;

no unresolved deployment issue prevents Beta Candidate review.

The accepted deployment remains a controlled Beta or demonstration environment.

Deployment acceptance does not establish production availability, production scalability, disaster recovery, Mainnet readiness, production monitoring, financial infrastructure readiness, or authorization for live operations.

15.7 Documentation Criteria

Documentation may be accepted when it accurately represents the delivered Beta Candidate and provides sufficient guidance for operation, review, verification, and reporting.

Documentation acceptance requires:

current product documentation;

relevant technical documentation;

relevant API or integration documentation;

Operator guidance;

reviewer or demonstration guidance;

release record;

known-limitations record;

Deliverable register;

evidence index;

traceability matrix;

appropriate version identification;

documentation review and approval evidence.

Accepted documentation must:

correspond to delivered product behaviour;

distinguish implemented from planned functionality;

distinguish Minimum from activated Recommended or Optional Scope;

preserve the Estonia-to-Uzbekistan fiat boundary;

distinguish Legacy Testnet Alpha behaviour from the target architecture;

preserve non-production limitations;

avoid unsupported product, security, regulatory, financial, traction, or return claims.

Documentation cannot compensate for missing product functionality. A documented capability is not accepted as implemented unless corresponding product and verification evidence exists.

15.8 Known-Limitations Criteria

Known limitations do not automatically prevent Beta Candidate acceptance.

A limitation may be acceptable when it:

is documented clearly;

is supported by an identifiable record;

does not invalidate the Development Objective;

does not prevent the approved end-to-end workflow;

does not compromise a mandatory authorization or financial control;

does not expose unacceptable security or data risk;

does not make a Minimum Deliverable materially incomplete;

remains consistent with Beta-level and non-production positioning;

has an approved disposition;

remains visible in relevant documentation and reporting.

A limitation is unacceptable when it:

prevents completion of a mandatory workflow;

invalidates a Core Deliverable;

bypasses a required authorization boundary;

compromises material financial or evidence integrity;
creates an unresolved critical security risk;
causes Investor disclosure to become materially misleading;
requires planned functionality to be represented as implemented;
conceals a failed verification requirement;
contradicts an approved product or financial boundary;
prevents objective review of the Beta Candidate.

Every accepted limitation must identify:

the affected requirement;
impact;
residual risk;
reason acceptance remains possible;
compensating control where applicable;
approving authority;
relationship to future work or Operational Readiness.

Hidden or omitted limitations are unacceptable.

Acceptance of a limitation for the Beta Candidate does not mean that the limitation will be acceptable for Operational Readiness, production deployment, Mainnet use, or a real Pilot.

15.9 Milestone Exit Criteria

Milestone Exit Criteria determine whether each Milestone has reached the verified state defined in Section 13.

The governance sequence for each Milestone is:

Included Work Packages completed



Required Deliverables completed



Verification Evidence assembled



Exit Criteria assessed



Milestone Acceptance Decision

Milestone acceptance requires:

included mandatory Work Packages to be complete;
required Deliverables to be complete;

dependencies to be satisfied;

Verification Evidence to be sufficient;

Exit Criteria to be satisfied;

material exceptions and limitations to be disclosed;

unresolved issues not to invalidate the Milestone state;

a documented decision by the authorized authority.

Completion of every mandatory Milestone is necessary but not sufficient for final Development Round acceptance.

Final acceptance additionally requires:

successful integration across Milestones;

completion of the full Beta Candidate;

consistency of the complete evidence package;

satisfaction of the final Completion Criteria;

formal evaluation of the Development Objective.

A Milestone accepted earlier may be reopened if later integration reveals that its output no longer satisfies the applicable criteria. Any reopening must be documented and reflected in subsequent reporting.

15.10 Final Beta Candidate Acceptance

Final Beta Candidate acceptance is the formal decision that the Development Round has produced the product state approved in Sections 5 and 6.

Final acceptance requires confirmation that:

the Development Objective has been achieved;

the Pilot Operations & Investor Evidence Beta Candidate exists;

the Minimum Viable Development Scope has been delivered;

all Core Work Packages are complete;

all Minimum Deliverables are complete;

all mandatory Milestones are accepted;

the end-to-end workflow satisfies the approved criteria;

Operator Acceptance Criteria are satisfied;

Investor Demonstration Criteria are satisfied;

QA and Security Criteria are satisfied;

Deployment Criteria are satisfied;

Documentation Criteria are satisfied;
Verification Evidence is sufficient;
complete traceability exists;
material exceptions and limitations are disclosed;
accepted limitations do not invalidate the Beta Candidate;
the Final Delivery Report accurately reflects the completed result;
the authorized governance decision has been recorded.

Final Beta Candidate acceptance does not constitute:

Corporate Setup completion;
legal or regulatory readiness;
Operational Readiness;
Production Readiness;
Mainnet Readiness;
banking, payment, custody, or settlement readiness;
live investment authorization;
Feedlot Pilot approval;
Hissar Pilot approval;
a Pilot GO decision;
verification or guarantee of investment returns.

An accepted Beta Candidate may proceed to a separate Operational Readiness Review. Final Beta Candidate acceptance does not predetermine that review's outcome.

Acceptance Governance

Acceptance requires:

completed Verification Evidence;
assessment against the applicable Completion or Exit Criteria;
disclosure of material defects, risks, exceptions, and limitations;
confirmation of applicable dependencies;
a documented decision;
an authorized approving authority;

a retained Acceptance Record.

The appropriate approving authority or designated decision-makers must be determined under the applicable AgriPartners governance model and any funder-specific agreement.

Acceptance must never result automatically from:

elapsed time;

budget expenditure;

repository activity;

completed coding;

a branch, commit, Pull Request, merge, or release tag;

passing tests without requirement coverage;

a completed demonstration without the required evidence;

report submission;

a task status;

a planned launch or presentation date;

external pressure or funding deadlines.

No schedule overrides acceptance criteria.

Acceptance Record

Every formal Acceptance Decision must identify:

the object being assessed;

reviewed version or baseline;

applicable criteria;

Verification Evidence index;

criteria assessment;

unresolved defects or exceptions;

accepted limitations;

decision;

decision rationale;

approving authority;

decision date;

conditions or follow-up obligations where applicable.

Acceptance identifiers and decisions must remain stable and traceable throughout later reporting, audit, funder review, and Operational Readiness assessment.

Acceptance Decision Types

The permitted formal decisions are:

Accepted

All applicable Completion Criteria are satisfied, required evidence is sufficient, and no unresolved limitation invalidates the accepted result.

Accepted with Approved Limitations

All requirements necessary for the intended Beta Candidate use are satisfied, while specifically documented, non-blocking limitations remain.

Each limitation must have an approved rationale, residual-risk assessment, and disclosure record.

Conditionally Accepted

Acceptance is permitted subject to one or more explicit, measurable, and approved conditions.

The decision must identify:

each unresolved condition;

responsible owner;

required evidence;

resolution requirement;

review authority;

consequence of non-resolution.

Conditionally Accepted is not equivalent to final Accepted status. The result must not be represented as fully accepted until the conditions are resolved and the decision is formally updated.

A condition must not be used to defer a failure that invalidates the Development Objective, Core Scope, mandatory security boundary, or Beta Candidate.

Not Accepted

One or more applicable Completion Criteria are not satisfied, required evidence is insufficient, or an unresolved issue invalidates the claimed result.

The decision must identify the rejection basis and the requirements for reconsideration where reconsideration remains possible.

Acceptance Traceability


Every Acceptance Decision must remain within the following traceability chain:

Development Objective

↓

Beta Candidate

↓

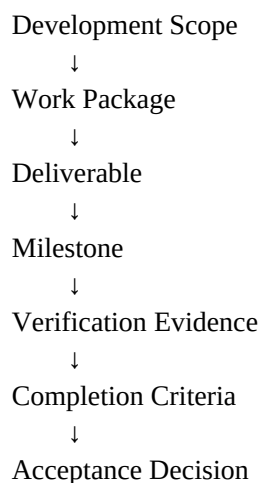

No Work Package, Deliverable, Milestone, or Development Round result may be represented as accepted outside this chain.

Relationship to Section 14

Section 14 establishes the Verification and Reporting Evidence used to assess Development Round results.

Section 15 establishes the Completion and Acceptance Criteria and the governance process through which those results receive a formal decision.

Evidence informs acceptance. Evidence never replaces acceptance.

Accordingly, this section is the governing acceptance standard for Work Packages, Deliverables, Milestones, the Beta Candidate, and final Development Round completion.

16. Expected Outcomes

This section defines the measurable value expected to exist after successful completion and formal acceptance of the Development Round.

Expected Outcomes describe the consequences of the accepted product state. They do not introduce additional Development Scope, Deliverables, Milestones, or Acceptance Criteria.

Collectively, the Expected Outcomes define the product, stakeholder, programme, partnership, and fundraising value created by the completed Development Round.

16.1 Product Outcome

The primary Product Outcome is an accepted **Pilot Operations & Investor Evidence Beta Candidate**.

This outcome confirms that:

the Development Objective has been achieved;

the Minimum Viable Development Scope has been completed;

all Core Work Packages have been completed;

all Minimum Deliverables have been completed;

all mandatory Milestones have been accepted;

the Project Expense, authorization, Operator, evidence, reporting, and Investor Transparency capabilities operate as an integrated product state;

the approved end-to-end operational workflow is demonstrable;

the completed product is supported by sufficient Verification Evidence;

the accepted product version and its limitations are documented.

The resulting product is more mature than the current Alpha because its principal operational and Investor evidence capabilities can be reviewed together through one controlled workflow.

This outcome is a completed Beta Candidate, not a production platform, live investment service, Mainnet system, or operational agricultural Pilot.

16.2 User-visible Outcome

After successful completion, users and reviewers will be able to observe product behaviour that cannot be demonstrated as one complete experience in the current Alpha baseline.

Operator-visible result

An authorized Operator will be able to:

access the relevant Project context;

review applicable workflow and budget information;

initiate and follow the supported Project Expense lifecycle;

perform permitted operational and authorization actions;

associate and review supporting evidence;

observe lifecycle history;

review relevant operational reporting;

identify prohibited or blocked actions through the product.

This creates a coherent Operator experience rather than a collection of disconnected technical foundations or administrative records.

Investor-visible product result

An authorized Investor will be able to review:

permitted Project context;

operational progress;

disclosed Project Expense information;

applicable budget or budget-summary information;

Expense status and lifecycle history;

permitted evidence availability or references;

relevant reports;

clearly differentiated financial and operational states.

The Investor experience will provide controlled transparency rather than unrestricted access or live financial activity.

Reviewer and demonstration result

An authorized external reviewer or demonstration participant will be able to:

access the controlled Beta Candidate environment;

follow the approved demonstration scenario;

observe the Operator and Investor workflows;

inspect resulting product records;

review supporting evidence and reporting;

compare the demonstrated result with the approved Deliverables and Acceptance Criteria;

identify known limitations and non-production boundaries.

The completed product will therefore be reviewable through observable behaviour rather than presentation claims alone.

16.3 Investor-visible Outcome

For prospective investors, venture studios, accelerators, and strategic funders, the completed Development Round will provide a more mature and evidence-supported basis for product evaluation.

The resulting value includes:

a completed and demonstrable Beta Candidate;

an integrated operational workflow;

observable Project Expense controls;

reviewable evidence handling;

controlled Investor Transparency;

documented product and financial boundaries;

verified Deliverables and Milestones;

an auditable implementation and reporting trail;

a clearer distinction between completed product capability and future operational requirements.

This reduces reliance on conceptual descriptions when assessing AgriPartners. Reviewers will be able to evaluate a functioning product state, its governance framework, its evidence, and its known limitations.

The outcome may reduce product-execution uncertainty by showing that the approved Development Objective has been achieved. It does not eliminate commercial, regulatory, operational, funding, agricultural, or execution risk.

It does not imply:
an investment decision;
an agreed valuation;
live Investor participation;
regulated financial activity;
guaranteed returns;
production readiness.

16.4 Grant Programme Outcome

For grant programmes, the Development Round will produce a discrete and verifiable funded outcome.

The programme-level value includes:

a defined Development Objective;
a completed Beta Candidate;
structured Work Packages;
identifiable Deliverables;
measurable Milestones;
documented Verification Evidence;
formal Acceptance Decisions;
traceable use of funds;
disclosed budget variances and contingency use;
a Final Delivery Report;
a controlled demonstration package.

This structure enables a grant programme to assess delivery through completed and accepted results rather than relying on activity reports, expenditure alone, or unsupported statements.

Each funded claim can remain traceable from the Development Objective through the relevant Work Package, Deliverable, Milestone, evidence, criteria, and decision.

The completed Development Round will therefore represent a grant-reportable product milestone suitable for adaptation to different programme formats.

This outcome does not guarantee grant approval, reimbursement, follow-on funding, or acceptance by a particular programme. Each funder retains its own eligibility, reporting, verification, and decision requirements.

16.5 Accelerator Readiness Outcome

For accelerators and venture studios, the completed Beta Candidate will provide a clearer basis for evaluating product maturity, execution discipline, and the project's readiness for structured development support.

The resulting value includes:

a stronger working-product demonstration;

an identifiable progression from Alpha to Beta Candidate;

evidence that the project can define and complete a bounded value milestone;

structured scope and Work Package governance;

measurable completion and acceptance rules;

clearer technical and non-production boundaries;

more reviewable product risks and limitations;

improved readiness for product, business-model, partnership, and fundraising discussions.

The governance and evidence framework may reduce uncertainty about what has been completed and what remains planned.

Accelerator readiness does not imply accelerator acceptance, investment, commercial validation, company incorporation, or readiness for live operations.

16.6 Strategic Partner Outcome

The completed Beta Candidate will provide strategic, technology, ecosystem, implementation, and agricultural partners with a concrete collaboration reference.

Potential partners will be able to review:

the product's operational workflow;

the role of the Operator Workspace;

Project Expense and evidence controls;

Investor Transparency;

reporting and lifecycle visibility;

the approved Estonia-to-Uzbekistan financial boundary;

the role and limitations of NEAR;

the remaining requirements before real operations.

This creates a more precise basis for discussing future collaboration in areas such as:

product implementation;

infrastructure;

security;

NEAR ecosystem support;

reporting and evidence;

agricultural operations;

Operator preparation;

future compliance or financial-provider integration.

The Beta Candidate functions as a collaboration platform for evaluation and planning. It is not evidence that a partner agreement exists, that an agricultural Operator has been approved, or that live integration or deployment has been authorized.

16.7 Fundraising Readiness Outcome

Successful completion of the Development Round will improve AgriPartners' readiness for future fundraising by replacing part of the project's execution narrative with an accepted and demonstrable product result.

The fundraising-readiness value includes:

a stronger product demonstration;

a completed Beta Candidate milestone;

an evidence-backed delivery history;

structured Development Budget governance;

traceable expenditure and Deliverables;

reviewable Work Package and Milestone records;

documented product boundaries;

a clearer due-diligence package;

known risks and limitations presented openly;

a defined relationship between product completion and future Operational Readiness.

This gives future funders a clearer basis for evaluating:

what has already been completed;

how the Development Round was governed;

whether the approved objective was achieved;

what remains outside the completed scope;

what the next independent funding and readiness requirements are.

Development Round completion may strengthen applications for grants, accelerators, strategic partnerships, Corporate Setup support, and future Pilot funding.

It does not guarantee:

additional grants;

accelerator acceptance;

investment;

Corporate Setup financing;

Feedlot Pilot funding;

Hissar Pilot funding;

commercial traction;

a particular valuation;

a successful Pilot.

Outcome Principles

Expected Outcomes describe:

completed value;

demonstrable capability;

verified product maturity;

stakeholder-visible improvement;

readiness for further evaluation.

Expected Outcomes must not describe:

future aspirations as completed results;

marketing ambitions;

financial projections;

guaranteed funding;

guaranteed investment returns;

unimplemented functionality;

production or Operational Readiness;

live Pilot activity.

An Expected Outcome may be claimed only when it is supported by the accepted Beta Candidate and applicable Verification Evidence.

Outcome Traceability

Every Expected Outcome must remain traceable through:

Development Objective

↓

Beta Candidate

↓

Development Scope



Work Packages



Deliverables



Milestones



Accepted Product State



Expected Outcome

No Expected Outcome may be claimed if the accepted product state does not support it.

Relationship to Future Work

The Expected Outcomes improve AgriPartners' readiness to proceed toward:

a separate Operational Readiness Review;

Corporate Setup completion;

Feedlot Pilot preparation;

Hissar Pilot preparation;

future grant and investment applications;

strategic and ecosystem partnership discussions.

They provide product evidence and governance inputs for those future activities.

They do not constitute:

completion of Corporate Setup;

completion of legal, accounting, banking, or compliance readiness;

a successful Operational Readiness Review;

Feedlot Pilot approval;

Hissar Pilot approval;

a Pilot GO decision;

completion of future fundraising.

This section is the official value statement of the Development Round. It defines the measurable product and stakeholder value created by the accepted Beta Candidate while preserving the independent governance of Corporate Setup, Operational Readiness, production deployment, and both Pilot Rounds.

17. Dependencies and Assumptions

This section defines the conditions, resources, systems, and planning premises upon which successful completion of the Development Round depends.

A **Dependency** is a prerequisite or supporting condition required for delivery, verification, or acceptance.

An **Assumption** is a planning premise accepted for the purpose of preparing the Development Round but remaining subject to validation where material.

An Assumption is not evidence and must not be presented as a completed fact.

Collectively, the identified Dependencies and Assumptions define the planning conditions under which the Development Objective is considered achievable.

Dependency Status

Dependencies should be classified as:

Established — already present and supported by the approved baseline;

Required during delivery — must remain available or be satisfied during the Development Round;

External or conditional — depends on a funder, provider, partner, or other external party;

Future-phase dependency — required for Corporate Setup, Operational Readiness, production, or a real Pilot, but not for Beta Candidate completion.

A future-phase dependency must not be treated as a current Development Round blocker unless a specific funding agreement makes it a commencement or payment condition.

Dependency Register

Material Dependencies must be recorded in a controlled Dependency Register.

Each record should identify:

a stable Dependency ID;

title and description;

dependency category;

current status;

affected Work Packages, Deliverables, or Milestones;

responsible owner;

internal or external source;

required condition;

evidence of satisfaction where applicable;

validation or review date;

consequence of failure;

escalation or reassessment requirement.

The Dependency Register is a control record. It does not replace the underlying evidence demonstrating that a Dependency has been satisfied.

17.1 Internal Product Dependencies

The Development Round begins from established product and governance foundations.

Verified Alpha baseline

The Development Round depends on the current verified AgriPartners Alpha platform remaining available as the starting product baseline.

The established baseline includes:

public and demonstration experiences;

Investor, Farmer, and administrative product experiences;

wallet authentication;

reporting and lifecycle visibility;

Treasury and Presentation Mode capabilities;

backend API;

PostgreSQL database;

NEAR Testnet integration;

existing testing and documentation foundations.

This dependency is established through the approved Current Product Baseline in Section 4.

Financial Workflow Foundation

The Development Round depends on the completed Stage 2 Financial Workflow Foundation.

This foundation provides the approved database basis for:

Project financial workflows;

Operator representation and assignment;

fiat-only Operator transfers;

financial states and lifecycle history;

evidence references;

financial-control boundaries.

The Development Round extends this foundation. It does not redefine it.

Project Expense Accounting Foundation

The Development Round depends on the completed Stage 2 Project Expense Accounting Foundation.

This foundation provides:

workflow budgets;

Project Expenses;

Expense categories;
immutable Expense lifecycle events;
evidence references;
derived reservations;
responsibility separation;
concurrency and overspending controls.

The existing foundation must remain consistent and available throughout the Development Round.

Approved product architecture

Delivery depends on preservation of the approved product and financial architecture, including:

AgriPartners OÜ as the future central company and Investor counterparty;
cryptocurrency stopping at the Estonia layer;
fiat-only Uzbekistan-facing financial operations;
Farmer and Uzbekistan Operator roles remaining non-crypto;
NEAR records remaining supplementary to legal, banking, accounting, and reconciliation authority.

A material architectural change would require formal reassessment rather than informal expansion of a Work Package.

Approved governance framework

The Development Round depends on the continued authority of:

the Development Objective;
Beta Candidate definition;
Development Scope;
Work Package portfolio;
Deliverable catalogue;
Development Budget;
Milestone framework;
Verification Evidence framework;
Completion and Acceptance Criteria.

These established elements form the internal governance basis for execution.

17.2 Technical Dependencies

Technical Dependencies are the product capabilities and system conditions required to integrate, verify, and demonstrate the Beta Candidate.

Backend capability

The Development Round depends on the existing backend remaining available as the application service foundation for authentication, profiles, Projects and Deals, reporting, administration, financial workflows, and Project Expense integration.

Frontend capability

The existing browser application must remain available as the user-visible foundation for Operator, Investor, reporting, and demonstration experiences.

Database consistency

The PostgreSQL schema and ordered migration history must remain consistent with the accepted financial and Project Expense foundations.

Database changes must preserve:

workflow ownership;

lifecycle integrity;

evidence relationships;

budget controls;

reservations;

concurrency protection;

historical records.

Authentication and authorization context

The current authentication and role baseline must remain available while the Beta Candidate adds the approved Project Expense authorization capability.

Product roles must remain distinguishable from legal, contractual, corporate, banking, or payment authority.

Workflow integration

The Beta Candidate depends on a consistent relationship among:

Project context;

financial workflow;

workflow budget;

Project Expense;

Expense lifecycle;

evidence;

Operator actions;

reporting;

Investor disclosure.

Failure of this relationship would prevent the integrated Beta Candidate outcome even if individual components existed separately.

Reporting and evidence context

The reporting and evidence capabilities depend on accurate source records, consistent lifecycle semantics, and role-appropriate disclosure.

Reports and product records must preserve distinctions among projected, recorded, approved, paid, reconciled, and completed states.

Controlled deployment capability

The accepted Beta Candidate depends on a controlled environment in which the approved version and end-to-end scenario can be reviewed.

This is a development and demonstration dependency, not a production infrastructure dependency.

17.3 Infrastructure Dependencies

The Development Round requires sufficient infrastructure to support development, verification, documentation, and controlled demonstration.

Required infrastructure may include:

development environments;

source repository availability;

branch and Pull Request workflows;

testing environments;

safe disposable database verification;

build and deployment tooling;

controlled demonstration hosting;

test or demonstration databases;

access control for review environments;

documentation storage;

Evidence Register storage;

logs and monitoring appropriate to Beta verification;

backup or retention of required evidence.

Infrastructure must support:

reproducible product review;

version identification;

evidence preservation;

authorized reviewer access;

protection of credentials and sensitive data.

The Development Round does not depend on production banking, production payment infrastructure, production custody, Mainnet operation, or live agricultural infrastructure.

A temporary provider interruption may delay affected verification or demonstration activity without redefining the Development Objective or completed Scope.

17.4 Funding Dependencies

Successful completion depends on sufficient financing for the full approved Minimum Viable Development Scope.

Availability of the Development Budget

The principal funding dependency is availability of the approved **USD 40,000 Development Budget** or a legally committed financing structure sufficient to complete the full Beta Candidate.

The Development Round must not rely on an uncommitted future funding gap.

Agreed funding mechanism

Before commencement, the applicable funding mechanism must be sufficiently defined, including:

single-tranche or multi-tranche structure;

eligible expenditure;

reporting requirements;

payment conditions;

commencement conditions;

currency and payment process;

any permitted budget variance;

any funder approval requirements.

Multi-tranche funding

Where funding is released by Milestone, the full financing commitment and tranche conditions must preserve the ability to complete the approved Core Scope.

A completed early tranche must not create an unfunded obligation to complete the entire Beta Candidate.

Delayed funding

Where committed funding is delayed, commencement or continued delivery may be adjusted. Unfunded work is not assumed.

Funding delay does not reduce the approved Scope or allow an incomplete result to be represented as complete.

Partial funding

Partial funding is not sufficient for the complete Development Round unless:

the remaining capital is legally committed; or

a separately approved, independently valuable funding phase is defined before expenditure begins.

Funder compliance

Completion also depends on compliance with applicable funder requirements, including:

cost eligibility;

reporting;

procurement where applicable;

evidence access;

Milestone review;

payment conditions.

A funder-specific requirement may change the format of the funding request or reporting package. It must not silently redefine the Development Objective or Beta Candidate.

17.5 External Dependencies

NEAR Ecosystem Dependencies

The current platform uses NEAR Testnet for wallet-linked Alpha workflows, smart-contract experimentation, selected references, and demonstration capabilities.

Relevant Development Round Dependencies may include:

NEAR Testnet availability;

wallet and access-key functionality;

supported wallet tooling;

relevant NEAR development libraries;

Testnet account and transaction availability;

ecosystem documentation and tooling.

The Beta Candidate does not require NEAR Mainnet operation.

Uzbekistan-facing Operator and Farmer financial workflows must not depend on NEAR, cryptocurrency, wallets, tokens, or on-chain actions.

A temporary Testnet or wallet-provider interruption may affect verification of the retained Testnet capabilities. It must not redefine the fiat-only product boundary or convert Mainnet operation into Development Scope.

No NEAR ecosystem grant, partnership, endorsement, or future technical support is assumed unless formally confirmed.

Estonia-related Dependencies

AgriPartners OÜ is part of the approved future corporate and financial architecture.

The Development Round's technical product objective does not inherently require completion of Estonian incorporation before product development can occur.

Estonia-related conditions may become external Dependencies where a specific funder requires:

a registered legal entity before signing;

an eligible corporate recipient before payment;

an Estonian account or corporate representation;

company documentation before commencement.

Such requirements must be confirmed for each funder rather than assumed universally.

Corporate Setup Dependencies

Corporate Setup is governed separately from the USD 40,000 Development Budget.

AgriPartners may apply as a founder or team where the relevant programme permits application before incorporation.

Where company registration is required after conditional approval but before agreement or payment, the dependency sequence may be:

Founder or Team Application



Conditional Approval or Equivalent Decision



Corporate Setup Funding



AgriPartners OÜ Registration



Funding Agreement



Development Funding

Corporate Setup is expected to be required for later corporate contracting, banking, KYB, Operational Readiness, and real Pilot operations.

It is not a technical prerequisite for building the Beta Candidate and is not a prerequisite for every founder-first application.

Corporate Setup must not be represented as completed until the relevant legal and administrative evidence exists.

External Provider Dependencies

The Development Round may depend on third-party services such as:

repository hosting;

development tooling;

application hosting;

database hosting;

domain or certificate services;

wallet tooling;

documentation services;

monitoring or logging services;

specialist QA, security, accessibility, or product review.

Provider availability does not guarantee successful delivery. Material provider changes, service discontinuation, pricing changes, or access restrictions may require reassessment.

No specific provider relationship should be presented as secured unless supported by an agreement or active service record.

Feedlot Operator Dependencies

The Beta Candidate uses approved agricultural workflow and demonstration context but does not require commencement of real Feedlot operations.

Development may rely on:

approved Feedlot model documentation;

controlled demonstration data;

established operational categories;

available domain input where formally included.

A real Uzbekistan Feedlot Operator, executed Operator agreement, live bank transfer, livestock acquisition, or operational agricultural activity is not required for Beta Candidate completion unless a formally approved scope revision states otherwise.

Operator identity, contractual authority, operational capacity, and Pilot readiness remain future-phase Dependencies for Operational Readiness and the real Feedlot Pilot.

The same principle applies to the future Hissar Pilot.

17.6 Assumptions Requiring Validation

The following planning Assumptions support Development Round preparation but remain subject to confirmation.

Funding assumption

It is assumed that the complete USD 40,000 Development Budget will be secured or legally committed before AgriPartners undertakes the full delivery obligation.

This is not evidence that funding has been obtained.

Funder eligibility assumption

It is assumed that the selected funder can support the approved product-development purpose and that the final budget can be adapted to its eligible-cost rules without invalidating Core Scope.

This must be validated for each funding source.

Corporate Setup timing assumption

It is assumed that at least some founder-first funding sources will permit application before AgriPartners OÜ is registered and will require incorporation only before agreement, payment, or implementation.

This must be confirmed through the rules and written guidance of each programme.

Product baseline assumption

It is assumed that the verified current baseline remains available and does not undergo an unapproved material architectural change before Development Round commencement.

Any material change requires a baseline and scope reassessment.

Delivery-capacity assumption

It is assumed that suitable product, engineering, QA, security, documentation, and specialist capacity can be engaged under the approved budget and funding conditions.

No specific contractor or provider is assumed to be committed without supporting evidence.

Infrastructure assumption

It is assumed that appropriate repository, development, testing, deployment, and documentation infrastructure will remain available on commercially and operationally reasonable terms.

Demonstration-data assumption

It is assumed that controlled demonstration data can support the approved end-to-end scenario without requiring live Investor funds, personal data, real agricultural expenditure, or production payment activity.

NEAR Testnet assumption

It is assumed that NEAR Testnet and the necessary supporting tooling remain sufficiently available for the retained Testnet demonstration capabilities.

This assumption does not extend to Mainnet.

Operational Readiness assumption

It is assumed that the completed Beta Candidate may become eligible for a separate Operational Readiness Review.

It is not assumed that the review will produce a GO decision.

Corporate and partner participation assumption

It is assumed that future Corporate Setup, service-provider relationships, Operator participation, legal preparation, and financial infrastructure may be pursued through separate governance and funding.

None is assumed completed or contractually secured.

Pilot funding assumption

It is assumed that Feedlot and Hissar Pilot funding will be pursued separately.

Development Round completion does not establish that either Pilot will be financed or approved.

Dependency Principles

Dependencies:

identify conditions required for successful delivery, verification, or acceptance;

must remain visible and attributable;

must have an identifiable status;

must be reassessed when materially changed;

may affect one or more Work Packages, Deliverables, or Milestones.

Dependencies do not:

guarantee successful delivery;

prove that implementation occurred;

substitute for Verification Evidence;

replace Acceptance Criteria;

establish Corporate Setup;

establish Operational Readiness;

guarantee funding, provider support, or partner participation.

A Dependency is considered satisfied only when appropriate evidence confirms the required condition.

Assumption Principles

Assumptions:

support planning;

reduce unnecessary repetition;

remain explicitly identifiable;

must not be presented as verified facts;

require validation where material;

must identify the consequence of invalidation where relevant.

If a material Assumption is invalidated, the affected Work Packages, Deliverables, Milestones, budget, schedule, and risks must be reassessed through the applicable governance process.

An invalidated Assumption must not be concealed through scope relabelling or unsupported completion claims.

Dependency Traceability

Dependencies must remain traceable through:

Development Objective



Beta Candidate



Development Scope



Work Package



Dependency



Verification Evidence



Acceptance

Dependencies support delivery. They do not replace delivery.

Relationship to Risks

Dependencies and risks are related but distinct.

Dependencies identify required conditions.

Risks evaluate uncertainty, likelihood, impact, and controls associated with possible events or failures.

A Dependency is not automatically a risk.

Failure, delay, degradation, or invalidation of a critical Dependency may create or increase a Development Round risk. Such risk must be assessed under Section 18 — Risks and Controls.

This section is the governing Dependency and Assumption framework for the Development Round. It distinguishes established foundations, active delivery conditions, external dependencies, and planning assumptions without presenting any of them as evidence of completion, Corporate Setup, Operational Readiness, Pilot approval, or future funding success.

18. Risks and Controls

This section establishes the official Risk Management Framework of the Development Round.

A **Risk** is an uncertain event or condition that may affect delivery, verification, acceptance, or appropriate future use of the Development Round results.

A **Control** is a preventive, detective, corrective, or governance measure intended to reduce the likelihood or impact of a Risk.

Controls reduce risk. They do not guarantee that a Risk has been eliminated.

Collectively, the identified Risks, Controls, escalation rules, and Residual Risk requirements define the complete Risk Management Framework supporting the Development Round.

Risk Classification

Risks must remain distinguishable from related governance concepts:

a **Dependency** is a required condition;

a **Risk** is uncertainty concerning a possible event or condition;

an **Issue** is a Risk or other condition that has occurred and requires action;

a **Known Limitation** is a present and documented constraint;

a **Control** is a measure intended to reduce Risk;

Residual Risk is the Risk remaining after applicable Controls.

A failed or delayed Dependency may cause a Risk to materialize as an Issue. It does not change the definitions.

Risk Assessment

Each material Risk should be assessed using documented qualitative or funder-approved criteria.

Likelihood

Likelihood may be classified as:

Low;

Medium;

High.

Impact

Impact may be classified as:

Low;

Medium;

High;

Critical.

Impact should consider possible effects on:

Minimum Scope;

Core Work Packages;

Deliverables;

Milestones;

budget;

schedule;

evidence sufficiency;

security;

acceptance;

non-production boundaries;

external reporting.

Risk classification must reflect current evidence and may change as delivery progresses.

Risk Register

All material Risks must be recorded in a controlled Risk Register.

Each Risk record should include:

stable Risk ID;

title and description;

category;

source or related Dependency;

affected Work Packages, Deliverables, or Milestones;

likelihood;

impact;

overall priority;

current status;

preventive Controls;

detective Controls;

corrective or contingency response;

Control owner;

Risk owner;

review date;

evidence supporting the assessment;

Residual Risk;

escalation threshold;

escalation status;

closure or acceptance decision where applicable.

Approved Risk statuses should distinguish among:

Identified;

Under Assessment;

Monitoring;

Mitigation in Progress;

Escalated;

Realized as an Issue;

Closed;

Accepted as Residual Risk.

The Risk Register supports governance, traceability, and review. It does not replace the evidence supporting the Risk assessment, Control operation, mitigation result, or Residual Risk decision.

Risk identifiers must remain stable throughout planning, delivery, verification, reporting, acceptance, and subsequent funder review.

18.1 Scope Risk

Risk

Scope Risk may arise when:

unapproved functionality is introduced;

Recommended or Optional work displaces Core work;

a funder or stakeholder requests additional functionality without approving the corresponding change;

existing Scope is substituted with easier but less valuable outputs;

Work Packages expand informally;

mandatory capabilities remain incomplete;

implementation activity is mistaken for completed Scope.

Uncontrolled Scope growth may consume budget and delivery capacity without producing the approved Beta Candidate.

Controls

Scope Risk is controlled through:

the governing Development Objective;

the approved Beta Candidate definition;

Minimum, Recommended, and Optional Scope classifications;

the approved Work Package portfolio;

unique Deliverable identifiers;

formal change control;

Optional Scope Activation Rules;

Deliverable and Milestone traceability;

Completion and Acceptance Criteria;

prohibition of informal scope expansion.

Core Work Packages and Minimum Deliverables retain priority over all Recommended and Optional work.

A material Scope change requires documented impact assessment, formal approval, traceability updates, and any required funder approval.

Scope Risk remains open until the Minimum Scope has been completed and accepted.

18.2 Budget Risk

Risk

Budget Risk may arise from:

insufficient funding;

underestimated Core work;

cost increases;

budget overrun;

contingency exhaustion;

ineligible expenditure;

uncontrolled reallocation;

duplicate charging;

spending outside approved Scope;

cross-subsidisation of Corporate Setup or Pilot activity;

expenditure without a Deliverable relationship.

Budget failure may prevent completion even where technical progress has occurred.

Controls

Budget Risk is controlled through:

the fixed USD 40,000 Development Budget;

Work Package allocations;

internal cost categories;

dual expenditure classification;

Minimum Scope protection;

controlled contingency;

approved reallocation rules;

Section 11 eligibility requirements;

Section 12 exclusions;

financial records and variance reporting;

no-cross-subsidisation rules;

partial-funding restrictions.

Contingency use must identify the protected Work Package, Deliverable, and Milestone. It must not be used to conceal overruns or finance unrelated activity.

Verified savings must follow the approved reallocation priority and cannot weaken Core delivery.

18.3 Schedule Risk

Risk

Schedule Risk may arise from:

delayed funding;

delayed commencement;

implementation delay;

unexpected integration work;

provider interruption;

specialist unavailability;

delayed reviews;

delayed evidence collection;

Milestone slippage;

delayed funder decisions or tranche release.

Schedule Risk affects delivery timing. It does not change what constitutes completion.

Controls

Schedule Risk is controlled through:

dependency-aware Work Package sequencing;

permitted parallel execution where dependencies remain protected;

early identification of blocking conditions;

Milestone-based progress assessment;

explicit status reporting;

delayed-funding provisions;

reassessment when a material Assumption becomes invalid;

escalation of critical delays;

controlled adjustment of planning dates where necessary.

The governing principle is:

No Schedule Overrides Completion, Verification, Acceptance, or Operational Readiness.

A deadline, launch date, presentation, funding window, or stakeholder expectation must not cause an incomplete result to be represented as complete.

Where delay threatens the Beta Candidate, governance may pause, resequence, or formally reassess delivery. It must not silently weaken the approved Scope or Acceptance Criteria.

18.4 Technical Risk

Risk

Technical Risk may arise from:

integration complexity;

regression in existing capabilities;

authorization defects;

inconsistent role behaviour;

data-integrity failures;

Project or workflow misassociation;

lifecycle inconsistency;

evidence-linkage defects;

budget or reservation-control failure;

reporting inconsistency;

deployment failure;

environment differences;

incompatibility with the current baseline.

A technically present feature may still fail to produce the integrated Beta Candidate.

Controls

Technical Risk is controlled through:

accepted architecture and financial boundaries;

stable current baseline;

Work Package decomposition;

dependency-aware integration;

preservation of existing database invariants;

automated and manual verification;

integration and regression testing;

negative-path testing;

financial-control testing;

controlled deployment verification;

version-specific evidence;

defect tracking and closure verification;

formal architecture and Scope change governance.

Technical Controls must protect the complete workflow rather than only isolated components.

A passing test suite does not eliminate Technical Risk outside the tested scope. Residual uncertainty must remain documented.

18.5 Security Risk

Risk

Beta-level product Security Risk may arise from:

unauthorized access;

privilege escalation;

incorrect role assignment;

bypass of authorization controls;

exposure of restricted Investor, Operator, Expense, or evidence information;

insecure token handling;

leaked credentials or secrets;

insecure configuration;

dependency vulnerabilities;

insufficient environment access control;

disclosure of sensitive security evidence;

public-repository exposure of private keys, seed phrases, tokens, or .env data.

Controls

Security Risk is controlled through:

authentication and authorization review;

role-boundary verification;

prohibited-action tests;

data-exposure review;

evidence-access review;

configuration review;

dependency review where applicable;

controlled demonstration access;

secret-handling rules;

prohibition on publishing secrets in the public repository;

Security Findings Register;

remediation and retesting;

documented accepted limitations;

Beta-level security closure decision.

No unresolved critical security issue may be accepted where it invalidates the Beta Candidate or controlled review environment.

This Risk framework addresses Beta-level product security. It does not constitute:

an independent external security audit;

production certification;

Mainnet audit;

custody approval;

regulatory approval;

Operational Readiness.

18.6 External Dependency Risk

Risk

External Dependency Risk may arise from:

NEAR Testnet interruption or change;

wallet-provider interruption;

hosting-provider outage;

repository-service unavailability;

database or deployment-provider changes;

documentation-tool interruption;

third-party price changes;

external specialist unavailability;
third-party service discontinuation;
changes to access or usage conditions.

The Development Round cannot fully control external providers.

Controls

External Dependency Risk is controlled through:

identification in the Dependency and Risk Registers;
provider-status monitoring where proportionate;
version and configuration records;
preservation of source and evidence;
controlled backups;
alternative provider or local verification options where practical;
limited reliance on non-essential third-party functionality;
reassessment following material provider change;
documentation of external interruptions;
formal escalation where a critical provider affects Milestone completion.

The Beta Candidate does not require NEAR Mainnet.

Uzbekistan-facing Operator and Farmer financial workflows must remain fiat-only and must not acquire a new crypto or wallet dependency as a response to an external provider issue.

18.7 Demonstration Risk

Risk

Demonstration Risk may arise when:

the review environment is unavailable;
the deployed version differs from the accepted version;
demonstration data is incomplete or misleading;
the scenario is not repeatable;
access instructions are unclear;
a reviewer cannot complete the intended journey;
presentation materials obscure missing functionality;
demonstration records are mistaken for live operations;

known limitations are hidden;

evidence cannot be traced to demonstrated behaviour.

A demonstration failure may reduce external confidence even where parts of the product are complete.

Controls

Demonstration Risk is controlled through:

an approved demonstration scenario;

controlled and clearly labelled data;

deployed-version identification;

environment verification;

access verification;

reviewer guidance;

known-limitations disclosure;

resulting product and system records;

repeat-run evidence where required;

evidence traceability;

separation between observable product behaviour and presentation materials;

prohibition on representing demonstration records as real investment or Pilot activity.

A video, screenshot, slide, or scripted explanation must not substitute for required observable product behaviour.

18.8 Funding Continuity Risk

Risk

Funding Continuity Risk may arise from:

funding withdrawal;

delayed payment;

delayed tranche release;

discretionary release conditions;

changing grant requirements;

ineligible-cost determinations;

currency or payment restrictions;

insufficient partial funding;

dependence on an uncommitted follow-on source;

inability to finance remaining Core Scope.

This Risk is particularly material because spending an insufficient initial amount may create incomplete outputs without producing the Beta Candidate.

Controls

Funding Continuity Risk is controlled through:

full-funding or legally committed financing requirements;

clear commencement conditions;

documented tranche conditions;

milestone-linked release structure where applicable;

eligibility confirmation;

delayed-funding provisions;

no obligation to perform unfunded work;

partial-funding restrictions;

independently valuable preliminary phases only where formally approved;

preservation of Minimum Scope;

formal reassessment if funding conditions change.

Partial funding must not create an obligation to complete an unfunded Development Scope.

AgriPartners must not begin the full Development Round merely on the assumption that the remaining funding gap will later be filled.

If committed funding is interrupted, governance must determine whether delivery should pause, whether a contractually funded phase can be completed independently, or whether formal restructuring is required.

18.9 Claims and Positioning Risk

Risk

Claims and Positioning Risk may arise from:

overstating product maturity;

presenting planned functionality as implemented;

presenting Beta Candidate acceptance as production readiness;

implying Operational Readiness;

implying Mainnet readiness;

presenting the platform as a regulated financial service;

implying live investment or custody;
presenting demonstration data as real operations;
presenting projected returns as verified or guaranteed;
implying Corporate Setup completion;
implying Feedlot or Hissar Pilot approval;
implying endorsement, partnership, grant approval, or investment commitment without evidence.
Unsupported claims may damage credibility, mislead funders, and create legal or reputational exposure.

Controls

Claims and Positioning Risk is controlled through:

approved terminology;
frozen Development Objective and Beta Candidate definition;
verified Current Product Baseline;
explicit non-production boundaries;
Use of Funds and Excluded Costs;
Verification Evidence requirements;
Acceptance Governance;
known-limitations disclosure;
content review against repository evidence;
distinction between Alpha, Beta Candidate, Operational Readiness, and production;
distinction between projected, recorded, paid, reconciled, and verified returns;
prohibition on unsupported partnership, funding, and traction claims.

Approved external positioning must state only what the accepted evidence supports.

Adaptation for a funder may change emphasis, length, or terminology required by that programme. It must not change the underlying facts or maturity status.

18.10 Mitigation and Escalation Principles

Risk management must follow the following principles.

Early identification

Material Risks should be identified before they prevent delivery or invalidate evidence.

Proportional response

Controls should be proportionate to likelihood, impact, cost, Development Scope, and Beta-level context.

Clear ownership

Every material Risk and Control must have an identifiable owner.

Evidence-based assessment

Likelihood, impact, Control effectiveness, and Residual Risk should be supported by available evidence and professional judgment.

Continuous reassessment

Risks must be reassessed when:

- a material Dependency changes;
- an Assumption is invalidated;
- a Work Package changes status;
- a Milestone review occurs;
- a significant defect or security finding appears;
- funding conditions change;
- an external provider changes;
- new evidence affects the assessment.

Transparent reporting

Material Risks, realized Issues, failed Controls, and Residual Risks must remain visible in Work Package evidence, Milestone reporting, and the Final Delivery Report where relevant.

Escalation

A Risk should be escalated when it may materially affect:

- the Development Objective;
- Minimum Scope;
- a Core Work Package;
- a Minimum Deliverable;
- a mandatory Milestone;
- budget sufficiency;
- funding continuity;
- security;
- evidence sufficiency;
- acceptance;
- approved product or financial boundaries.

Escalation may result in:

additional review;

Control strengthening;

contingency use;

Work Package resequencing;

delivery pause;

funder notification;

formal Scope or budget change request;

decision not to proceed.

Escalation does not imply project failure. It is a normal governance response to material uncertainty.

No unsupported closure

A Risk must not be closed solely because:

no incident has yet occurred;

the scheduled date has arrived;

related work was performed;

a Control was designed;

a report was submitted.

Closure requires evidence that the Risk is no longer applicable, has been resolved, or has been formally accepted as Residual Risk.

Residual Risk

Some Risk remains after Controls are applied.

Residual Risk must:

be identified;

be assessed;

be documented;

remain linked to the original Risk;

identify applicable Controls;

remain visible during verification and acceptance;

have an approved disposition where material.

Residual Risk is not automatically unacceptable.

It may be accepted where:

the Development Objective remains achievable;

Minimum Deliverables remain valid;

mandatory security and authorization boundaries remain protected;

the end-to-end workflow remains demonstrable;

the Risk is consistent with Beta-level positioning;

the limitation is disclosed;

the authorized authority approves the residual position.

Residual Risk is unacceptable where it invalidates the Beta Candidate, conceals incomplete Core Scope, creates an unresolved critical security condition, or makes external positioning materially misleading.

Acceptance of Residual Risk for the Beta Candidate does not mean that the same Risk is acceptable for Operational Readiness, production, Mainnet, custody, or real Pilot operations.

Risk Traceability

Every material Risk must remain traceable through:

Development Objective



Development Scope



Work Package



Dependency



Risk



Control



Residual Risk



Verification Evidence



Acceptance Decision

A Risk or Control must not be represented as evidence that a Deliverable or Milestone has been completed.

Relationship to Operational Readiness

Development Round Risk Management supports completion and acceptance of the Beta Candidate.

It does not replace:

corporate risk management;

legal or regulatory risk assessment;

production security assessment;

banking or payment-provider risk assessment;

agricultural operational risk assessment;

livestock and biosecurity risk management;

Feedlot Pilot risk assessment;

Hissar Pilot risk assessment;

Operational Readiness Review.

Risks acceptable within a controlled Beta environment may be unacceptable for live financial or agricultural operations.

This section is the governing Risk Management Framework for the Development Round. It ensures that material uncertainty is identified, assessed, controlled, documented, escalated, and reflected in Verification and Acceptance without being misrepresented as evidence of completion or a guarantee of success.

19. Relationship to Operational Readiness

This section establishes the official governance boundary between successful completion of the Development Round and authorization to begin real-world Pilot operations.

Successful completion of the Development Round confirms only that:

the Development Objective has been achieved;

the Pilot Operations & Investor Evidence Beta Candidate has been accepted;

the approved product milestone has been completed.

It does not establish Corporate, Legal, Financial, Operator, Funding, or Operational Readiness and does not authorize commencement of a Feedlot or Hissar Pilot.

Collectively, the requirements in this section define the governance transition from accepted product completion to a separate Operational Readiness decision.

19.1 Development Completion vs Operational Readiness

Development Completion and **Operational Readiness** are separate project states governed by separate decisions.

Development Completion confirms that:

the approved product has been delivered;

Core Work Packages are complete;

Minimum Deliverables are complete;

mandatory Milestones are accepted;

required Verification Evidence exists;

the Beta Candidate satisfies the applicable Completion and Acceptance Criteria.

Operational Readiness determines whether AgriPartners has the organizational, corporate, legal, financial, security, funding, Operator, and operational capability required to begin a real Pilot.

Development Completion answers:

Has the approved product milestone been completed and accepted?

Operational Readiness answers:

Is AgriPartners prepared and authorized to use the product within a real, funded, legally structured, and controlled Pilot operation?

A positive Development Completion decision is necessary for the intended Pilot pathway, but it is not sufficient for Pilot authorization.

Operational Readiness must not be inferred from:

completed software;

a successful demonstration;

passing tests;

accepted Development Milestones;

grant completion;

product documentation;

available Pilot Capital;

an interested Investor;

an interested Operator;

a planned Pilot date.

19.2 Beta Candidate Handoff

After final Development Round acceptance, the accepted Beta Candidate becomes an input to the Operational Readiness Review.

The handoff package should include:

accepted Beta Candidate version and baseline;

Final Delivery Report;

Verification Evidence index;

Acceptance Records;

accepted Milestone packages;

Deliverable Traceability Record;

product and technical documentation;

Operator and reviewer guidance;
release record;
Known Limitations Register;
Risk Register;
Residual Risk records;
security validation evidence;
controlled deployment evidence;
demonstration scenario and results;
unresolved issues and approved exceptions;
non-production boundary statement.

The handoff establishes what product capability is available for readiness evaluation. It does not represent an Operational Readiness decision.

Operational Readiness reviewers may:

rely on accepted Development Round evidence where it remains applicable;
request clarification;
require updated evidence;
identify additional readiness requirements;
require remediation before Pilot authorization;
determine that a Beta-acceptable limitation is unacceptable for real operations.

Where new evidence shows that an accepted product capability no longer satisfies its original Acceptance Criteria, the applicable acceptance decision may be reopened under Section 15.

Otherwise, a readiness finding does not rewrite the historical Development Round result. It determines whether the accepted product can proceed into real operations under current conditions.

19.3 Operational Readiness Review

The Operational Readiness Review is an evidence-based evaluation of whether AgriPartners is prepared to begin the proposed real Pilot safely, legally, financially, and operationally.

At minimum, the Review must evaluate the following domains.

Product Readiness

Product Readiness should confirm that:

the accepted Beta Candidate remains identifiable;
required Pilot-facing capabilities remain available;

material Known Limitations are understood;
product evidence remains applicable;
any additional controls required for real operations have been addressed;
no unresolved product issue prevents Pilot use.

Corporate Readiness

Corporate Readiness should evaluate:

establishment of the required legal entity;
corporate authority;
governance and decision-making authority;
authorized representatives;
corporate records;
capacity to enter into relevant agreements;
applicable KYB readiness.

Legal Readiness

Legal Readiness should evaluate:

applicable legal and regulatory advice;
Investor-facing agreements;
Operator agreements;
Pilot or Farm agreements;
supplier and service-provider agreements where required;
governing law and dispute provisions;
data-protection and disclosure requirements;
authority, signature, and execution evidence;
restrictions affecting investment, payments, cryptoassets, or agricultural operations.
Repository templates or drafts do not establish Legal Readiness unless appropriately reviewed and executed.

Financial Readiness

Financial Readiness should evaluate:

approved bank or payment infrastructure;
accounting and reconciliation arrangements;
treasury controls;

segregation of funds;

payment authority;

fiat disbursement and return procedures;

Investor settlement procedures where applicable;

the Estonia-to-Uzbekistan financial boundary;

evidence that cryptocurrency stops at AgriPartners OÜ;

confirmation that Uzbekistan-facing financial activity remains fiat-only.

Operator Readiness

Operator Readiness should evaluate:

identity of the proposed Uzbekistan Feedlot Operator;

legal and operational authority;

executed agreements;

operational competence;

personnel and responsibility assignments;

facilities and agricultural capacity;

reporting and evidence capability;

financial-control capability;

understanding of the fiat-only operating model;

ability to use the approved product workflow.

The Operator must not be required to receive cryptocurrency, use a crypto wallet, hold tokens, interact with a smart contract, or perform an on-chain financial action.

Funding Readiness

Funding Readiness should evaluate:

whether the complete applicable Pilot Capital is available or legally committed;

conditions attached to the funding;

payment and disbursement timing;

contingency requirements;

restrictions on use of funds;

ability to complete the Pilot without relying on an unsecured future funding gap;

separation of Pilot Capital from Development and Corporate Setup funds.

Partial funding must not authorize a Pilot where failure to secure the remaining capital could strand earlier expenditure or prevent Pilot completion.

Additional readiness domains

The governance process may introduce additional domains where relevant, including:

production security;

data and evidence governance;

agricultural and livestock readiness;

biosecurity;

insurance;

emergency procedures;

supplier readiness;

facility readiness;

monitoring;

incident response;

business continuity.

Introducing an additional readiness domain does not change the completed Development Objective. It reflects the broader requirements of real operations.

19.4 Operational Readiness Board

The Operational Readiness Board is the governance body responsible for reviewing the Operational Readiness evidence and issuing the formal Pilot readiness decision.

The Board should be constituted by the appropriate AgriPartners governance authority or its designated decision-makers.

Its structure may evolve as AgriPartners develops. This Funding Package therefore does not assign fixed future corporate titles.

The applicable governance record should define:

Board mandate;

decision scope;

required evidence;

participating decision-makers;

subject-matter input where required;

conflict-of-interest treatment;

decision method;

quorum or equivalent participation requirement where applicable;

decision record;

conditions and follow-up requirements;

reassessment triggers.

The Board must assess the complete readiness position rather than relying solely on product completion or the recommendation of one participant.

The Board's authority is governance-neutral but must be explicit, documented, and appropriate to the decision being made.

A separate readiness decision should be made for each Pilot. A GO decision for the Feedlot Pilot does not automatically authorize the Hissar Pilot, and a decision concerning one Operator, site, funding structure, or agreement set does not automatically apply to another.

19.5 GO / CONDITIONAL GO / NO-GO Boundary

The Operational Readiness Board may issue only one of the following decisions.

GO

A GO decision confirms that:

all mandatory readiness conditions are satisfied;

required evidence is sufficient;

critical risks are controlled;

complete Pilot Capital is available or legally committed;

required corporate and legal arrangements are effective;

the Operator and operational environment are ready;

no unresolved condition prohibits Pilot commencement.

Only an explicit GO decision authorizes commencement of the approved real Pilot, subject to any continuing controls stated in the decision.

CONDITIONAL GO

A CONDITIONAL GO decision confirms that the proposed Pilot may continue through approved preparation activities while one or more clearly defined readiness conditions remain open.

The decision must identify:

each open condition;

responsible owner;

required evidence;

completion requirement;

review authority;

consequence of non-completion.

A CONDITIONAL GO does not authorize:

live Investor capital intake;

transfer of Pilot Capital to the Operator;

livestock acquisition;

commencement of agricultural operations;

production settlement;

any other activity reserved for GO status.

Pilot operations may begin only after all required conditions are satisfied and the Board formally converts or replaces the decision with GO.

NO-GO

A NO-GO decision confirms that one or more critical readiness conditions remain unsatisfied.

Under NO-GO:

Pilot commencement is prohibited;

Pilot Capital must not be deployed for operations;

livestock must not be acquired;

Operator funding must not begin;

the project must address the identified blockers before seeking reassessment.

NO-GO is a governance control, not necessarily termination of the project. The decision should identify whether remediation and future reassessment remain possible.

Development Round completion never determines GO by itself.

A GO decision remains subject to reassessment if material conditions change before or during Pilot commencement.

19.6 No Schedule Overrides Readiness

The governing principle is:

No Schedule Overrides Readiness.

No planned date or external expectation may override mandatory Operational Readiness criteria.

This includes:

grant deadlines;

grant Milestones;

tranche dates;

Investor expectations;

partner expectations;
marketing events;
public announcements;
presentations;
conferences;
ecosystem events;
livestock-purchase opportunities;
seasonal pressure;
expiring commercial offers;
internal target dates.

If mandatory readiness conditions have not been satisfied, the Pilot must not begin.

A delay is preferable to commencing a Pilot without adequate corporate, legal, financial, security, funding, Operator, or operational readiness.

No schedule, funding pressure, or public commitment may convert:

NO-GO into GO;

CONDITIONAL GO into GO;

missing evidence into satisfied evidence;

incomplete funding into Funding Readiness;

an unresolved critical Risk into an acceptable condition.

19.7 Conditions Preventing Pilot Launch

The following non-exhaustive conditions may prevent Pilot commencement:

AgriPartners OÜ or another required corporate structure is not established;

required corporate authority is absent;

KYB requirements are incomplete;

legal or regulatory readiness is unresolved;

required legal advice has not been obtained;

required agreements are incomplete, unreviewed, unsigned, or ineffective;

the proposed Uzbekistan Operator has not been verified or approved;

Operator authority or operational capability is insufficient;

required facilities are unavailable or unsuitable;

agricultural, veterinary, biosecurity, insurance, or emergency requirements are unresolved;
complete Pilot Capital is neither available nor legally committed;
funding conditions make complete Pilot execution uncertain;
banking or payment infrastructure is unavailable;
fiat disbursement and reconciliation procedures are incomplete;
the Estonia-to-Uzbekistan fiat boundary cannot be maintained;
an Uzbekistan-facing workflow requires cryptocurrency or a crypto wallet;
an unresolved critical security issue exists;
an unresolved critical Operational Risk exists;
required production controls are absent;
required evidence is missing or unreliable;
the Operational Readiness Review is incomplete;
the Board has issued CONDITIONAL GO with unresolved conditions;
the Board has issued NO-GO;
a previous GO decision has been suspended following material change.

Any one critical condition may be sufficient to prevent Pilot commencement.

The absence of a listed condition does not automatically establish readiness. GO requires affirmative evidence that all applicable mandatory conditions are satisfied.

Operational Readiness Principles

Operational Readiness:

evaluates organizational capability;
evaluates corporate capability;
evaluates legal capability;
evaluates financial capability;
evaluates product and security capability;
evaluates funding capability;
evaluates Operator capability;
evaluates real operational capability;
relies on current and applicable evidence;

requires a documented governance decision.

Operational Readiness does not evaluate software alone.

Product acceptance, Corporate Setup, available Pilot Capital, an executed agreement, or an identified Operator may each be necessary, but no single factor independently establishes Operational Readiness.

Operational Readiness Traceability

The transition to a real Pilot must remain traceable through:

Development Objective



Accepted Beta Candidate



Verification and Acceptance Records



Beta Candidate Handoff



Operational Readiness Review



Operational Readiness Board



GO / CONDITIONAL GO / NO-GO



Approved Feedlot or Hissar Pilot

No Pilot may bypass this chain.

Relationship to Future Work

Successful Operational Readiness and an explicit GO decision are required before:

deployment of Feedlot or Hissar Pilot Capital;

Operator funding;

livestock acquisition;

commencement of agricultural operations;

live Investor funding activity where applicable;

production payment or settlement activity;

representation of the Pilot as operational.

Corporate Setup, Legal Readiness, Financial Readiness, Operator Readiness, and complete Pilot financing remain independently governed future requirements.

This section is the official Operational Readiness governance boundary of the Development Round. It ensures that successful product completion is treated as a necessary input to real operations, but never as automatic authorization to begin them.

20. Post-Round Position

This section defines the official AgriPartners project position immediately following successful completion and formal acceptance of the Development Round.

The post-round position determines:

the accepted product status;

the claims AgriPartners may make;

the claims that remain prohibited;

the preparation activities that may continue;

the work that remains outside the completed Development Scope;

the governance sequence required before a real Pilot may begin.

Collectively, these requirements define the complete post-completion positioning boundary of the Development Round.

20.1 Product Status After Completion

Following final acceptance, the official product status will be:

AgriPartners Pilot Operations & Investor Evidence Beta Candidate — Accepted, Controlled, and Non-Production

This status confirms that:

the Development Objective has been achieved;

the approved Beta Candidate exists;

the Minimum Viable Development Scope has been completed;

all Core Work Packages have been completed;

all Minimum Deliverables have been completed;

all mandatory Milestones have been accepted;

the end-to-end operational workflow is demonstrable;

required Verification Evidence exists;

the Completion and Acceptance Criteria have been satisfied;

the accepted product and its Known Limitations are documented.

The accepted version, repository reference, deployment reference, evidence package, and Acceptance Record will establish the new product baseline for subsequent planning and review.

Later work must distinguish between:

the accepted post-round baseline;

subsequent approved additions;

planned future capabilities;

production or Pilot requirements.

The post-round product status remains a Beta Candidate status. It is distinct from production deployment, Operational Readiness, Mainnet readiness, regulatory approval, and live Pilot operations.

20.2 Permitted External Claims

After successful completion and formal acceptance, AgriPartners may make claims supported directly by the accepted evidence.

Permitted claims may include:

“AgriPartners has completed its USD 40,000 product Development Round.”

“AgriPartners has completed and accepted the Pilot Operations & Investor Evidence Beta Candidate.”

“The approved Minimum Viable Development Scope has been completed.”

“The platform demonstrates an integrated Project Expense, Operator, evidence, reporting, and Investor Transparency workflow.”

“An authorized Operator can complete the supported operational scenario within the controlled product environment.”

“An authorized Investor can review permitted Project activity, Project Expense information, evidence availability, reporting, and lifecycle history.”

“The Beta Candidate supports a controlled and repeatable end-to-end demonstration.”

“Development Round completion is supported by Work Package, Deliverable, Milestone, Verification Evidence, and Acceptance records.”

“The completed product is ready to enter a separate Operational Readiness Review.”

“The product remains controlled, non-production, and subject to documented limitations.”

Permitted claims must:

correspond to the accepted version;

remain within the accepted Development Scope;

identify material limitations where relevant;

use the approved terminology;

remain traceable to Verification Evidence and Acceptance Records;

distinguish product completion from operational authorization.

Where a funder, accelerator, Investor, or strategic partner requires shorter wording, the claim may be condensed but must not change its factual meaning.

A claim that was accurate for one accepted version must be reassessed if later changes materially affect the product or supporting evidence.

20.3 Claims That Remain Prohibited

The following claims remain prohibited after Development Round completion unless separately supported by future evidence and an appropriate governance decision:

production-ready;

Operationally Ready;

Pilot-ready without an applicable GO decision;

Mainnet-ready;

deployed on NEAR Mainnet;

externally audited, unless a specifically identified external audit has occurred;

security-certified;

regulator-approved;

a regulated financial service;

a licensed investment platform;

a licensed crowdfunding platform;

a production payment, custody, exchange, or settlement system;

a live investment platform;

accepting live Investor funds;

processing live Investor payouts;

operating production treasury infrastructure;

commercially validated;

proven at operational scale;

a completed Feedlot Pilot;

an operational Feedlot;

a completed Hissar Pilot;

an operational Hissar project;

verified or audited agricultural performance;

verified, audited, or guaranteed investment returns;

guaranteed principal protection;

guaranteed future funding;

approved by a named funder, regulator, partner, or ecosystem organization without authoritative evidence.

The following implications are also prohibited:

that Beta Candidate acceptance establishes Corporate Setup;

that product records prove a bank payment;

that an on-chain reference proves fiat settlement;

that demonstration data represents real investment activity;

that projected economics represent realised returns;

that an interested party is a committed partner or Investor;

that an application constitutes funding approval;

that a conditional decision constitutes final approval.

A future claim may become permitted only after the relevant event has occurred, sufficient evidence exists, and the applicable governance authority has approved the claim.

20.4 Readiness for Feedlot Pilot Preparation

The accepted Beta Candidate enables AgriPartners to proceed with structured preparation for a future Feedlot Pilot.

Permitted preparation activities may include:

Beta Candidate handoff;

Operational Readiness planning;

preparation of the Operational Readiness evidence package;

Corporate Setup fundraising and completion where applicable;

legal and regulatory review;

preparation and review of required agreements;

Operator identification and due diligence;

facility and agricultural readiness assessment;

banking, payment, accounting, and treasury preparation;

Feedlot Pilot budget confirmation;

Feedlot funding applications;

Investor and partner discussions;

conditional Pilot funding commitments;

insurance and biosecurity planning;

supplier and service-provider discussions;

Pilot risk assessment;

controlled demonstration and due diligence sessions.

These activities prepare for a possible Pilot. They do not authorize:

deployment of Pilot Capital;

Operator funding;

livestock acquisition;

commencement of agricultural operations;

live Investor capital intake;

production payment or settlement activity.

Preparation must remain consistent with the applicable corporate, legal, financial, disclosure, and Operational Readiness boundaries.

20.5 Remaining Corporate, Legal and Operational Work

The following major categories remain outside the completed Development Round.

Corporate work

AgriPartners OÜ registration where not already completed;

corporate governance and authority;

corporate records;

KYB preparation;

legal address and contact-person arrangements;

corporate administration.

Legal and regulatory work

jurisdiction-specific legal advice;

regulatory classification;

Investor agreements;

Operator agreements;

Farm or Pilot agreements;

supplier and service-provider agreements;

privacy, disclosure, and data-protection readiness;

signature and execution evidence;

applicable compliance preparation.

Financial work

banking and payment-provider onboarding;

accounting infrastructure;

treasury controls;

fund segregation;

crypto-to-fiat provider arrangements where applicable;

fiat disbursement procedures;

reconciliation procedures;

Investor settlement procedures;

AML, KYC, KYB, or sanctions controls where required.

Operator and agricultural work

Operator verification and approval;

facility confirmation;

livestock-sourcing preparation;

veterinary and biosecurity planning;

feed and supplier arrangements;

personnel readiness;

insurance;

emergency procedures;

agricultural monitoring;

operational reporting readiness.

Funding work

complete Feedlot Pilot Capital;

any required Feedlot contingency;

funding conditions and agreements;

payment timing;

restrictions on Pilot use of funds;

confirmation that the Pilot can be completed without an unsecured funding gap.

Production and readiness work

Operational Readiness Review;

production-level security and monitoring;

incident response;

business continuity;

production infrastructure;

final Pilot authorization;

Operational Readiness Board GO decision.

These activities belong to subsequent funding components and project phases. Their necessity does not reduce the value or completion status of the accepted Development Round, but they remain mandatory where applicable before real operations.

20.6 Transition to Feedlot Pilot Round

The official transition is:

Development Round



Accepted Beta Candidate



Beta Candidate Handoff



Operational Readiness Preparation and Review



Operational Readiness Board Decision



Explicit GO



Feedlot Pilot Capital Release and Deployment



Controlled Feedlot Pilot

Every transition requires its own evidence and governance decision.

Feedlot fundraising, due diligence, and conditional funding commitments may occur during post-round preparation and Operational Readiness.

However:

complete Pilot Capital must be available or legally committed before GO;

Pilot Capital must not be released for operations before GO;

Operator funding must not begin before GO;

livestock must not be acquired before GO;

agricultural operations must not commence before GO.

For this sequence, **Feedlot Pilot Round activation** means the approved release and deployment of Pilot Capital following GO. It does not prohibit earlier fundraising discussions or conditional commitments required to demonstrate Funding Readiness.

A Feedlot GO decision applies only to the reviewed Feedlot Pilot, Operator, site, funding structure, agreements, and conditions.

It does not authorize:

the Hissar Pilot;

another Operator;

another site;

a larger commercial deployment;

unrestricted production operations.

The Hissar Pilot requires its own funding, Operational Readiness Review, and explicit GO decision.

Post-Round Principles

The completed Development Round:

establishes a more mature product state;

creates an accepted Beta Candidate;

provides a demonstrable operational and Investor evidence workflow;

creates reviewable delivery and governance evidence;

improves grant and fundraising readiness;

supports due diligence;

supports Corporate Setup and partner discussions;

supports Operational Readiness preparation;

supports future Feedlot Pilot preparation.

It does not independently:

establish Corporate Setup;

establish Legal or Financial Readiness;

establish Operational Readiness;

authorize live Investor operations;

authorize Pilot Capital deployment;

authorize livestock acquisition;

authorize Feedlot or Hissar Pilot commencement;

establish production or Mainnet readiness.

Post-Round Traceability

The post-round position must remain traceable through:

Development Objective



Accepted Beta Candidate



Verification Evidence



Acceptance Decision



Expected Outcomes



Post-Round Position



Operational Readiness Preparation

Every post-round claim must remain connected to the accepted product state and evidence supporting it.

Relationship to Section 21

Section 20 defines:

What AgriPartners officially becomes after successful completion of the Development Round.

Section 21 defines:

How the completed Funding Package may be adapted for different funder categories without changing its approved substance, boundaries, or factual claims.

Funder adaptation may change emphasis, terminology, format, evidence selection, or reporting structure. It must not change the accepted post-round status or convert a prohibited claim into a permitted claim.

This section is the official post-completion positioning statement of the Development Round. Accordingly, it defines what AgriPartners may claim, demonstrate, and undertake after final acceptance while preserving the separate governance of Corporate Setup, Operational Readiness, production deployment, and both Pilot Rounds.

21. Funder Adaptation Framework

This section establishes the official framework governing how the approved Development Round Funding Package may be adapted for different funder categories.

AgriPartners maintains one authoritative Development Round Funding Package. Every grant application, accelerator submission, investment package, venture-studio proposal, or strategic-partner presentation must derive from this same approved core.

Adaptation changes how the Development Round is presented. It does not change what the Development Round is.

Collectively, the requirements in this section define the complete adaptation-governance framework for all future Development Round funding submissions.

21.1 Core Package That Remains Unchanged

The authoritative core consists of the approved Funding Strategy v1 and Sections 1–21 of this Development Round Funding Package.

The following elements remain unchanged in every adaptation:

Development Objective;

current verified Product Baseline;

Beta Candidate definition;

Development Scope;

Minimum, Recommended, and Optional Scope hierarchy;

Work Package portfolio;

Deliverable catalogue;

Development Budget of USD 40,000;

Use of Funds;

Excluded Costs;

Milestone framework;

Verification and Reporting Evidence framework;

Completion and Acceptance Criteria;

Expected Outcomes;

Dependencies and Assumptions;

Risks and Controls;

Operational Readiness boundary;

Post-Round Position;

Funding Strategy v1.

The authoritative core remains the same regardless of whether the intended recipient is:

a technical grant programme;

a protocol or ecosystem fund;

the NEAR ecosystem;

an accelerator;

an angel or pre-seed Investor;

a venture studio;

a strategic Investor;

an impact Investor;

an agricultural partner;

a development organization.

An external adaptation may omit sections that are not required in the initial application format, but omission does not remove their authority.

If an adapted submission conflicts with the authoritative core, the authoritative core controls and the submission must be corrected.

Before Development Round completion, an adapted package must distinguish clearly between:

the current verified Alpha baseline;

the approved future Beta Candidate;

the work proposed for funding.

After Development Round completion, external claims must use the accepted post-round baseline and corresponding evidence.

The future Beta Candidate must never be presented as currently implemented merely because it is fully defined in this Funding Package.

21.2 Technical Grant Adaptation

A technical grant adaptation may emphasize:

the verified current technical baseline;

the defined Alpha-to-Beta Candidate transition;

Project Expense API and Authorization;

Operator Workspace;

Evidence Management;

Investor Transparency;

reporting;

technical Work Packages;

measurable Deliverables;

Development Milestones;

repository traceability;

test and QA evidence;

product security evidence;

demonstration evidence;

completion reporting.

The adapted submission may reorganize Work Packages into a funder's required technical format, provided that a crosswalk preserves the approved Work Package and Deliverable identities.

Technical terminology may be made more detailed for engineering reviewers, but technical claims must not exceed: the verified current baseline when describing existing functionality;

the approved Beta Candidate definition when describing proposed functionality;

the accepted post-round baseline when reporting completed functionality.

A technical grant adaptation must preserve:

the USD 40,000 product-only request;

Minimum Scope protection;

the non-production boundary;

the distinction between activity and completion;

the requirement for Verification Evidence and formal Acceptance.

Repository activity must remain supporting evidence. Commits, Pull Requests, tests, or deployment records do not independently prove completion.

21.3 NEAR Ecosystem Adaptation

A NEAR ecosystem adaptation may emphasize:

the current NEAR Testnet implementation;

wallet-linked Alpha capabilities;

wallet authentication;

smart-contract experimentation;

Testnet transaction references;

transparent workflow concepts;

lifecycle and evidence visibility;

product governance;

evidence-based delivery;

the potential role of NEAR in audit, automation, and transparency infrastructure.

The adaptation must preserve the approved financial boundary:

cryptocurrency stops at AgriPartners OÜ in Estonia;

Uzbekistan-facing Operator and Farmer financial workflows remain fiat-only;
the Uzbekistan Feedlot Operator does not receive cryptocurrency;
the Farmer does not require a wallet, token, smart contract, or on-chain financial action;
on-chain records remain supplementary to contracts, bank records, accounting, and reconciliation evidence.

The current Testnet implementation must not be presented as:

Mainnet readiness;
audited smart-contract infrastructure;
production custody;
production settlement;
a live investment system;
production financial decentralization.

Legacy Farmer wallet, funding, withdrawal, and payout behaviour must remain identified as Legacy Testnet Alpha where relevant.

A NEAR funding submission may emphasize the ecosystem value of the Development Round, but it must continue to finance the same approved Beta Candidate and product-only Development Scope.

No NEAR grant, partnership, endorsement, Protocol Reward, or ecosystem commitment may be claimed until supported by authoritative evidence.

21.4 Accelerator Adaptation

An accelerator adaptation may emphasize:

progression from a verified Alpha to a defined Beta Candidate;
product maturity;
the completed technical foundations;
a clear next value milestone;
demonstration capability;
execution discipline;
Development Scope control;
Work Package governance;
measurable Milestones;
evidence-based reporting;
known limitations;

Operational Readiness boundaries;

international company and Pilot planning context.

The accelerator package may include additional founder, team, market, programme-fit, or interview materials where required. Such materials are supporting addenda and must not redefine the Development Round.

Corporate Setup may be presented as a separate readiness requirement where relevant to the accelerator.

If an accelerator offers a broader funding commitment that includes Development and Corporate Setup, the components must remain separately identified:

Accelerator Readiness Commitment

- |
- |-- USD 40,000 Development Round
- |
- |-- Separate Corporate Setup component
- |
- |-- Other separately approved readiness support

Combining the components in one external offer does not merge their internal budgets or Uses of Funds.

Acceptance into an accelerator, selection for an interview, or participation in a programme remains an independent decision and must not be implied by submission of this package.

21.5 Angel and Pre-Seed Adaptation

An angel or pre-seed adaptation may emphasize:

the accepted Development Objective;

the verified current Alpha;

the Beta Candidate as the next product milestone;

execution capability;

product and financial governance;

evidence-based delivery;

future Operational Readiness;

the separation of Development, Corporate Setup, and Pilot Capital;

the project's post-round fundraising and partnership position.

The adaptation may present a broader Readiness funding request where an Investor is prepared to finance more than product development.

A broader request may include:

the USD 40,000 Development Round;

a separately identified Corporate Setup component;

separately identified initial corporate-readiness expenditure;

another approved readiness component.

The Development Round must remain unchanged and separately accounted for within the broader request.

Equity, SAFE, convertible instrument, governance rights, valuation, Investor protections, and investment documentation remain subject to separate negotiation and legal review. They are not defined by this Development Round Funding Package.

An adapted package must not imply:

an agreed investment;

an agreed valuation;

commercial validation;

guaranteed follow-on funding;

Pilot approval;

guaranteed returns.

21.6 Venture Studio Adaptation

A venture-studio adaptation may emphasize:

the project's verified implementation baseline;

the Beta Candidate target state;

Work Package modularity;

technical and product maturity;

implementation governance;

verification and acceptance discipline;

identified dependencies and risks;

future scalability questions;

commercialization preparation;

Corporate Setup and partnership needs.

The package may identify where a venture studio could contribute through:

product expertise;

engineering capacity;

security or QA support;

company-building support;

fundraising support;

network access;

commercialization planning.

Such proposed support must be mapped to:

an approved Development Work Package;

a separate Corporate Setup component;

or another separately approved future workstream.

Venture-studio participation does not authorize informal expansion of Development Scope.

Scalability and commercialization may be evaluated during the engagement, but production commercialization remains outside the Development Round.

Submission, discussion, due diligence, or studio participation does not imply investment, partnership, company formation, or commercial success.

21.7 Strategic and Impact Investor Adaptation

A strategic or impact-oriented adaptation may emphasize:

agricultural accountability;

transparent use-of-funds workflows;

controlled Project Expense management;

Operator accountability;

evidence-linked reporting;

Investor visibility;

measurable governance;

the Estonia-to-Uzbekistan financial boundary;

fiat-only local operations;

readiness for structured Pilot preparation;

potential ecosystem or development relevance.

For agricultural and development organizations, the package may explain how the Beta Candidate provides a collaboration platform for future operational planning and evaluation.

Impact claims must remain proportionate to available evidence.

The Development Round must not be presented as proof of:

improved farmer income;

agricultural productivity;

livestock performance;

employment creation;

financial inclusion;

rural development impact;

environmental impact;

completed real-world Pilot results.

Such impact outcomes require separate Pilot evidence, measurement methods, and governance.

The Development Round remains product-focused even where the funder's mandate is agricultural, developmental, strategic, or impact-oriented.

A strategic discussion does not establish a partnership. An impact thesis does not establish measured impact. An agricultural model does not establish an operational Pilot.

21.8 Programme-Specific Budget and Reporting Addenda

A funder may require:

a different budget template;

local-currency presentation;

eligible-cost classifications;

indirect-cost treatment;

procurement information;

personnel-cost detail;

tranche structure;

programme-specific Milestone terminology;

reporting templates;

evidence schedules;

risk formats;

results frameworks;

appendices;

declarations or certifications.

These requirements may be addressed through a programme-specific addendum.

Each addendum must include a crosswalk to the authoritative package covering, where applicable:

Development Scope;

Work Packages;

Deliverables;

Milestones;

budget allocations;

cost categories;

Verification Evidence;

Completion and Acceptance Criteria.

Budget presentation

The canonical Development Budget remains USD 40,000.

Where another currency is required, the addendum must identify:

conversion currency;

exchange-rate source;

conversion date;

rounded amount;

treatment of exchange-rate variance.

Currency presentation must not silently change the underlying USD 40,000 request or reduce Minimum Scope.

Cost eligibility

Where a programme excludes a planned cost category, AgriPartners must:

reclassify only where the underlying purpose genuinely fits an eligible category;

replace the cost with another eligible cost supporting the same approved result;

finance the excluded cost separately;

or formally reassess whether the complete Scope remains financeable.

A cost must not be mislabelled to obtain eligibility.

Programme Milestones

A funder may use different Milestone names or combine reporting checkpoints.

Equivalent terminology is permitted only where the addendum preserves a clear mapping to Milestones 1–5.

Programme terminology must not redefine Milestone Exit Criteria or permit incomplete work to be reported as complete.

Reduced awards

An award below USD 40,000 does not automatically create a reduced version of the Development Round.

The Partial-Funding Restrictions in Section 10 continue to apply.

Before accepting a reduced award, AgriPartners must confirm that:

the remaining Development funding is legally committed; or

a separately governed, independently valuable phase can be completed; or

the full Development Round will not commence until the financing gap is resolved.

Broader funding offers

Where a funder supports Development together with Corporate Setup or another readiness component, the adapted package must preserve separate:

objectives;

budgets;

Uses of Funds;

Excluded Costs;

reporting;

acceptance conditions.

A broader external commitment does not change the internal financial architecture.

Adaptation Principles

Adaptation may modify:

presentation;

section order;

length;

emphasis;

audience terminology;

programme terminology;

evidence selection;

supporting documents;

appendices;

budget format;

reporting format.

Adaptation must never modify or misrepresent:

facts;

current implementation status;

the Development Objective;

the Beta Candidate definition;

Minimum Scope;

Core Work Packages;

Minimum Deliverables;

the USD 40,000 Development Budget;

eligible and excluded financial boundaries;

mandatory Milestones;

Verification Evidence requirements;

Completion and Acceptance Criteria;

non-production boundaries;

Operational Readiness requirements;

Funding Strategy v1.

An adaptation must not:

present future functionality as current;

remove a material Known Limitation;

conceal a funding gap;

imply a partnership or approval;

convert Testnet into Mainnet readiness;

convert Beta Candidate completion into Operational Readiness;

convert demonstration records into real-world evidence;

convert projected returns into verified performance.

Adaptation Governance

Every external adaptation must remain:

factually equivalent to the authoritative core;

traceable to the approved Funding Package;

evidence-based;

internally consistent;

consistent with Funding Strategy v1;

appropriate to the intended audience;

explicit about any programme-specific addendum.

Each material adaptation should identify:

Adaptation ID;

target funder or funder category;

source Funding Package version;

preparation date;

included and omitted sections;

terminology crosswalk;

budget crosswalk;

evidence crosswalk;

additional supporting material;

deviations required by the programme;

equivalence review;

approving authority;

submission version.

Where programme terminology differs, equivalent terminology may be used if the factual and governance meaning remains unchanged.

Before submission, the adapted package should receive:

factual review;

product-status review;

claims and positioning review;

budget-boundary review;

evidence review;


consistency review;

approval through the applicable governance process.

Any requested adaptation that would change the Development Objective, Budget, Minimum Scope, Core Deliverables, Milestones, or Acceptance Criteria is not a presentation adaptation. It is a proposed substantive revision and must be processed through formal Funding Package governance.

Adaptation Traceability

Every external submission must remain within the following traceability chain:

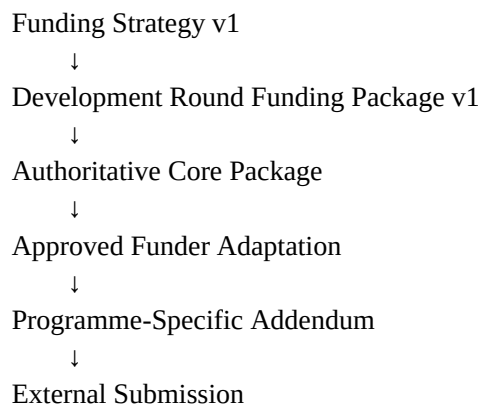

A reviewer must be able to trace each material claim, budget amount, Milestone, and proposed outcome back to the authoritative core.

Final Funding Package Principles

The approved Development Round Funding Package represents:

- one Development Objective;
- one Beta Candidate;
- one Development Scope;
- one Work Package portfolio;
- one Deliverable catalogue;
- one USD 40,000 Development Budget;
- one Use of Funds framework;
- one Excluded Costs boundary;
- one Milestone framework;
- one Verification framework;
- one Acceptance framework;
- one Expected Outcomes framework;
- one Operational Readiness boundary;
- one Funding Strategy v1.

Different submissions present the same approved Development Round.

They do not create separate Development Rounds, different Beta Candidates, alternative completion standards, or conflicting factual baselines.

This section is the official Funder Adaptation Framework of the Development Round Funding Package. Accordingly, every future funding submission may adapt presentation to the decision logic of its intended funder, but must preserve the approved substance, evidence, governance, financial boundaries, and factual integrity of the authoritative package.

Appendices A–J

Appendix A — Controlled Terminology Register

Term	Canonical meaning
Development Round	Product-only funding round with an approved budget of USD 40,000.
Pilot Operations & Investor Evidence Beta Candidate	The completed demonstrable, non-production product state defined in Section 6.
Current Alpha Baseline	The implemented starting point described in Section 4; it is not the future Beta Candidate.
Corporate Setup	A separate funding and readiness component; not part of the Development Budget.
Operational / Legal Readiness	A separate post-development governance process preceding any live Pilot.
Feedlot Pilot Capital	Separate capital for the Feedlot Pilot; excluded from the Development Round.
Hissar Pilot Capital	Separate capital for the Hissar Pilot; excluded from the Development Round.
Work Package	A controlled implementation unit defined in Section 8.
Deliverable	A completed, reviewable output defined in Section 9; not merely an activity.
Verification Evidence	Reviewable evidence under Section 14; evidence informs but does not replace acceptance.
Acceptance	Formal decision under Section 15.
Investor	Capital provider in the product and funding narrative; no direct Investor–Farmer payment relationship is implied.
Operator	Uzbekistan-facing operating role receiving and using fiat only.
Farmer	Non-crypto agricultural participant.

Capitalization shown above is authoritative where the term denotes a defined governance object.

Appendix B — Scope and Work Package Crosswalk

Scope outcome	Primary Work Packages	Priority
Project Expense platform and controls	WP-C01, WP-C02	Minimum
Operator Workspace	WP-C03	Minimum
Evidence Management	WP-C04	Minimum
Investor Transparency	WP-C05	Minimum
Reporting	WP-C06	Minimum
Demonstration Environment	WP-C07	Minimum
QA and Product Security	WP-C08	Minimum
Documentation and Acceptance Support	WP-C09	Minimum
Product Experience Enhancement	WP-R01	Recommended
Enhanced Reporting and Presentation	WP-R02	Recommended

Scope outcome	Primary Work Packages	Priority
Demonstration Reliability	WP-R03	Recommended
Analytics / AI and extended scenarios	WP-O01, WP-O02	Optional; activation-controlled

Section 8 remains authoritative if this crosswalk is incomplete or inconsistent.

Appendix C — Deliverable and Milestone Crosswalk

Milestone	Principal result	Evidence focus
Milestone 1 — Expense Platform Complete	Completed Project Expense workflow, API, authorization and financial controls	End-to-end lifecycle, permitted/prohibited action, role, authorization and financial-control evidence
Milestone 2 — Operator Workspace Complete	Completed Operator Workspace and Operator-facing role-aware frontend integration	Complete Operator journey, role-access, action-control, lifecycle and workspace-review evidence
Milestone 3 — Evidence Layer Complete	Completed Evidence Workflow and integrated Project Expense and evidence data flow	Evidence association, classification, access, restriction, lifecycle-linkage and integrated data-flow evidence
Milestone 4 — Investor Transparency Complete	Completed Investor Transparency experience, operational and Investor reporting, and role-aware frontend integration	Investor journey, role-access, disclosure/restriction, reporting, source-record comparison and authority-labelling evidence
Milestone 5 — Beta Candidate Complete	All Minimum Deliverables and the integrated controlled Beta demonstration	End-to-end demonstration, integrated journeys, QA, security, deployment, documentation, traceability and completion-reporting evidence

This is a derived matrix only. Section 13 exclusively governs Milestone titles, mappings, dependencies and Exit Criteria. Detailed Deliverable identities are governed by Section 9, and completion and acceptance are governed by Sections 14–15.

Appendix D — Budget Control Schedule

Control	Rule
Total Development Budget	USD 40,000
Funding purpose	Product development only
Minimum Scope	Protected before Recommended or Optional activation
Contingency	Controlled under Section 10; not an unallocated discretionary reserve
Reallocation	Requires documented approval and must preserve Core Work Package completion
Eligibility	Governed by Section 11
Prohibition	Governed by Section 12
Double funding	Prohibited
Uzbekistan financing source	Excluded; foreign funding only
Irreversible commitment	No irreversible work before full minimum closing

This schedule summarizes Sections 10–12 and does not amend their allocations or controls.

Appendix E — Evidence Register Template

Complete one record per evidence item:

Evidence ID: EV-___

Work Package: WP-___

Deliverable / Milestone: D-___ / M-___

Evidence type: Repository / Test / Security / Deployment / Demonstration / Documentation

Location and version: ___

Evidence date: ___

Owner: ___

Reviewer: ___

Status: Draft / Verified / Accepted / Limited

Limitation or exception: ___

Evidence must be relevant, attributable, accessible, reviewable, versioned where appropriate, and preserved in accordance with Section 14.

Appendix F — Risk and Dependency Register Template

Complete one record per Risk, Dependency or Assumption:

ID: R-___ / DEP-___ / A-___

Type: Risk / Dependency / Assumption

Description: ___

Probability or current status: ___

Impact: ___

Owner: ___

Control or response: ___

Trigger / review date: ___

Residual position: ___

Dependencies and Assumptions are governed by Section 17; Risks and Controls are governed by Section 18.

Appendix G — Acceptance Record Template

Acceptance object: Work Package / Deliverable / Milestone / Beta Candidate / Development Round

Identifier and version: ___

Applicable criteria: ___

Evidence reviewed: ___

Known limitations: ___

Decision: Accepted / Accepted with Approved Limitations / Conditionally Accepted / Not Accepted

Conditions and due dates: ___

Decision authority: ___

Decision date: ___

Sign-off / record reference: ___

Only an authorized decision under Section 15 constitutes Acceptance.

Appendix H — Claims and Positioning Matrix

Topic	Permitted wording	Prohibited implication
Current state before completion	Implemented and demonstrable Alpha; verified foundations	Completed Beta or production platform
Target state	Proposed Pilot Operations & Investor Evidence Beta Candidate	Already implemented future capability
After acceptance	Accepted Beta Candidate within approved non-production boundaries	Production-ready, mainnet-ready, audited or regulated
Blockchain	NEAR Testnet demonstration and traceability support	Proof of fiat clearing, legal agreement, audit or settlement
Pilot status	Readiness review may begin after product handoff	Live or automatically authorized Pilot
Financial operations	Product demonstration of controlled workflows	Production custody, payout or settlement

Sections 4, 6, 19 and 20 control all external claims.

Appendix I — Funder Adaptation Crosswalk

Funder category	May emphasize	Must preserve
Technical grant / protocol ecosystem	Technical baseline, Work Packages, tests, evidence, milestones	USD 40,000 product-only request and non-production boundary
NEAR ecosystem	Testnet integration, traceability, repository evidence	No mainnet, custody or production-settlement claim
Accelerator	Team execution, product maturity, readiness path	Separate Corporate Setup, readiness and Pilot financing
Angel / pre-seed / venture studio	Value milestone and post-round fundraising position	Same Beta Candidate, scope, budget and acceptance standard
Strategic / impact investor	Agricultural transparency and evidence value	No unsupported impact, return, readiness or live-operation claim

Every adaptation must be traceable to Section 21 and must not create an alternative authoritative package.

Appendix J — Publication and Change-Control Checklist

- ☒ Sections 1–21 present in approved architecture.
- ☒ Sections 1, 3, 5 and 13 identified as Reissued Canonical Sources.
- ☒ Remaining Sections classified as Preserved Approved Sources.
- ☒ Development Budget remains USD 40,000 and product-only.
- ☒ Corporate Setup, readiness costs and Pilot Capital remain excluded.

☒ Alpha, Beta Candidate, Operational Readiness and live Pilot states remain distinct.

☒ Foreign-funding, fiat-only Uzbekistan and non-production boundaries preserved.

☒ Terminology, cross-reference and consistency reviews completed.

☒ Markdown, DOCX and PDF outputs generated.

☒ Freeze Registry, Revision History and Governance Policy issued.

☒ Publication manifest and SHA-256 checksums generated.

Future substantive change requires an authorized revision, updated Revision History, new hashes and a replacement publication package.
